



Sagarmala Finance Corporation Limited

Request for Proposal

(Tender invited through e-Tendering mode only for selection from CPSE/PSU/ Govt Bodies)

For

**SELECTION OF VENDOR FOR
UNDERSTANDING, DESIGN, DEVELOPMENT, CONFIGURATION,
IMPLEMENTATION, COMMISSIONING, STABILIZATION & MAINTENANCE OF
WEB & MOBILE-BASED
INTEGRATED ENTERPRISE RESOURCE PLANNING (ERP) SOLUTION & Website
in SMFC LTD**

Tender No. SMFCL/ERP/2025-26/62

Dated: 23/03/2026

Issued by:

Sagarmala Finance Corporation Ltd. (SMFC)
1st Floor, Thapar House, Gate No. 2
124, Janpath, New Delhi – 110 001

For more information, visit <https://www.sdclindia.com> & GeM Portal (www.gem.gov.in)

Disclaimer

1. This EOI document is neither an agreement nor an offer by the Sagarmala Finance Corporation Limited (SMFC LTD) [Formerly Known as Sagarmala Development Company Ltd.] to the prospective Applicants or any other person. The purpose of this EOI is to provide information to interested parties that may be useful to them in the formulation of their proposal pursuant to this EOI.
2. SMFC LTD does not make any representation or warranty as to the accuracy, reliability, or completeness of the information in this EOI document and it is not possible for SMFC LTD to consider the needs of each party who reads or uses this EOI document. This EOI includes statements which reflect various assumptions and assessments arrived at by SMFC LTD in relation to the consultancy. Such assumptions, assessments and statements do not purport to contain all the information that each Applicant may require. Each prospective applicant should conduct its own investigations and analyses and check the accuracy, reliability and completeness of the information provided in this EOI document and obtain independent advice from appropriate sources.
3. SMFC LTD will not have any liability to any prospective Applicant/Consultancy Company/ Firm/ as the case may be or any other person under any laws (including without limitation the law of contract, tort), the principles of equity, restitution or unjust enrichment or otherwise for any loss, expense or damage which may arise from or be incurred or suffered in connection with anything contained in this EOI document, any matter deemed to form part of this EOI document, the award of the Assignment, the information and any other information supplied by or on behalf of SMFC LTD or their employees, any consultants or otherwise arising in any way from the selection process for the Assignment. SMFC LTD will also not be liable in any manner whether resulting from negligence or otherwise caused arising from reliance of any Applicant upon any statements contained in this EOI.
4. SMFC LTD will not be responsible for any delay in receiving the proposals. The issue of this EOI does not imply that SMFC LTD is bound to select an Applicant or to appoint the Selected Applicant for the consultancy and SMFC LTD reserves the right to accept/reject any or all of proposals submitted in response to this EOI document at any stage without assigning any reasons whatsoever. SMFC LTD also reserves the right to withhold or withdraw the process at any stage with intimation to all who submitted the EOI Application.
5. The information given is not an exhaustive account of statutory requirements and should not be regarded as a complete or authoritative statement of law. SMFC LTD accepts no responsibility for the accuracy or otherwise for any interpretation or opinion on the law expressed herein.
6. SMFC LTD reserves the right to change/ modify/ amend any or all provisions of this EOI document. Such revisions to the EOI/ amended EOI will be made available on the website.

ABBREVIATIONS

ACL	Access Control Lists	LOA/LOI	Letter of Authorization/ Letter of Intent
ACR	Annual Confidential Report	MEITY	Ministry of Electronics Information and Technology
AMC	Annual Maintenance Contract	MFA	Multi-Factor Authentication
API	Application Programming Interface	MIS	Management Information Systems
APT	Advanced Persistent Threat	MM	Materials Management
ATS	Annual Technical Support	MPLS	Multi-Protocol Label Switching
BCP	Business Continuity Plan	NAT	Network Address Translation
BG	Bank Guarantee	NBSP	Network Bandwidth Service Provider
BIA	Business Impact Analysis	NIC	Network Interface Cards
BI	Business Intelligence	O&M	Operation and Maintenance
BOQ	Bill of Quantities	PDF	Portable Document Format
BPML	Business Process Master List	OEM	Original Equipment Manufacturer
CCB	Change Control Board	OPC	Open Platform Communications
CCN	Change Control Notice	OS	Operating System
CERT-In	Indian Computer Emergency Response Team	OWASP	Open Web Application Security Project
CMMI	Capability Maturity Model Integration	P2P	Peer to Peer
CPG	Contract Performance Guarantee	PDA	Personal Digital Assistant
CRP	Conference Room Pilot	PERT	Program Evaluation Review Technique
CSP	Cloud Service Provider	PKCS	Public Key Cryptography Standards
DC	Data Center	POA	Power of Attorney
DDA	Data Digitization Agency	POP3	Post Office Protocol version 3
DDOS	Distributed Denial of Service	PQC/PQR	Pre-Qualification Criteria/Requirements
DHCP	Dynamic Host Configuration Protocol	PS	Project Planning & Management
SMFC LTD	Sagarmala Finance Corporation Limited	PSU	Public Sector Undertaking
DMS	Document Management System	PT	Performance Testing
DMZ	Demilitarized Zone	QA	Quality Assurance
DNS	Domain Name System	QC	Quality Control
DRC	Disaster Recovery Center	RAID	Redundant Array of Independent Disks
EMD	Ernest Money Deposit		
EMS/N MS	Element / Network Management System	RDBMS	Relational Database Management System
ERP	Enterprise Resource Planning		
ERPSI/SI	Enterprise Resource Planning System Integrator	RFP	Request for Proposal
ESS	Employee Self Service	RFP	Radio Frequency
F&A	Finance and Accounts Management	RICEFW	Reports, Interface, Conversion, Enhancements, Forms and Workflow
FAQ	Frequently Asked Questions	RPO/RTO	Recovery Point Objective / Recovery Time Objective

FMS	Facility Management Services	SAAS	Software as a Service
FRS	Functional Requirement Specifications	SAN	Storage Area Network
FTP	File Transfer Protocol	SANS	Sys Admin, Audit, Network and Security
GCC/S CC	General/Special Conditions of Contract		
GIGW	Guidelines for Indian Government Websites	SDLC	System Development Life Cycle
GIS	Geographic Information System	SD-WAN	Software-defined Wide Area Network
GPS	Global Positioning System	SI	System Integrator
GST	Goods and Services Tax	SIT	System Integration Testing
GUI	Graphical User Interface	SLA	Service Level Agreement
HIPS	Host Intrusion Prevention System	SMTP	Simple Mail Transfer Protocol
HLD/L LD	High-Level Design / Low-Level Design	SOA	Service Oriented Architecture
		SOAP	Simple Object Access Protocol
HTTP/ HTTPS	Hypertext Transfer Protocol	SOW	Statement of Work/ Scope of Work
IaaS	Infrastructure as a Service	SPOC	Single Point of Contact
ICMP	Internet Control Message Protocol	SQL	Structured Query Language
IAM	Identity and Access Management	SSD	Solid State Drive
IDS/IPS	Intrusion detection systems and intrusion prevention systems	SSE	Server-Side Encryption
IFB	Invitation for Bids	SSL	Secure Sockets Layer
INDAS	Indian Accounting Standards	STLC	Software Testing Lifecycle
IOC	Indicator of Compromise	STQC	Standardization Testing and Quality Certification
IOPS	Input/output Per Second	TAC	Technical Assistance Centers
IP	Internet Protocol	TCP	Transmission Control Protocol
JPEG	Joint Photographic Experts Group	TIFF	Tag Image File Format
IPS	Intrusion Prevention System	TPAA	Third-Party Audit Agency
ISMS	Information Security Management Systems	TQR	Technical Qualification Requirements
ISO	International Organization for Standardization	TRS	Technical Requirement Specifications
IT	Information Technology	TSI	Turnkey System Integration
ITB	Instruction to Bidders	UAT	User Acceptance Testing
ITIL	Information Technology Infrastructure Library	UT	Unit Testing
ITSM	IT Service Management	VM	Virtual Machine
IVR	Interactive Voice Response	VPN	Virtual Private Network
JDBC	Java Database Connectivity	WAF	Web Application Firewall

Contents

SECTION-I - TENDER INFORMATION.....	6
SECTION-II – INSTRUCTIONS TO BIDDERS.....	9
SECTION-III – OBJECTIVE STATEMENT	18
SECTION-IV - GENERAL FEATURES OF SYSTEM	25
SECTION-V ELIGIBILITY AND QUALIFICATION REQUIREMENTS	49
SECTION-VI BID EVALUATION METHODOLOGY	54
SECTION-VII BIDDING FORMS- TECHNICAL PROPOSAL.....	62
SECTION VIII FINANCIAL PROPOSAL- FORMS.....	107
SECTION IX. ERP SYSTEM REQUIREMENTS AND SERVICE LEVEL AGREEMENTS.....	112

SECTION-I - TENDER INFORMATION

1.1 Background

Sagarmala Finance Corporation Limited (SMFC LTD) [Formerly Known as Sagarmala Development Company Ltd.], having its registered office at New Delhi, is a schedule B CPSE under the Ministry of Ports, Shipping and Waterways, Government of India. It is part of the Sagarmala Programme, a flagship initiative launched by the Government of India, to promote port-led development through the Sagarmala initiative. SMFC LTD strives to reduce logistics costs for both domestic and EXIM cargos. It intends to create, among others, ports, port-connectivity, and transshipment hub of international standards to generate economic activity all along the Indian coastline, with the participation of coastal communities. SMFC LTD also assists the state level/zone level special purpose vehicles (SPVs) and SPVs to be set up by the ports, with equity support for implementation of the projects that they will undertake. SMFC LTD is under the process of getting itself registered as Non-Banking Financial Company (NBFC) with Reserve Bank of India (RBI). SMFC LTD at present has a few stand-alone IT systems in operation with minimal IT infrastructure. To meet the ambitious growth path of the SMFCL, it has been decided to replace these stand-alone systems with an enterprise-wide integrated ERP system which will thrive the entire business of SMFCL, thus injecting speed, accuracy and efficiency in the business processes. The upgradation of the IT infrastructure capable to run the ERP system will be taken up separately.

SMFC LTD invites bids for Selection of a Developer-cum-System-integrator-cum-support vendor to Design, Develop, Configure, Commission, Stabilize, Support & Maintain a Centralized Integrated ERP solution in SMFCL to automate all business functions of the organization without any manual intervention. Henceforth the selected vendor will be referred by 'ERPSI' or 'SI'. Both 'ERPSI' and 'SI' will be changes interchangeably in this RFP with same meaning.

1.2 Important information

The bid document may be downloaded from SMFCL corporate website www.sdclindia.com (for reference only) and GeM Portal. Brief description about the bidding process is given below:

Sr No.	Event	Information to the agencies
1	Name of the Project	Understand, Design, Develop, Implement, Install, Configure, Data Migration, Commission, Stabilize, Support and maintain an automated & integrated ERP system for SMFCL business processes and SMFCL Website development & Hosting

2	Tendering mode	Through GeM only
3	Method of Selection	Quality and Cost Based (QCBS) (70:30)
4	Technical qualifying score	60%
5	Language of bid	English only
6	Currency	Currency in which bidder will the quote the price and will receive the payment is INR only
7	Submission of Bids	Through GeM portal only
8	Pre-bid meeting details	Date & Time = As per GeM portal Mode – Physical/Virtual mode Venue for Physical: SMFCL Office Link for Virtual: https://teams.microsoft.com/meet/48314019691971?p=11PV0ARxMRDHXBMBJH Meeting ID: 483 140 196 919 71 Passcode: fX9AF9Ux
9	Corrigendum, if any	GeM portal , sdclindia.com only
10	Opening of Eligibility & Technical Bids	Through GeM portal only
11	Evaluation of Bid	By Evaluation Committee (off-line)
12	Opening of Commercial bids for technically qualified bidders	Through GeM portal only
13	Notification to finally selected bidder	Through GeM portal only
14	Date of Release of Tender Document	Dates as given in GeM portal
15	Last date of receipt of Pre-bid queries	
16	Date, time and place of Pre-bid Meeting	
17	Publication of Pre-bid Responses	
18	Start date and time of submission of bids	
19	Last date and time of submission of bids	
20	Date of opening of Eligibility & Technical bid	
21	Tender Document	Available in SMFCL corporate website, GEM website & CPP Portal

22	EMD / Bid Security	Bid Security declaration
23	Address for Bid submission/EMD/PBG	Mr. Umesh Garg Sagarmala Finance Corporation Limited, 1st Floor, Western Wing, 124, Thapar House, Janpath Lane, New Delhi, 110001
24	Contact Person	Mr Umesh Garg (Chief Manager – IT) Sagarmala Finance Corporation Limited, 1st Floor, Western Wing, 124, Thapar House, Janpath Lane, New Delhi, 110001 Email: CM.IT@SDCLINDIA.COM
25	Validity of Bid	180 days from the date of Opening of bids

The Proposal in the prescribed format, shall be submitted online at GeM only as per procedure prescribed in this document. No proposal will be accepted in hard copy format, or by fax, e-mail or any other such means. The Applicant must be registered with GeM portal. This RFP document is also available on SMFC LTD website: <http://www.sdclindia.com> for reference only and not for submission.

SECTION-II – INSTRUCTIONS TO BIDDERS

2.1 RFP

- 2.1.1 RFP shall mean **Request for Proposal**. RFP & Tender shall be used interchangeably with same meaning. Bidder & Vendor are synonymous. 'Company' or SMFCL mean SMFC Ltd.

2.2 General Instructions for e-Tendering:

- 2.2.1 Bidders should be CPSE/PSU/Govt Bodies who has already experience in NBFC banking projects.
- 2.2.2 Bidders shall submit their bid online, in GeM portal. Bid submitted anywhere else will be summarily rejected.
- 2.2.3 Bidders will be responsible for downloading the RFP Document along with all addenda/ corrigendum/ amendment/ clarification thereto available on the portal, examine and understood before submission of their response.
- 2.2.4 Any unresponsive bid shall be summarily rejected.
- 2.2.5 SMFC Ltd reserves the right to take any decision with regard to RFP process for addressing any situation which is not explicitly covered in the RFP document.
- 2.2.6 The Bidder must disclose any actual or potential conflict of interest with SMFC Ltd.

2.3 EARNEST MONEY DEPOSIT (EMD) / Bid Security

All bidders should submit Bid security document as per prescribed format (Annexure 2), filling which the bid shall be declared non responsive and shall not be consider for evaluation.

2.4 Pre-Bid Clarifications of Bidding Documents

- 2.4.1 A prospective Bidder requiring any clarification of the bidding documents may notify SMFCL in writing through email at **cm.it@sdclindia.com** up to one day prior pre-bid meeting.
- 2.4.2 Bidders shall submit the queries only in the format given below with subject in the following format:

Tender Name: Development of integrated ERP system Tender No. SMFCL/ERP/2025-26/62

Bidder's Name:

Subject: Pre-Bid Queries

S. No.	Page No.	Clause No./Point No.	Description in the RFP document	Clarification Sought
--------	----------	----------------------	---------------------------------	----------------------

2.4.3 A pre-bid meeting will be held as per date, time and place given in section I, Prospective bidders may choose to attend the meeting physically/virtually. However, SMFCL will accept clarifications only received through e-mail mentioned in section I.

2.4.4 Response to all such clarifications will be compiled and uploaded in the GeM portal. Any modification to the bidding documents which may become necessary as a result of such responses shall be made by SMFCL. The clarification as well as modification of bid documents will be published as Addendum/Corrigendum to the bid document, on GEM Portal and deemed to have communicated to all prospective bidders. The published Addendum(s)/Corrigendum(s) will become an integral part of the bid document and binding upon the bidder. There will be no individual response to any bidder in this regard.

2.4.5 Time for Pre-Bid:

- Query Submission Deadline = 31th March
- Pre Bid Discussion meeting is schedule on 2nd April at 3 pm

Microsoft Teams meeting

Join:

<https://teams.microsoft.com/meet/48314019691971?p=l1PV0ARxMRDHXBMBJH>

Meeting ID: 483 140 196 919 71

Passcode: fX9AF9Ux

2.5 Zero Deviation

2.5.1 This is a ZERO Deviation Bidding Document. Bidder is to ensure compliance of all provisions of the bidding document and submit their bid accordingly. Bids with any deviation to the bid conditions shall be liable for rejection. This includes published Corrigenda/Addenda, if any.

2.6 Amendment of Bidding Documents

2.6.1 At any time prior to the deadline for submission of bids, SMFCL may for any reason, whether at its own initiative or in response to a clarification requested by a bidder, amend the bidding documents.

2.6.1.1 Amendments will be provided in the form of addenda/corrigenda to the bidding documents, which will be posted on GEM Portal. Addenda will be binding on bidders. It will be assumed that the amendments contained in such addenda/corrigenda have been considered by the bidder in its submitted bid.

2.6.1.2 In order to provide bidders a reasonable time in which to take the amendment into account in preparing their bids, SMFCL may, at its discretion, extend the deadline for the submission of bids, in which case, the extended deadline will be posted in Company's website and GEM Portal.

2.6.1.3 From the date of issuance of the addenda/corrigenda to the tender, it shall be deemed to form an integral part of the RFP.

2.7 JV / Consortium bidding

2.7.1 Any type of formation of consortium and joint assignments will not be allowed/ considered. Such proposals will be disqualified.

2.8 Preparation of Bid

2.8.1 Bid Price. Prices must be quoted in Indian Rupees only and should include all costs including all applicable taxes.

2.8.2 Period of Validity of Bids.

2.8.3 Bids shall remain valid for a period of 180 days after the date of bid opening.

2.8.4 SMFCL holds the right to reject a bid valid for a period shorter than 180 days as non-responsive, without any correspondence

2.8.5 Format of Bid: Bids shall be submitted online as detailed in the section - Submission of Bids, Clause 2.10.10 in this Section.

2.8.6 Bid Currency. All prices shall be expressed in Indian National Rupees (INR) only.

2.8.7 Bid Language. The bid shall be in English language only.

2.8.8 Preparation of Technical bid

2.8.8.1 Technical bid is preferred to be submitted through on-line mode. All information and documents in related to fulfilment of PQC criteria are to be submitted in the Eligibility Criteria and all information and documents related to technical requirement are to be submitted under the Technical proposal.

2.8.8.2 All scanned documents are to be signed/digitally signed by the authorised signatories, arranged sequentially with proper labelling, page no and indexed, irrespective of the content and to be uploaded at the respective sequence and proposal section.

2.8.9 Preparation of Financial Bid

2.8.9.1 Financial bid to be submitted through online mode in the format as defined in the bidding document. Same may be downloaded from GeM Portal and after filling, it is to be uploaded through digital signature. The detailed methodology of uploading of financial bid is enclosed at Annexure I of Section II.

2.8.9.2 Bidders to quote their rates strictly as per the financial bid format enclosed at Section VIII: Format 2 and uploaded as “Additional document” on GeM under Financial bid along with a printed and scanned pdf document, duly signed and stamped, as detailed in Annexure -I of Section -II.

2.8.9.3 Price Bid should give all relevant price information and should not contradict the Technical Bid in any manner. Price quoted by bidders with any deviation or any conditionality, the offer will be treated as incomplete and will be rejected.

-
- 2.8.9.4 All items in the Financial Bid (Section VIII) must be quoted failing which the bid is liable to be rejected.
- 2.8.9.5 The Bidder shall not quote, disclose or submit its price in the Technical Proposal or in any other manner, whatsoever, except as part of the Financial Proposal. In case of any non-compliance in this regard, the Proposal shall be out-rightly/summarily rejected.
- 2.8.9.6 In case the price/rate of a required line item is mentioned as zero i.e., "0" in FINANCIAL BID (Section VIII) the same shall be treated as the bid price for the item.
- 2.8.9.7 Rates quoted should be firm and fixed for entire contract period. No price variation and escalation will be allowed during the entire contract period.
- 2.8.10 Submission of Bids
- 2.8.10.1 Bidding shall be conducted **under Two Stage Bidding process viz, Technical (consisting of Eligibility & Technical) and Financial/Commercial through GeM** as specified in Annexure I and Section III.
- 2.8.10.2 Bidder fulfilling the Eligibility & Pre-qualification criteria mentioned in Section V should upload Bid document with duly signed scanned soft/hard (as applicable) copy of the documents given in Section VII along with the technical bid.
- 2.8.10.3 An incomplete and/or ambiguous and/or conditional Proposal and/or Proposal submitted late shall be out-rightly/summarily rejected.
- 2.8.10.4 Bidders are requested to submit their bid response well in advance of last date & time of bid submission. SMFC LTD shall not be held liable for any delay due to portal failure beyond its control. It is the bidders' responsibility to verify the portal for the latest information related to this RFP, which includes, but not limited to important dates, submission and opening of proposal, EMD/ Bid Security, Fee, address for communication, etc.
- 2.8.10.5 A bidder can submit one bid only. Not more than one tender shall be submitted by bidder(s) having business relationship. A breach of this condition will render the tenders of all such parties liable to rejection.
- 2.8.10.6 Bidder who has downloaded the tender document from the SMFC website / GeM, shall not tamper/modify the tender, including downloaded price bid template in any manner. In case if the same is found to be tampered/modified in any manner, tender will be rejected and EMD/ Bid Security would be forfeited, and Bidder is liable to be banned from doing any business with SMFC Ltd.
- 2.8.10.7 The bid offer shall be valid for a period of 180 days from the date of last submission of the bids for this tender.
- 2.8.10.8 Scanned copy of Earnest Money Deposit, Power of Attorney and Integrity Pact along with all annexures and supporting documents to be submitted online and the original documents to be submitted in hard copy form to SMFCL before opening of PQC-cum-Technical bid.

2.8.10.9 If SMFCL office happens to be closed on the specified date and time of opening of the bid documents, the bids will be opened on the next working day at the same time and venue or as may be notified by the Company.

2.9 Pre-Qualification & Technical Document submission

2.9.1 All the documents of Pre-Qualification Criteria documents (Eligibility Criteria) are to be properly named, labelled and sequenced. All pages and all related Annexures being submitted must be signed / digitally signed by the authorized signatory, irrespective of nature of content of the documents before uploading. Scanned and Signed copy of the documents are to be furnished by the bidder preferably consolidated in a single PDF file which shall form part of the Technical Bid.

2.9.2 Similarly, All the pages of technical documents and all related Annexures being submitted are to be properly names, labelled, sequenced and must be signed / digitally signed by the authorized signatory, irrespective of nature of content of the documents before uploading. Scanned and Signed copy of the documents are to be furnished by the bidder preferably consolidated in a single PDF file which shall form part of the Technical Bid.

2.9.3 The documents are to be sequenced properly as per relevance, labelled with page no, indexed. Bidders need to ensure that the size and format of the documents conform to the ones specified.

2.10 Price/Financial Bid submission

2.10.1 Price bid to be submitted in the financial bid section only. No documents related to price to be uploaded as part of the PQC-cum-Technical bid.

2.10.2 The Price Bid should give all relevant price information and should not contradict the Technical Bid in any manner. The prices quoted in the price bid should be without any conditions.

2.10.3 The Financial Proposal/Commercial Bid format is provided along with this tender document. Bidders are advised to download the excel sheet of Price Bid as it is and quote their offers/rates in the permitted column and upload the same in the commercial bid. Bidder shall not tamper/modify downloaded price bid template in any manner. In case if the same is found to be tampered/modified in any manner, tender will be completely rejected and Bidder is liable to be banned from doing business with SMFCL. For detailed information, **see Annexure – 1, Procedure for Submission of Financial Bid.**

2.11 Rejection of Bid. A bid is liable to be rejected if:

2.11.1 The document doesn't bear signature of authorized person.

2.11.2 It is submitted in hard copy form.

- 2.11.3 Incomplete/incorrect/non-responsive Bids, including non-submission or non-furnishing of requisite documents / conditional bids / bids or not conforming to the terms and conditions stipulated in this Request for Proposal are liable for rejection by SMFCL.
- 2.12 [Extension of Deadline for Submission of Bid.](#) SMFCL may, at its discretion, extend this deadline for submission of bids by amending the Bidding Documents which will be intimated GeM Portal, in which case all rights and obligations of SMFCL and Bidders will thereafter be subject to the deadline as extended.
- 2.13 [Modifications and Withdrawal of Bids.](#) Bids once submitted will be treated as final and no further correspondence will be entertained on this. No bid will be modified after the deadline for submission of bids.
- 2.14 [Right to Reject, Accept or Cancel the Bid.](#)
- 2.14.1 SMFCL reserves the right to accept or reject, in full or in part, any or all the offers without assigning any reason(s) whatsoever.
- 2.14.2 SMFCL does not bind itself to accept the lowest or any tender and reserves the right to reject all or any bid or cancel the tender any time during the tender process, without assigning any reason(s) whatsoever. SMFCL also has the right to re- issue the tender without the vendors having the right to object to such re-issuance.
- 2.15 [Contacting the Client](#)
- 2.16 Any attempt to contact SMFCL with a view to canvas for a bid or put any pressure on any official(s) of SMFCL may entail disqualification of the concerned bidder or his/her bid.
- 2.18 [RFP Abandonment.](#)
- SMFCL may at its discretion abandon this RFP process any time before Notification of Award or Work order.
- 2.19 [Other Terms and Conditions](#)
- 2.19.1 [Right to Alter Quantities & Repeat Orders.](#) SMFCL reserves the right to alter quantities as also to delete/add some items specified in this RFP.
- 2.19.2 SMFCL may, at its discretion, place orders based on the Change Management during the contract period, total of which shall not exceed 25% of total bid value as quoted in the RFP. All such additional orders will be based on the prices and terms & conditions fixed as per the main contract.
- 2.19.3 SMFCL may choose to purchase additional quantity of products/Licenses/services listed in this RFP as per the True-up schedule.

2.19.4 Engagement Duration: The engagement period will be for a period of 1+1+5 years, out of which first 1 year is to Understand, Design, Develop, Supply, Implement, Configure, Data Migration, Commission, stabilize; then 1-year warranty and then next 5 years to maintain & support the implemented & stabilized solution. After that the engagement period may be further renewed for 3 years (on yearly basis) based on mutual agreement between SMFC LTD and the selected bidder.

2.19.5 Offer from following types of bidders will not be accepted:

2.19.6 Who are under liquidation, court receivership and /or similar proceedings

2.19.7 Offer from joint bidders/consortium will not be accepted

2.19.8 The subject work is indivisible and shall be awarded to single successful bidder unless stated otherwise elsewhere in the tender document.

2.19.9 Bidder cannot make any claim against SMFC LTD towards its expense incurred in connection with the preparation and delivery of their bids, site visit, participating in the discussion and other expenses incurred during bidding process.

2.20 Clarification of Bids after submission

2.20.1 During evaluation of the bids, SMFC LTD may at its discretion, ask the bidder for clarification of its bid. The request for clarification and the response shall be in writing and no change in price of the bid shall be sought, offered, or permitted.

2.20.2 Written replies submitted in response to the clarifications sought by SMFCL, if any, will be reviewed

2.20.3 SMFCL reserves the right to interact with the customer references submitted by bidder, if required

2.20.4 No Bidder shall contact SMFC LTD on any matter relating to its bid, from the time of the bid opening to the time the work is awarded, unless asked for in writing.

2.20.5 Any effort by a Bidder to influence SMFC LTD in its decisions on bid evaluation, bid comparison or award decisions may result in rejection of the Bidder's bid and SMFC LTD will declare the bidder ineligible, either indefinitely or for a stated period from participation in future RFPs/tenders of SMFC LTD.

2.21 Bid opening & Evaluation Methodology

2.21.1 The SMFC LTD will first examine the bids to determine whether they are complete, whether any computational errors have been made, whether required sureties have been furnished, whether the documents have been properly signed and whether the bids are generally in order qualifying to which bids shall be summarily rejected.

2.21.2 Evaluation and comparison of bids will be carried as per provisions mentioned in the bid documents and documents submitted by the bidder(s). The bids will be evaluated for pre-

qualifying criteria first, as defined in Section-V and Evaluation Methodology as defined in Section VI. SMFC LTD reserves the right to verify the site of operation for above activity and list of persons provided as per qualifying criteria and accordingly decide upon meeting the requirement.

2.22 Award Criteria

2.23.1 SMFCL will award the work-order to the bidder whose commercial bid will be found to be in full conformity as per bid documents and becomes the H1 bidder as per evaluation methodology mentioned in **Clause 6.4**. In case of tie, bidder having scored higher in the Technical Evaluation phase will be declared as the successful bidder. In case, if that also results in a tie, the bidder having quoted lower Financial bid will be declared as the Successful bidder. In case, if that also results in a tie, the tied bidders will be asked to give a 'Best and Final Commercial offer'. The bidder offering the lowest price will be awarded the offer or else the above process will continue till the clear lowest commercial bid is arrived at. (Make-in-India guideline will be applicable in cycle/stage of this evaluation).

On issue of Award Criteria, bidder will acknowledge the receipt of the Word order within 3 days of the issue of work order and accept the same within 7 days of issuance of work order (working days).

2.23 Signing of Contract

Selected bidder will sign an agreement with SMFCL with all terms and conditions within 1 month of issue of work order.

Annexure I

2.25 Procedure for submission of Financial Bid (Through GeM portal)

The Financial Bid shall only be submitted electronically (through GeM portal). As per the following methodology:

- 2.25.1 The total financial quote (QP) will be entered as the Financial bid value in the GeM portal. This will be treated as the final financial quote.
- 2.25.2 The Bidder is then required to download the excel format uploaded in the Financial Bid (mentioned in Format-2, Section-VIII) from the GeM portal for providing detailed breakup.
- 2.25.3 The excel file shall be duly filled in the respective columns against each line item & the applicable GST. The individual line-item price and the total bid price will automatically be calculated by the excel file.
- 2.25.4 Bidders are required to duly fill in the financial break-up in the downloaded excel file only. Only financial figure needs to be filled in.
- 2.25.5 Bidders shall not tamper/modify downloaded excel/file template in any manner. In case, if the same is found to be tampered / modified in any manner, bid will summarily be rejected and bidder will be liable to be banned from doing business with SMFCL.
- 2.25.6 After that, bidders are required to upload the downloaded and filled in MS Excel file under the Price bid section of the bid in the portal.
- 2.25.7 It is to be strictly ensured that the total figure of the price break-up entered in the detailed breakup price table shall match with the amount (QP) entered in the Final Financial quote. In case of any discrepancy between these two, the amount quoted as the final financial quote (QP) will be taken as the final bid amount. Subsequently, if selected, the bidder shall resubmit the price quoted in the breakup table to match the finally accepted quote.
- 2.25.8 No price bid information shall be uploaded in the Technical bid. If any bidder uploads any price bid information as part of the technical bid, the bid will be summarily rejected and bid evaluation will continue for rest of the submitted bids.

SECTION-III – OBJECTIVE STATEMENT


3.1 Objective of the Assignment

The objective of this exercise is to develop, implement and maintain an integrated digital platform for capturing transaction (from source), store, process/analyze and share data and information across the organization without any intermittent manual intervention. It aims to automate and drive the entire business & other processes across all functional areas, in an integrated, efficient, resilient, robust, reliable straight-thru-processing manner satisfying the present and future needs & challenges.

The Enterprise Resource Planning System Implementer (ERPSI) shall understand the present and future need of the organizational business processes, document, design, develop and commission the Enterprise Resource Planning (ERP) System mentioned above integrating the business processes across the different all departments of the organization and support & maintain for the entire tenure of the contract. ERPSI will also continuously improve the system for efficiency as well as the needs that will come with the growth of the organization during the tenure of the contract.

ERPSI will also integrate the ERP system (ERP part) with other systems running/implemented in the organization, during the tenure, as per requirement. ERPSI shall play a critical role in helping businesses streamline their operations, improve efficiency, and make informed decisions by effectively deploying ERP solutions.

Key Drivers and Objectives of this project

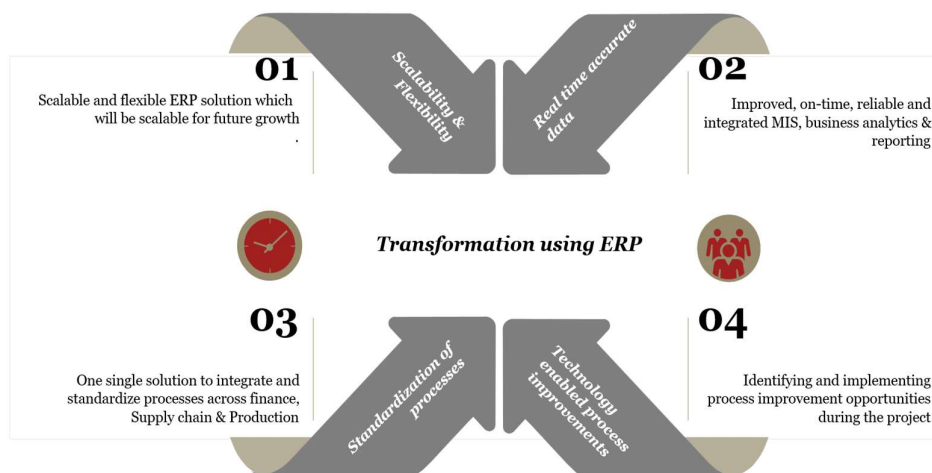

3.2 ERP Architecture

Enterprise Resource Planning (ERP) architecture states the structure and design of the software system that is to be used to manage and integrate various business processes and functions across different departments. The proposed ERP system shall be comprehensive, modular, SOA based, integrated, scalable, inter-operable Agile-based software solution that provides a centralized view of an organization's data and processes.

Here are key components and considerations in ERP architecture:

3.2.1 Presentation Layer

The presentation layer or user interface is what employees interact with to access and use the ERP system. A well-designed, intuitive and user-friendly UI is essential for user adoption and efficiency. ERP systems should offer web-based interfaces which is responsive and can be accessed from a variety of devices.

- *Purpose:* User interface for accessing ERP functionalities.
- *Components:* Web portals, mobile apps, dashboards, website
- *Technology:* HTML5, JavaScript frameworks, mobile SDKs.

3.2.2 Application Layer: The application layer is where the ERP software runs. The software It consists of various modules that cater to different business functions such as finance, human resources, project management and business reporting etc. Each module is responsible for specific tasks and interacts with the database to retrieve and update data.

3.2.2 Business Process Layer

- *Purpose:* Orchestrates workflows and business logic.
- *Components:* BPM engines, workflow managers.
- *Function:* Coordinates services to execute end-to-end business processes like order-to-cash or procure-to-pay.

3.2.3 Service Layer

- *Purpose:* Encapsulates business functions as services.
- *Components:* Inventory service, HR service, finance service, etc.
- *Design:* Services are loosely coupled and reusable across modules.

3.2.3 Integration Layer

ERP systems should be designed to integrate and streamline various business processes. The proposed ERP system will be developed modular with each module carries out specific business activity. All these modules will be integrated at the integration layer so that data flows seamlessly between different modules and external systems without any/minimal manual intervention. This layer will also include middleware and connectors to link the ERP system with other software, such as in-house applications

systems, e-commerce platforms, third-party applications etc. In this context, in future if SMFC LTD opts for third party modules offering API based integrations, ERPSI will provide such integration by making additional developments for enabling such integration on mutually agreed terms, conditions and charges.

The ERP system will also be integrated with the DNS & AD system of the organization, to provide authentication and single sign-on provision, if required.

Key Integration Flows (examples)

- **Hire-to-Retire (HR → Finance → HR)**

Recruitment → Job allocation → Learning, Development, Promotion, Transfer, Disciplinary Action, Vigilance → Superannuation

- **Hire-to-Pay (HR → Finance):**

HR creates employee → Payroll calculates net pay → Finance posts payroll journals to GL → Treasury triggers disbursements via payment rails → Notifications send payslips → Superannuation

- **Procure-to-Pay (Inventory/Procurement → Finance/Treasury):**


PO → Inventory → AP invoice created in Finance → Treasury schedules payment → GL postings → Life Cycle

- **Loan Origination-to-Servicing (Loan → Treasury/Finance):**

Application → Received → Appraisal → approval → Disbursement from Treasury → Repayment schedules to Finance (AR) → Collections workflow via events → Risk metrics updated.

- **Work-Order-to-Asset (Technical → Finance/Inventory):**

Work order consumes parts (Inventory) → Cost capitalization in Finance → Asset register updated → Depreciation scheduled.

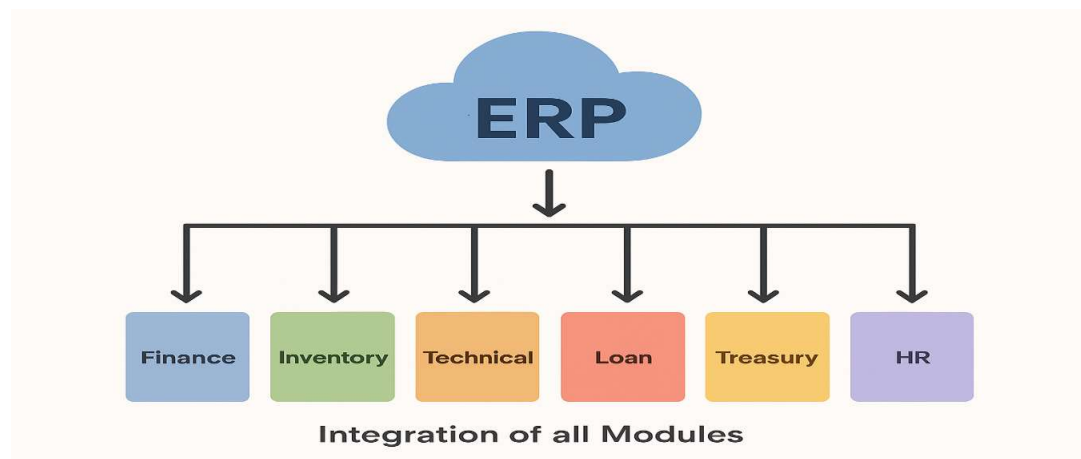

ERP integrated Data Flow



3.2.5 Data Layer (Database)

The data layer is at the core of any ERP system. It should store all the data related to SMFC LTD business processes, including customer information, inventory, financial data, and more. The selected database management system (DBMS) shall be open-sourced based, preferably PostgreSQL

3.2.6 Security & Governance Layer

- *Purpose:* Ensures secure and compliant operations.
- *Components:* Identity management, access control, audit logs.
- *Function:* Enforces policies, monitors service usage, and ensures data protection.

3.2.7 Scalability: ERP architecture should be scalable to accommodate the growth of SMFC LTD. As the business expands, the ERP system should be able to handle increased data loads, user accounts, and transaction volumes without significant performance degradation.

Security: Security is a paramount concern in ERP architecture. Security to be made as integral part of the development, implementation and maintenance phase as per standard SSDLC. Confidentiality, data integrity, Access control, data encryption and other security measures are essential to protect sensitive business data from unauthorized access and breaches.

High Availability: Ensuring high availability is crucial to minimize downtime. This often involves redundancy, failover mechanisms, and disaster recovery plans.

Cloud hosting, Business Continuity and Recovery: The developed ERP system shall be hosted on cloud environment. Cloud-based ERP systems offer scalability and reduced infrastructure management. In addition, the ERP system is to implement and configure in both primary and secondary data centers with appropriate replication, backup and recovery mechanism as per defined RTO, RPO etc. Periodical exercise and support for live DR drill need also to be carried out.

Mobile Access: The ERP architecture to be designed and system to be developed to support operation on mobile devices (for both Android and iOS platforms) or responsive web interfaces for all types of mobile devices to enable users to operate, access data and perform tasks using on the go.

Analytics and Reporting: ERP system shall have an in-build Dashboard system that includes built-in reporting and analytics tools that allow users to generate insights from their data in report/tabular/graphical mode. The architecture should support these features and enable the extraction of meaningful business intelligence. There will also be feature to generate trivial & adhoc reports by the end-users.

Compliance and Regulatory Requirements: NBFCs are subject to many regulatory compliance requirements. ERP systems shall need to adhere to specific compliance and regulatory standards. The architecture should facilitate the implementation of necessary controls and reporting capabilities to meet these requirements. Some indicative standards are as specified by RBI, parent ministry, MeitY, SEBI, ITAA 2008, DPDP Act 2023, National Cyber Security Policy, Cert-In, ISO etc.

Version Management & Change Management: Version and Change management are critical components of IT governance and Software Life Cycle management. These ensure that updates, enhancements, fixes and issues are implemented in a controlled, traceable, documented and efficient manner under automated workflow environment. Automated tools shall be used for these purposes.

Standard Separate instances for different purposed: To create and maintain separate instances viz, Production, Staging/Quality, Testing, Development etc. for the ERP system. Backup of each of the same.

ITSM tools-SLA Management and Ticketing tools: To implement and support integrated supporting tools to streamline IT service operations including SLA tracking, incident & request management, reporting and integration with the ERP system. It is desirable that the SLA reports are generated through this tool by capturing data directly from the IT systems under the set-up.

LOG management: To develop/configure/implement system and processes to collect, store, analyze and monitor log data generated by the ERP and other systems under the scope. It shall be able to provide data to an integrated Security center, if needed.

3.3 Implementation phase

The following phases shall be followed during the ERP implementation:

3.3.1 Project Planning: Develop a detailed project plan that outlines the implementation timeline, resource allocation, and milestones. This plan should also address data migration and system testing.

3.3.2 Business Needs: To thoroughly understand the existing and future needs, goals, and processes of the client's business. This involves conducting a comprehensive analysis of the existing and proposed NBFC systems, processes and workflows.

3.3.3 Delivery: Supply of licenses, software etc.: Required as per Scope of this bid.

3.3.4 Development: To develop the ERP system aligned with the identified processes and requirements of the SMFC LTD business in integrated manner mentioned here-in.

3.3.5 Testing and Quality Assurance: Rigorously test the ERP system, both module-wise (CRP) and integrated manner, to identify and resolve any issues or bugs before going live. This includes unit testing, integration testing, and user acceptance testing.

3.3.6 Data Migration: Ensuring a smooth transition of data from the legacy systems to the newly developed ERP system is crucial. The ERPSI must migrate data accurately and efficiently, minimizing downtime and zero data loss. Mock runs of the Data Migration are also be conducted to verify the effectivity of the plan.

3.3.7 Training and Change Management: Train employees on how to use the ERP system effectively. Additionally, provide change management support to help employees adapt to new processes and workflows. Training categories includes Change Management activity, training for Senior Management, end-users, technical training for IT staffs, IT Admin etc. The ERPSI shall prepare detailed training plans and comprehensive manuals for each of these training; change management support.

3.3.8 Go-Live Support: Assist SMFC LTD during the ERP system's launch to ensure a smooth transition. Address any immediate issues or concerns that may arise during the initial period of usage.

3.3.9 Stabilization Support: Provide post deployment stabilization support which includes, inter-alia, hand-holding support, identifying and resolving bugs or issues, providing minor enhancements & configuration adjustments, monitoring system performance and availability and ensuring data integrity and security.

3.3.10 Warranty support: To provide warranty support post stabilization for the pre-defined period which includes bug fixing, gaps, efficiency enhancement, support, improvement etc.

3.3.11 Post-Implementation Support: Provide ongoing support and maintenance to address any post-implementation issues, software updates, new business requirement and continuous improvement efforts.

3.3.12 Monitoring and Performance Optimization: Continuously monitor the ERP system's performance and identify areas for improvement. Optimize the system to enhance efficiency and meet evolving business needs.

3.3.13 Cost Control: Manage the project within budget and seek cost-effective solutions wherever possible.

3.3.14 Documentation: Maintain comprehensive documentation of the ERP system's configuration, customizations, user-manuals and integrations for reference and future upgrades.

Overall, the objective is to enable SMFC LTD to leverage ERP technology effectively to achieve its strategic goals and improve its competitive position in the market. This involves a combination of technical expertise, project management skills and a deep understanding of the business processes.

SECTION-IV - GENERAL FEATURES OF SYSTEM

4. Overview

The ERP system should be so designed such that all the required software with upgrades satisfy the ERP system requirements and service level agreements as specified in this Contract while considering technical obsolescence over the operating life of the system and suitability for future scale up. Entire responsibility of design phase to support & maintaining phase of fully functional ERP system starting from scratch shall rest with the ERPSI, including meeting the performance levels as given in the Contract. The ERPSI shall ensure that the Solution complies with the Applicable Law, technical specifications, and other provisions of the Contract.

4.1 Scope of Work

Broad Scope of Work includes implementation of a fully functional cloud-hosted ERP system to meet the performance levels as given in the Contract. The ERPSI shall ensure that the Solution complies with the Applicable Law, technical specifications, and other provisions of the Contract.

.4.1.1 Detailed Scope of Work includes:

- 4.1.1.1 Understand, Design, Develop, Install, Configure, Test, Implement, Migrate, Commission, Stabilize, warranty, Support and Maintain a Customized & tailor-made ERP System, fulfilling necessary features of a standard ERP system & Website development & Hosting of SMFCL website and meeting needs of SMFCL.
- 4.1.1.2 Supply of all necessary tools, licenses and other IT systems necessary for design, development, testing and managing various instances and scope as defined in this document.
- 4.1.1.3 Recommend necessary hardware, network and security infrastructure requirement for running and maintaining the ERP system
- 4.1.1.4 To follow standard Secured Software Development Life Cycle during entire of the contract.
- 4.1.1.5 To provide complete documentation of the project which includes but not limited to System Requirement Specification (SRS), Functional Design Document (FDD), Technical Design Document (TDD), User Training Manual (UTM), test case document, configuration documents for administrators etc.
- 4.1.1.6 It is the responsibility of the bidder to prepare data migration strategy, planning and templates for all data points required for one-time migration from the legacy system(s) to the newly developed ERP system. It should be ensured that document date of posting of document in legacy system, may be captured.
- 4.1.1.7 To provide system familiarization training to all employees of SMFCL including top management and also drive change management activities.
- 4.1.1.8 Installation and configuration of Data Base system

-
- 4.1.1.9 Supply, installation, customization, configuration, Go-Live and management of SLA management & Ticketing tool
- 4.1.1.10 Following features shall be a part of the new ERP system and under the scope
- Email & SMS alerts. Provide SMS gateway
 - Email gateway will be provided by SFCL, however feature for auto mail will be developed/integrated in system.
 - SMS and WhatsApp gateway will be borne by SFCL, however ERPSL will be facilitate arrangements of such services for SFCL and integrated the services with software for auto/transaction based alerts.
 - Audit Logs, versioning, Change Management
 - Thorough testing of the new system at each phase
 - Bug fixing and resolution
 - Ensure appropriate backup, restoration, recovery & DR drill
 - Define Go-Live procedures and roll-out of the system to all users
 - Post implementation support & maintenance
 - Develop Dashboard and generation of MIS reports
- 4.1.2 Technology framework to be used for development
- 4.1.2.1 Open-source platform
- 4.1.2.1.1 The new system to be developed with open source technology stack like Microsoft .Net/PHP/JavaScript/Angular technology stack preferably utilizing MVC architecture and incorporating the latest versions of HTML, CSS etc. and also ensures an secured and user-friendly user experience.
- 4.1.2.1.2 Any external integrations with the proposed ERP system shall use open standards like OpenAPI, OAuth 2.0, SOAP etc.
- 4.1.2.2 The application must prioritize device responsiveness. It should adapt seamlessly to various devices, including desktop computers, laptops, tablets, iPad and mobile phones.
- 4.1.2.3 Any version change in the OEM software used within the application shall be upgraded by the bidder at no additional cost during the contract period.
- 4.1.2.4 Backend of the application to utilize Postgres SQL server, latest version. Bidder has to ensure that the database designed for the application shall be at least in third normal form and code writing should have much as much elaboration as possible.
- 4.1.2.5 System developed to be made as much parametrized as possible and instances of hardcoding shall be avoided.
- 4.1.2.6 The System design and coding to be done with Security by Design and Privacy by Design principle
- 4.1.2.7 The ERP system must demonstrate cloud-native architecture with benchmark for loads, user and data volume which will be decided at the time of design phase. Bidder to present

Module-wise prototypes before and obtain approval from SMFCL. TO-BE phase will not be considered completed without this activity.

4.2 Infrastructure and Audit requirement

- 4.2.1 The new system shall be hosted on a cloud environment. However, if decided in future, to host the System at on premise data centre, bidder will be responsible for complete migration from cloud to on premise environment.
- 4.2.2 Prior to Go-Live and post UAT phase, Bidder shall arrange for the application to be audited by a CERT-In empaneled auditor for a comprehensive VA/PT audit including OWASP Top 10 vulnerabilities. A detailed audit and closure report are to be submitted by the bidder prior to Go-Live phase.
- 4.2.3 Prior to Go-Live and post UAT phase, Bidder shall conduct a Data Migration audit by a CA/Cert-In empaneled agency to ensure that legacy data has been uploaded in the newly developed system properly. A detailed audit and closure report are to be submitted by the bidder prior to Go-Live phase.
- 4.2.4 The statutory Business Continuity Management policy necessitates business critical applications adhere to the directives and guidelines stipulated by statutory bodies. Compliance of the same will be the responsibility of the bidder at no extra cost during entire tenure of contract.
- 4.2.5 SMFCL will undertake VA-PT, security audits, information system audits etc. of the application and infrastructure on regular basis to assess any vulnerabilities in the IT Set-up. It will be the responsibility of the bidder to facilitate all such audits and close any such observations that occur, on account of the ERP application.
- 4.2.6 To ensure backup, data replication, DR Drill are carried out within specified parameters and frequency within the scope of the bidder.
- 4.2.7 The developed ERP system should be robust enough to handle concurrent load of 100 users at any point of time, as operation will be carried out by all employees simultaneously and there shouldn't be any slowness or service disruption during peak load.
- 4.2.8 The development and testing environment for the system shall be provided by SMFCL at its local Data Centre
- 4.2.9 On request, remote VPN access to the development & testing environment may be provided to the bidder subject to:
- 4.2.10 Access is done through device and set-up owned by the bidder having all latest end-point security and under protected and secured environment and not through private or public device or network.
 - 4.2.10.1 Used by its employee deputed only in this project
 - 4.2.10.2 An undertaking is furnished before such remote access is provided

4.3 Go-Live

Go-Live will be declared only on completion of:

- 4.3.1 Signing of User Acceptance Testing phase
- 4.3.2 Completion of Data Migration phase (Migration, verification, Audit & closure)
- 4.3.3 Completion of Security audit phase (Audit, verification, closure)
- 4.3.4 Submission of documents & deliverables specified in section IX.
- 4.3.5 Training to end-user & IT department users
- 4.3.6 Final system validation check & smoke testing
- 4.3.7 Set-up of DC & DR - Configuration, tuning, instances, Log enabling etc.
- 4.3.8 Backup and roll-back planning
- 4.3.9 Integration with AD, User identification, role & access provisioning
- 4.3.10 Backup & Rollback planning
- 4.3.11 Establish Help Desk support, resource on boarding
- 4.3.12 Final communication
- 4.3.13 Final cut-over activity


ERPSI shall prepare a Comprehensive Go-Live strategy containing all these activities in detail and get it approved by SMFCL.

4.4 Post Go-Live phase

- 4.4.1 The application will have a 3 months Stabilization phase after declaration of Go-Live.
- 4.4.2 The application will be under warrantee for a period of 1 year after expiry of stabilization period.
- 4.4.3 The application will be under support & maintenance phase for a period of 5 years after warrantee period. There will be provision to extend this phase for another 3 years (annual basis) after 5 years on mutually agreed upon terms and conditions.
- 4.4.4 Troubleshooting, bug-fixing, hand-holding, enhancement & modification of functionalities within broad scope of work, regulatory compliance, Change management etc.
- 4.4.5 Framing of required & relevant policies, SOPs, training, documentation etc.
- 4.4.6 Bidder shall arrange for the application to be audited by a CERT-In empaneled through out the contract period as per CERT-In / RBI / Govt Guidelines.
- 4.4.7 Procurement and deployment of all necessary certificate/ Licenses etc. shall be consider under the scope of ERPSI.
- 4.4.8 The cost associated with Audit requirement, including all expenditure shall be part of ERPSI. SMFCL shall not pay any charges on this account.
- 4.4.9 Other Scope
 - 4.4.9.1 ERPSI will devise other required policies, procedures, guidelines for smooth running of the ERP system
 - 4.4.9.2 The ERP system shall operate reliably in the network range of SMFC LTD

4.4.9.3 Furthermore, the ERPSI shall be the Single Point of Contact (SPOC) relating to all responsibilities and issues pertaining to Implementation of overall ERP System.

4.4.9.4 The ERPSI shall be required to carry out the scope of work as per standard ERP implementation phases, which shall include but not be limited to the following:

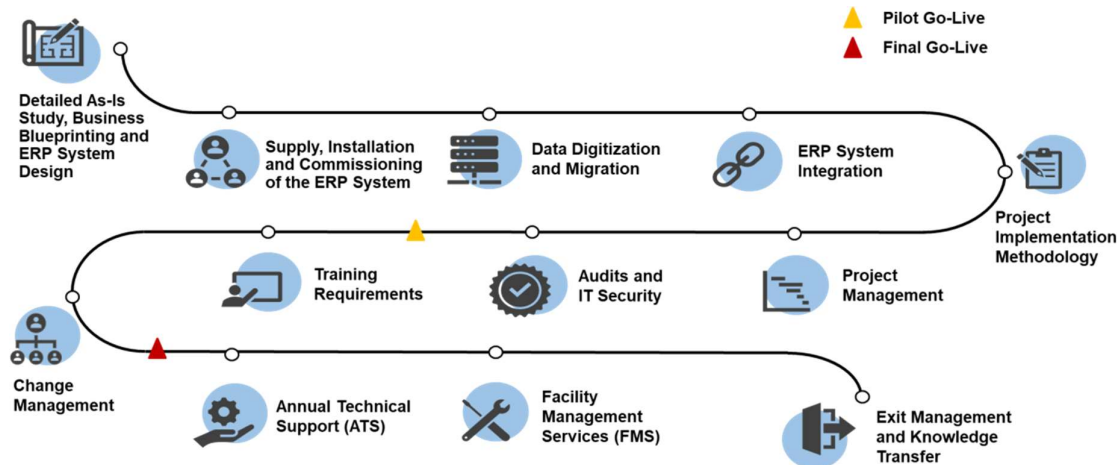

4.4.9.5 Unless otherwise stipulated in the RFP or Contract, the scope of work shall include all such items not specifically mentioned in the Contract but that can be reasonably inferred from the Contract as being required for comprehensive, successful, and satisfactory implementation of the Solution as if such items were expressly mentioned in the Contract. The same may be mutually enlisted and agreed upon by SMFC LTD and ERPSI during the design phase as defined in the Contract.

4.4.9.6 Wherever references are made in the RFP to codes and standards in accordance with which the Solution shall be executed, the edition or the revised version of such codes and standards shall be those specified in the scope of work.

4.4.9.7 The systems which are at a risk of technical obsolescence over the operating life of the system should be identified; this should include end-of-sale and end-of-support policies governing the proposed technologies. Forward and backward compatibility need to be considered and mitigation option shall be indicated in detail and shall not be limited to periodic update from implementer.

4.4.9.8 Unless otherwise stipulated in the RFP or Contract, the scope of work shall include all such items not specifically mentioned in the Contract but that can be reasonably inferred from the Contract as being required for comprehensive, successful, and satisfactory implementation of the Solution as if such items were expressly mentioned in the Contract. The same may be mutually enlisted and agreed upon by SMFC LTD and implementer during the design phase as defined in the Contract

4.4.9.9 Following shall be excluded from ERPSI's scope of work under the contract:

- Providing hardware including OS, network and security infrastructure for hosting application

- Building of Data Center including construction of building, air conditioning, ventilation, lighting, and fire-fighting system for ERP Data Monitoring Centre
- Providing Network link from Network/Internet service provider (NBSP).
- Any modifications in the existing IT systems of the SMFC LTD (Website, etc.)

4.5 Functional Requirements

4.5.1 ERPSI shall carry out As-Is Study for existing Enterprise Architecture, IT Applications & Solutions, SMFC LTD Business process, Cloud Infrastructure Solutions, End user's competency etc. along with requirement gathering workshops to identify the Gaps and areas of improvements in current state of SMFC LTD. The ERPSI will take the necessary inputs and approval on the formulated As-Is Status report from Stakeholders/Nodal Officers of SMFC LTD.

4.5.1.1 All business processes; existing, which are likely to be introduced near future and can be envisaged shall under the functional scope of requirement.

4.5.1.2 ERPSI will identify and make suggestions on existing IT Applications & Solutions which need to be phased out post implementation of the ERP System.

4.5.1.3 ERPSI shall formulate the As-Is & To-Be Document (Business blue print including Gap), Business & Process Design Documents, Technical Design Documents – HLD & LLD including Data Conversion & Migration Strategy based on the requirement gathering workshops in line with the Scope of project. This will also include Business Process Reengineering, process improvement, efficient inter-process information exchange etc.

4.5.1.4 ERPSI shall carry out detailed Functional Requirement study, System Requirements Study and Finalize Business Blueprint Design for ERP System

4.5.1.5 All the software and database licenses delivered shall be in the name of SMFCL Ltd with perpetual, irrevocable, transferable rights and no vendor renewal dependencies. Additionally, the ERPSI shall be responsible for renewing all required licenses under the scope until the end of the AMC period. Also SMFCL shall have exclusive ownership for all the codes developed during the entire phase of the project. The ERP solution together with relevant database, licenses, and other software in conformance to Industry standards, shall include the modules and sub-modules, mentioned in the following section, at the minimum.

4.6 Modules to be developed

Following modules, which are tentative, are to be developed as part of the ERP project:

4.6.1 Accounting Modules

- a. Accounting/General Ledger as per prevailing standard
- b. Trial Balance & Balance sheet as per Ind-AS (or any prevailing standard)

-
- c. Budgetary control and Linkage of expenditure with budget
 - d. Ind-AS features for discounting of Assets/Liabilities and integration of same with Accounting/Balance Sheet modules.
 - e. BRS and Interest Reconciliation. As per interest certificates from different Banks
 - f. TDS
 - g. GST
 - h. Fixed Deposit management, including tracker and it's reports.

4.6.2 Fixed Assets

4.6.3 Employee Related Modules

- a. HRIS (Hire to Retire including promotion, transfer, attendance, Leave management etc.)
- b. Payroll including Superannuation benefit
- c. Superannuation portal
- d. Computation of Income Tax
- e. Interest on loans
- f. Employee Self Service (ESS)

4.6.4 Loan Origination System

4.6.5 Entity Appraisal including KYC, Credit Rating

4.6.6 Project Technical Appraisal

4.6.7 Loan Accounting & Management System - Assets

4.6.8 NPA Management

4.6.9 Legal Module

4.6.10 Payable Loan Control System - Liabilities

4.6.11 Asset Liability Management

4.6.12 Payable Controls

4.6.13 Credit Risk Management

4.6.14 Compliance

4.6.15 Dashboard

4.6.16 Vendor Portal

4.6.17 Customer Portal

4.6.18 Inventory Management

4.6.19 Grievance Portal

4.6.20 Reports/Analytics/MIS

4.6.21 Website

4.6.22 Mobile Apps

4.7 Tentative Scope of Each Module

The module-wise detailed requirements given here are tentative and minimum requirements. However, actual requirements will be finalized during the information/requirement gathering phase (As-Is) of the project. Also the ERP system will evolve and mature along with the maturity of the business processes in SMFCL with time during the entire tenure of the project.

4.7.1.1 Accounting modules

Accounting system enables recording of voucher, generation of financial statements/reports. The accounting system will be multi-location and multi-unit. The system will have integrated interface with Diary, TDS, BRS, Interest Calculation etc.

- Voucher Creation - Accounting System accepts vouchers from Claim Processor and also provides option for generating JV/BPV/BRV/CPV/CRV. All vouchers are initially stored as temporary vouchers and voucher number is not assigned to same at this stage. However, system shall permit direct posting of vouchers in case of non-availability of manpower at a particular Hierarchy or in case of exigency of work.
- Integration with sub modules – Vouchers are the final stage transactions in accounting and depending on nature of account code operated various types of details could be required for completing the voucher. Few examples of such additional details are below
 - o For current/non-current working of balance on Balance Sheet date, expected disposal date of transaction to be insisted.
 - o In case of TDS deductions, gross value, tax rate, tds section etc. to be included.
 - o For employee loan payments, recovery start date and installment to be included.
 - o For insurance payments – period of validity to be insisted so that pre-paid expenses can be computed.
 - o For Inter Unit Transactions – Advice Number to be insisted.
 - o For Fixed Assets transactions – Details of assets to be insisted.
 - o Approval of miscellaneous expenses of officials as per DOP–employee number of approving officer so that annual limit can be enforced
- Approval of Vouchers – All officers of finance have been delegated powers for approval of vouchers as per their level and type of vouchers. Such powers will be defined in system and according to type/amount of voucher, approval by suitable level of officer will be insisted by system. Voucher approval may require forwarding of voucher to senior levels and final approval by seniors, therefore “WORKFLOW” for such approval channels will be developed. Details of officers who approved/recommended the voucher will be printed on had copy of voucher.

-
- Voucher Posting – Temporary vouchers are posted in accounting system according to the financial limits of users. Normally vouchers are created in accounting on current date, however in special circumstances vouchers can be created on back dates with the authorization of Administrator.
 - Tool for creation of voucher from excel data.
 - Provision of pushing of payment vouchers on Banking platform
 - Provision for posting of Loan repayment entry of Borrower directly from Banking Platform to ERP system
 - Financial Reports
 - Trial Balance
 - General Ledger
 - Party Ledger
 - Party Balance Summary
 - Bank Book/Cash Book
 - Voucher Reports
 - Summary of Vouchers
 - Banking Reports
 - Cheque Forwarding Letter to parties
 - RTGS Letter to Bank
 - Cheque printing – In Case of RTGS/DD Front side in the name of Bank and back side with payee details
 - Cheque Register
 - Bank Credit List for employees
 - Queries
 - Searching Vouchers according to voucher number, date, party code, amount range etc.
 - HBA /Education Loan Insurance
 - Secured/unsecured employee loans
 - Count of vouchers- Summary of vouchers in given date range
 - Trial with Monthly balances
 - Department Wise Cost
 - Exception Reports
 - Non-Moving Balance
 - Odd Balance Report
 - Balances for left employees
 - Other exception reports as decided during implementation

- Archive of Scanned documents for annexure of vouchers
 - o Scanned copy of annexures and signed copy of voucher uploaded in system.
 - o Such documents are maintained with hierarchy of Unit, Year, Month, Date, Voucher Type, Voucher No and can be searched according to given parameters.
 - o Such documents are stored in secured manner with limited access to power users.
- Exception Reports- Age Wise Analysis of SD/EMD/BG/Creditors/Payable
- Ind AS Related Transaction (New) - Discounting of Long Term Financial Assets & Liabilities , Computation of ROU Assets/Liabilities, Related Party Transaction code.

4.7.1.2 Bank Reconciliation

- o Reconciliation of Banking transactions as per accounting and Bank Statement.

4.7.1.3 TDS Controls

Capture data from transactions for TDS needs and generate quarterly returns for different sections of TDS.

4.7.1.4 GST Controls

- o In case of GST, TDS Deductions, Gross Value, Tax Rate, GST-RCM etc. to be insisted.
- o For GST Returns data: GST FCM and GST RCM/GSTR – R1, 3B, 7, 9, 9C, 2A,2B etc. format data from the ERP system.
- o Computation of GST in case of Forward charge such as Loan processing fee etc., and generation of invoice in compliance with GST Act.

4.7.1.5 Fixed Deposit Tracker and its Reports:

Fixed Deposit module to be devised and it's report to be generated for interest and accrued interest reconciliation as per the interest certificates from different banks for different FD(s) made during the financial year.

4.7.1.6 Balance Sheet

- Masters for
 - o Balance Sheet Schedules/Notes
 - o Format of Balance Sheet with options of formatting/controls
 - o Mapping of Account Codes with Balance Sheet Grouping Codes
 - o Mapping of Grouping Codes with Balance Sheet Format
 - o error of Balance Sheet
- Balance Sheet to be generated as per prevailing accounting standard (e.g. Ind-AS) with schedule 6 requirements i.e. Details of current/non-current balances. Such

current/ non-current balances to be generated automatically with manual intervention according to input provided during creation of vouchers.

- ☐ Balance Sheet generated for 3 accounting cycles so as to generate cash flow automatically.
- ☐ Provision for opening, locking, un locking Balance Sheet and consequent protection of corresponding of accounting data.
- ☐ Reporting
 - o Balance Sheet
 - o Cash Flow Statement
 - o Grouping
 - o Consolidated Balance Sheet of company
 - o Consolidation with unit wise details
 - o Unit wise trial balance
 - Ind-AS features for discounting of Assets/Liabilities and integration of same with Accounting/Balance Sheet modules.

4.7.2 Fixed Assets

- ☐ Databank of all assets of corporation with details of
 - o Category of asset – Major/Minor/Group
 - o Description of assets
 - o Quantity
 - o Physical location for physical verification
 - o Purchase Details – supplier, bill no, date, basic cost, taxes etc.
 - o Capitalization Date
 - o Depreciation Rate as per company's act, IT act, Electricity Act, CERC etc.
- ☐ Enable depreciation computation under multiple methods i.e. Companies Act, Income Tax etc.
- ☐ Gross Block/Cumulative Depreciation to be maintained individually for each head.
- ☐ Special Provisions for
 - o BER Assets
 - o Zero Depreciation Categories i.e. Land
 - o Full Depreciation Categories i.e. Small value assets
- ☐ Transactions for assets
 - o Addition of assets through purchase, transfer, acquisition etc.
 - o Sale of assets
 - o Write off/deletion of assets

-
- o Inter Unit Transfer of assets to other units
 - o Intra Unit Transfer of assets within same unit i.e. From one head to other head
 - o Adjustment for gross block/depreciation
 - Computation of depreciation
 - o According to methodology required for depreciation method adopted by company.
 - o Proportionate according to number of days of utilization
 - o Computation of prior period depreciation
 - Reporting
 - o Asset Schedule – Group Wise, Sub Group Wise, Asset ID Wise
 - o Asset register
 - o Transactions during the period
 - o Physical Verification Reports I.e. Location Wise, Category Wise reports of assets
 - o Other reports as decided during implementation

4.7.3 Employee Related Modules

4.7.3.1 Human Resource Information System

- 4.7.3.1.1 Scope: Entire manpower resource life cycle from Hire-to-Retire that includes Recruitment, Manpower & Succession planning, Learning & Development, Promotion, Transfer, Disciplinary Action, Vigilance & Superannuation etc.
- 4.7.3.1.2 Employee Master – Joining/Resignation/Leaving/Promotions and Increments & Deductions
- 4.7.3.1.3 Time Office – Attendance Management System with integration with bio metric, monthly attendance finalization, out duties etc.
- 4.7.3.1.4 Leave Management System – Credit, Online leave application/approvals
- 4.7.3.1.5 Employees Performance Appraisal System
- 4.7.3.1.6 Employees Asset & Liability details (including Lokpal)

4.7.3.2 Payroll System

- DPE Based pay structure
- Components of Pay
 - o Basic Pay – Fixed on initial appointment, revised on increments/promotions. The Basic is regulated with pay structure and increment rates.
 - o DA – Revised on quarterly intervals.
 - o HRA – Percentage of Basic Pay
 - o Lease as per corporation rules paid in lieu of HRA. In case of Lease, HRR/Extra Rent recovered as per defined rates. Applicable perquisites for company provided accommodation also computed for Income Tax purpose.

-
- o Perquisites – As per prevailing policy of the corporation. There shall be provision for Employees to choose scheme, heads and percentage of perquisites within overall prescribed limit.
 - ☐ Variable Transactions
 - o Provision for variable payment /recoveries from salary for components selected by users and for amount defined. Such option to be used for handling temporary payments/recoveries not handled in normal payroll processing.
 - ☐ Permanent Payment/Recoveries
 - o Fixed amount payment/recoveries for a defined period of time.
 - ☐ Savings recoveries from salary
 - o Recoveries for LIC, VPF etc. Schedules for such recoveries will be generated along with policy number for submission to respective organizations and also recoveries will be considered for rebate computation while computing income tax.
 - ☐ Statutory Recoveries
 - o PF as per statutory requirements
 - o Company contribution
 - o ENPS/NPS as per statutory requirements.
 - ☐ Loan recoveries -
 - o One-time outstanding balance of loans imported in payroll.
 - o Regular payment of loans will be entered manually in payroll system.
 - o Payroll to ensure regular recovery of loans, tracking of balances and recovery of interest after full repayment of principal.
 - ☐ Modalities for computation of pay revision due on 01.01.2027
 - ☐ Provision of Employee claims such as Travelling, Medical, Telephone etc.
 - ☐ Forms
 - o Input –
 - ☐ Employee Master
 - ☐ Basic Details – Employee No, Name, Designation, Department, Date of Birth, Date of Leaving, Date of Joining etc.
 - ☐ Pay Details – Basic Pay, Personal Pay, Special Pay, Family Planning Allowance, Stagnation Pay etc.
 - ☐ Allowance Details – HRA, Lease, DA Category, Perquisites and other allowances.
 - ☐ Increment Details – Date of increment and flag for allowing/ disallowing increments.

-
- ☐ Variable Transactions
 - ☐ Employee No
 - ☐ Transaction Head
 - ☐ Payment/Recovery
 - ☐ Amount
 - ☐ Month for which payment is being made
 - ☐ Permanent Payment/Recoveries
 - ☐ Employee No
 - ☐ Transaction Head
 - ☐ Period of payment/recovery
 - ☐ Amount
 - ☐ Loan Details
 - ☐ Loan Head
 - ☐ Principal Amount
 - ☐ Installment
 - ☐ Balance
 - ☐ Start month of recovery
 - ☐ Saving deduction
 - ☐ ☐ ☐ Employee No
 - ☐ Controls
 - ☐ Savings Head
 - ☐ Amount
 - ☐ Period of recovery
 - ☐ Monthly computation and payment of salary
 - ☐ Booking to Accounting System – Consolidate or company wise
 - ☐ Accrued Interest for the month to be booked with salary
 - ☐ Data of closed months protected
 - ☐ Data of closed months available for reporting
 - ☐ Arrears for promotion/salary revision
 - ☐ Input of revised Pay and effective period
 - ☐ Arrear computation in the event of revision of pay from back date
 - ☐ Arrear statement with due/drawn
 - ☐ Transfer payable amount to salary and to Income Tax
 - o Reporting
 - ☐ Pay slip

- ☐ Bank Schedule
- ☐ Head-wise schedule of pay components
- ☐ PF Schedule
- ☐ Loan Recoveries
- ☐ Interest Statements
- ☐ Annual Earning Statement
 - o employees
- ☐ Cost Center/Company Wise cost report.
- ☐ Comparison of salary with previous month for controls
- ☐ Other reports as needed
 - Modalities for computation of pay revision due on 01.01.2027
 - Loan to Employees - Grant of HBA / Multipurpose/ Other Loans to employees as per SMFCL Rules and Regulations.
 - Development of Report for providing data relating to Actuarial valuation.

4.7.1.2 Income Tax

- ☐ Input of income from payroll and projection for remaining portion of the year.
 - o In case of new joining/retirement/resignation during the year – computation of taxable income for part of the year.
- ☐ On line submission by employees for:
 - o Proposed/actual savings
 - o House rent receipt
 - o Receipt for cash allowances (Conv Reimb/Uniform Reimb etc.).
- ☐ Perquisites on account of subsidized interest loans/leased accommodation.
- ☐ Computation of rebates on account of House Rent Receipt/Conveyance Reimbursement Receipt/Uniform Reimbursement Etc.
- ☐ Computation of relief under section 89(1)
- ☐ Taxable Income, tax due, tax paid and balance tax computation
- ☐ Compute tax to be deducted in current month.
- ☐ Reporting
 - o Income Tax computation statement
 - o Tax due/paid/balance
 - o Quarterly/Annual E-Return/TDS Certificates

4.7.3 Interest computation on employee loans

- ☐ Party Ledger of accounting system contains balances and transactions of employees.
- ☐ Extract data from party ledger is used for computation of accrued interest on employee loans.

-
- ☐ Data extrapolated for remaining period of the financial year based recovery of loan from salary in current month.
 - ☐ Interest computed according to slabs/rates of company rules.
 - ☐ Interest as per Income Tax Rules compute according to prime lending rate of SBI for computation of perquisites on subsidized interest loans
 - ☐ Rebate allowed for Family Planning Incentive
 - ☐ Reporting for
 - o Interest Statement – Employee Wise, Loan Wise for the selected year
 - o Perquisites for subsidized interest loans
 - o Summary of interest
 - ☐ Integration with
 - o Payroll for booking of accrued interest JV on monthly basis
 - o Income Tax for adding perquisites to Taxable Income

4.7.4 Loan Origination System

- a) Application
- b) Validation
- c) Document upload
- d) Fee collection
- e) Backend integrity

4.7.5 Entity Appraisal

a) KYC Module

- a. Module to create master data and uploading KYC in **CKYC Register**
- b. Linking of KYC with master data of loans as well as Resource Module

b) Credit Rating Module

- a. Define Risk Categories and Risk Heads – Project/Sponsor/Finance
- b. Input for various Risk Heads – Project/Sponsor/Financial
- c. Compute Rating/Score of case
- d. Work Flow for approval of rating by concerned HOD and committee
- e. Reporting of rating history

c) Appraisal

4.7.6 Technical/Loan Appraisal

- a) Unique identifier generation
- b) Application processing
- c) Approval
- d) Sanction
- e) Fee collection
- f) Disbursement

4.7.7 Loan Accounting & Management System - Asset

-
- a) Masters for
 - i) Customers
 - ii) Schemes
 - iii) Tranches of loans
 - iv) Applicable interest rate for loans (Floating / Fixed)
 - v) Master interest rate with parameters
 - vi) Master for security creation
 - b) Financial Concurrence
 - c) Disbursement
 - d) Computation to:
 - i) Generate principal repayment schedule
 - ii) Generate Interest payment schedule
 - e) Generate Demand Notice
 - f) Manage Interest Income
 - g) Managing repayment from borrowers
 - h) Restructuring of Loans
 - i) Recoveries
 - i) Generate Monthly principal recoverable list – customer wise
 - ii) Generate Monthly interest recoverable list – customer wise
 - iii) Apportion payments receipts on due amounts
 - j) Delayed payments
 - i) Calculated Delayed Interest/Penal Interest
 - k) Accrued Interest computation
 - l) Tracking of Security submitted by borrower for loan availed.
 - m) Provision for capturing pre-disbursement condition
 - n) Provision for tracking of Penal Interest on Borrower
 - o) Centralized Fee management module

4.7.8 NPA Management

- a) NPA identification
- b) NPA Classification
- c) NPA provisioning
- d) OTS settlement

4.7.9 Legal Module

- a) Documentation
- b) Agreements
- c) Verification of documents
- d) Security creation

4.7.10 Payable Loan Control System - Liabilities

4.7.10.1 Masters for

- i) Agencies
- ii) Schemes
- iii) Tranches of loans
- iv) Applicable interest rate for loans

4.7.10.2 Tools for

- i) Generate principal repayment schedule
- ii) Generate Interest payment schedule

4.7.10.3 Payments

- i) Generate Monthly principal payment list – customer wise
- ii) Generate Monthly interest payment list – customer wise
- iii) Apportion and record actual payments against dues

4.7.10.4 Accrued Interest computation

4.7.11 Asset Liability Management

4.7.11.1 Assets

- i) Interface with ERP for extraction of Data
- ii) Customer Master
- iii) Scheme Master
- iv) Scheme Tranche Data
- v) Disbursements
- vi) Prevailing Interest Rates
- vii) Repayments
- viii) Principal Repayment Schedule
- ix) Interest Recovery Schedule
- x) Reset Details

4.7.11.2 Adjustment of Data extracted from ERP

- i) Scheme Master
- ii) Scheme Tranch Data
- iii) Disbursements
- iv) Prevailing Interest Rates
- v) Repayments
- vi) Principal Repayment Schedule
- vii) Interest Recovery Schedule
- viii) Reset Details

4.7.11.3 Liabilities

-
- i) Data Maintenance
 - ii) Borrowers Master
 - iii) Borrowing Scheme
 - iv) Borrowing Tranches
 - v) Interest Rates
 - vi) Principal Repayment Schedule
 - vii) Interest Computation and Payment Schedule
 - viii) Actual Principal Repayments
 - ix) Actual Interest Payments
 - x) Forex module which includes hedging, swapping facility
 - xi) Management of Bonds (Retail, 54EC etc.)

4.7.11.4 Data Processing

4.7.11.5 Reporting

- i) Liquidity Gap Analysis and Reporting
- ii) Interest Rate Sensitivity Analysis and Reporting
- iii) Short Term Cash – Flow Statement
- iv) Short Tem Dynamic Statement
- v) Net Interest Income / Net Interest Margin Analysis and Reporting.

4.7.11.6 Reports

- i) Duration / Modified Duration Analysis and Reporting.
- ii) Loan Assets/ Other assets Reports – Ability to do analytics and generate various Reports at Account level related to Loan Assets and other Assets / Investments.
- iii) Borrowings / Other Liability Reports – Ability to do analytics and generate various Reports at Account level related to Borrowings and other liabilities.
- iv) Historical Analysis on various parameters related to Loan Assets, Borrowings, Income, Expenses, Profit and Loss account and Balance sheet.
- v) Scenario Analysis / Forecasting / projections on various parameters related to Loan Assets, Borrowings, Income, Expenses, Profit and Loss account and Balance sheet.
- vi) Exception reports.
- vii) MIS reports related to weighted Average cost of Borrowings, Weightage Average Lending Rate and other reports as per the requirement of SMFCL relating to Loan assets, Investments, other assets, Borrowings and other liabilities.
- viii) Others reports as required under RBI Reporting System.

4.7.12 Payable Controls

- ☐ **Bank Guarantee**
 - o Keep record for all bank guarantees submitted to company with details of
 - ☐ Type of BG – Advance/Performance etc.

-
- ☐ BG No
 - ☐ Issuing Bank/Branch
 - ☐ Contact Person of Bank – Phone/Mail. /Name etc.
 - ☐ Party Details
 - ☐ Amount
 - ☐ Validity of BG
 - o Generate confirmation letter to Bank in specified format
 - o On receipt of confirmation from Bank, record in system and mark Bg as “Confirmed”.
 - o Generate alert for expiring BG’s on predefined intervals i.e. 2 weeks before/1 month before etc.
 - o Generate renewal letter of BG to Bank/Party/Concerned Department in specified format.
 - ☐ **Payment petty purchases/small contracts,**
 - o Functionality of processing bills without contract
 - MSME Tagging of parties and generation of reports
 - Related Parties Tagging and reports
 - ☐ **Contract Management Module**
 - Comprehensive module for Contract Management starting from Contract Creation (Including BOQ), generation of bills and processing/payment of same in finance.
 - Vendors to have access to module for viewing of their bills and status thereof

4.7.13 Credit Risk Management

- 4.7.13.1 Credit administration, Measurement & monitoring
- 4.7.13.2 Credit Risk Rating
- 4.7.12.2 Credit Risk Review & control system
- 4.7.13.3 Early warning signal
- 4.7.13.4 Management of stressed assets
- 4.7.13.5 Reporting on Risk Management and classification as Low Risk, Medium Risk & High Risk.

4.7.14 Compliance

- 4.7.14.1 Master for creation of compliances
- 4.7.14.2 Module to capture all compliances from various concerned divisions
- 4.7.14.3 Compliance monitoring & reporting
- 4.7.14.4 Report on various Regulatory compliances.
- 4.7.14.5 Objective is to capture and automate all compliance processes

4.7.15 Dashboard (organization-wide covering all modules)

- 4.7.15.1 Data collection
- 4.7.15.2 Data consolidation
- 4.7.15.3 Data visualization including drill-down, slicing & graphical representation
- 4.7.15.4 Display summarized information
- 4.7.15.5 Predictive analysis
- 4.7.15.6 Borrower history and time of repayments due from different borrowers.
- 4.7.15.7 Lender history and time of repayment to different lenders.
- 4.7.15.8 Bank balances and real time status etc.
- 4.7.15.9 Dash Board for senior management – multiple layers showing key summarized Information of various aspects.
- 4.7.15.10 Dashboard shall have drill down facility up to the lowest detail

4.7.16 Vendor portal

- 4.7.16.1 Vendor Registration and Authentication
- 4.7.16.2 Order & Invoice management
- 4.7.16.3 Access Management
- 4.7.16.4 Integration to GeM portal
- 4.7.16.5 Reporting
- 4.7.16.6 Capturing MSME details.
- 4.7.16.7 Objective is to capture & automate all interactions/transactions with Vendors through this portal

4.7.17 Customer Portal

- 4.7.17.1 Borrower registration and authentication
- 4.7.17.2 Integration to Loan Original System
- 4.7.17.3 360-degree view of borrower account & reports
- 4.7.17.4 Communication & support
- 4.7.17.5 Objective is to capture & automate all interactions/transactions with customers/borrowers through this portal

4.7.18 Inventory Management

- 4.7.18.1 Creation of inventor
- 4.7.18.2 Stock management
- 4.7.18.3 Integration with procurement (desirable)
- 4.7.18.4 Reporting

4.7.19 Grievance Module

- 4.7.19.1 Capture grievance on-line from all stakeholders
- 4.7.19.2 Provision to enter grievance detail received from other sources
- 4.7.19.3 Grievance resolution matrix
- 4.7.19.4 Entire workflow of resolution
- 4.7.19.5 Workflow of escalation
- 4.7.19.6 Related reports

4.7.20 Other Reports/MIS

- 4.7.20.1 Creation of a Report/MIS server and provision to generate reports from that service
- 4.7.20.2 Data migration for data provided in excel and migration report
- 4.7.20.3 Other MIS Reports/feature modification as required for NBFC Accounting / RBI Reporting/SEBI Reporting etc. shall be done by the ERPSI at free of cost from time to time during the contract and AMC period.

4.7.20.4 It is estimated to have a total 200 reports to be developed in the ERP system as part of development & implementation. More report requirements will be met as part of support and maintenance. This does not include the adhoc report requirements.

4.7.20.5 There will be provision to generated reports and export the same in formats such as 'Excel' and '.pdf' format as required by various stakeholders. All reports should support filtering based on parameters such as Date, Status, Loan Type, Customer Category and other business-defined criteria.

4.7.21 Website

4.7.21.1 A new website should be developed ensuring proper security controls to protect against hacking attempts, including secure authentication, data encryption, and regular vulnerability assessments.

4.7.21.2 Technical Requirements of the Web Hosting server

The website of SMFCL may require the following tentative infrastructure for hosting:

RAM (IN GB)	16 GB
VCPU	8 vCPU
Types of Server(s)	As per ERPSI
Usages Types (Primary / DR)	Primary
Storage (In GB)	100 GB
Type of Storage Media/Drive	SSD
System Software / DB	As per ERPSI
Operating System.	As per ERPSI
Tier of the Data Centre	III or above
Deployment Model.	GCC or Meity Empaneled cloud
Web Server	IIS 10 or above
Connectivity	For accessing the website through internet with sufficient bandwidth

This requirement is for both the Primary Hosting centre and also the Disaster/Standby centre.

4.7.21.3 Other requirements:

- i. The offer should be from a Meity empaneled Cloud service provider
- ii. Hosting of the SMFCL corporate website in the shared public cloud with Windows latest version and Data Base. Both the Windows & database servers along with required licenses are to be supplied by the bidder.
- iii. Establish & Configuration of required resources including VMs, web servers, storage, network, security etc.
- iv. Facilitate installation, configuration of the website, Database and the Content Management System.
- v. Automated backup of the website and data, as per defined frequency. SMFCL will download the same into its on-premises Data center to establish standby provision.
- vi. Conducting Live drill of the Website as per defined frequency. Seamless switch over from the **PDC to DRC** within defined RPO & RTO, in case of any disaster.
- vii. The proposed solution will include 24x7 NMS & SOC support.
- viii. The proposed Data Centers should be IPv6 compliance.

-
- ix. The proposed solution should ensure high availability (redundancy), Security & Performance for running the website.
 - x. The bidder will share the certificate updates, periodical security audit and closure report for the set-up to SMFCL by Cert-In empaneled audit agencies.
 - xi. In addition to the set-up mentioned above, the offer should include the following:
 - Shared firewall, web Application Firewall, **load balancers**, IPS/IDS etc.
 - DDoS protection
 - Access control, domain set-up & DNS service integration
 - Logging and Alert mechanism
 - Compliance to SLA parameters as mentioned in this bid document
 - Enable HTTPS with SSL/TLS certificates
 - Regular patching and updation of the platform provided
 - xii. Deliverables
 - Fully functional and accessible corporate website on the cloud
 - Licenses required for running the cloud
 - Documentation of infrastructure architecture along with configuration
 - Access credentials and administrative rights
 - Monthly performance, availability and security reports
 - Certification documents updated from time to time
 - Backup of data & application as per defined frequency
 - Audit and closure reports
 - Live DR Drill reports
 - Unplanned outages and incidence report

4.7.21.4 Terms and Conditions

- **SMFCL shall get the security audit/certification done, for its website, from an audit/certification agency** and the CSP shall provide any required information and assistance for the same. In addition, if there is any observation related to the web-hosted infrastructure, the CSP shall submit a closure report within reasonable timeframe.
- CSP shall Implement necessary security features such as firewall **including Web Application Firewall, antivirus, anti-ransomware, anti-malware, load balancer, access & identity management, and DDOS protection.**
- CSP shall Notify SMFCL promptly in case of security incidents or foreign government access requests.
- CSP shall Monitor application performance, hardware performance, and bandwidth usage, taking remedial measures as needed.
- Bidder shall provide SMFCL with the right to conduct audits whether by its internal or external auditors, or by external specialists appointed to act on its behalf and to obtain copies of any audit or review reports and findings made on bidder in conjunction with the services performed for SMFCL.
- The offered solution shall be compliant to the requirement of hosting the Government website as per the guidelines issued by the Government of India, a self-declaration in this regard may be provided with the bid.
- The Website/services of SMFCL shall be hosted on the server located in India only and preferably in NCR, Delhi CSP shall provide the server location details and proposed server configuration for SMFCL with the bid.

-
- The Third-Party Security Audit/certification details of the server from Government approved agencies shall be submitted by the CSP with its bid.
 - Bidder shall ensure that SMFCL has the right to access all books, records and information relevant to the activity available with them.
 - The offered Services are located in India and there will be no movement of data of SMFCL to outside India

SECTION-V ELIGIBILITY AND QUALIFICATION REQUIREMENTS

- 5.1 A Bid can be submitted by a Bidder as an individual entity who are eligible to participate in tenders for public procurement in India in accordance with Applicable Laws including the guidelines issued in Order No. F/No.6/18/2019-PPD by Ministry of Finance, Department of Expenditure, Public Procurement Division dated 23 July 2020, Order No No.9/16/2016-Trans-Part (2) dated 18 November 2020, latest Government of India Guidelines for Make in India, Domestically manufactured products, Atmanirbhar Bharat and circulars DIPP Office Memorandum No. P-45021/2/2017-PP (BE-II) date: 16th Sept. 2020, MeitY Circular No.1(10)/2017-CLES dated 06.12.2019 and Order No. 11/05/2018-Coord. by the Ministry of Power dated 17 September 2020 including any amendments or modifications to the same from time to time. Any subsequent release of order by any ministry related to areas mentioned in this clause will also automatically becomes part of this clause.
- 5.2 If at any stage of the bidding, any order/ ruling is found to have been passed in the last 3 (three) year preceding the Bid submission deadline by a competent Court of Law or any appropriate Commission or any Arbitral Tribunal against the Sole Bidder or its Affiliates for breach of any Contract awarded by any Government agency/department, then Bids from such Bidders shall be liable to be rejected. All Bidders shall confirm in accordance to Form 12 given in Section VII that no such order(s)/ ruling(s) have been passed by a competent Court of Law or an appropriate Commission against it or its Affiliates. In case of any such order/ ruling, it is the duty of the Bidder to inform SMFC LTD for the same during the Bid submission
- 5.3 Technically qualified Bidders shall continue to maintain compliance with the Eligibility and Qualification Requirements specified herein. Failure to comply with the aforesaid requirements shall make the Bid from such Bidders liable for rejection at any stage of the bidding process.
- 5.4 The bidder shall submit the Bid after submitting the Bid Security as per the various terms, schedules and formats prescribed in this RFP. Further, the bidder shall be the Single point of contact during the Bid process during entire of the contract.
- 5.4.1 Bidders must ensure compliance to the prevailing GFR issued by Govt of India.
- 5.4.2 The successful bidder shall not be allowed to sub-contract works to any contractor from a country which shares a land border with India unless such contractor registered with the Competent Authority.
- 5.5 Responsiveness of Bid

5.5.1 The bid shall be checked for their responsiveness before evaluation of technical and financial requirements of qualification. The bid shall be declared non-responsive if they are not supported with

- Bid Security Declaration
- Pre contract integrity pact

5.5.2 The non responsive bid shall not be evaluated further processing.

5.6 Pre-Qualification Requirements

5.5.1 The technical and financial requirements of qualification for the System Implementer (SI) are as follows:

The prospective Bidder (referred to as ERPSI) shall have to enclose all documentary evidence in support of pre-qualification/ qualification criteria.

Sr No	Requirements	Supporting Documents
1	GENERAL	
1.1	The Bidder should be CPSE/PSU/Govt Bodies.	Copy of the following documents needs to be submitted along with the bid: Certificate of Incorporation/ Registration Certificate PAN, GST Certificate & Documentary proof
1.2	The bidder should have at-least any one of the following valid certifications as on the last date of bid submission: 1. CMM/CMMI level 3 or above 2. IEC/ ISO 27001:2022 certification 3. ISO 9001:2015 certification	Copy of certification from authorized certification body valid as on date

Sr No	Requirements	Supporting Documents
1.3	The bidder should not be blacklisted or debarred by any govt. organization or public sector organisation as on the date of submission of bid.	Self-declaration on non-Judicial stamp paper of Rs. 100/-
1.4	The bidder must have at least 10 full time developer resources on its payroll out of which at least 5 full time resources in the mandatory module (F&A, LMS, HR) as on last date of submission of bid.	Separate letter by HR dept.(authenticated by authorised signatory) to be submitted for full-time professionals in each category.
		Work Orders/Completion Certificate
1.5	Bidder should have a functional office in Delhi/NCR	Address proof and letter of HR
2	FINANCIAL	
2.1	The bidders should have at least an average annual turnover of Rs 500 Cr. (Rupees Five Hundred crore only) per year during last three years, ending 31st March of the previous financial year i.e., FY: 2024-25, 2023-24, 2022-23, The turnover refers to the individual Bidder and not the composite turnover of its affiliates, subsidiaries / sister concerns or parent company(ies) etc.	Copy of Annual Audited Financial Statements or Certificate by chartered Accountant with specific mentioning that the turnover so certified is based on the audited accounts of the company/firm incl. LLP
2.2	Positive Net-Worth for each of last three Audited Financial Years.	Copy of Annual Audited Financial Statements or Certificate by chartered Accountant with specific mentioning that the net-worth so certified is based on the

Sr No	Requirements	Supporting Documents
		audited accounts of the company/ firm incl. LLP
3	CREDENTIALS AND EXPERIENCE	
3.1	The Bidder should have developed and implemented web-based applications in least 4 Govt owned entities (Central/State) (PSUs/ NBFCs like PFC/REC/HUDCO/IREDA etc.)	Bidder should submit Copy of Work order/Contract/LoA (Mandatory) & Any one document out of the following: Payment receipts duly certified by CA Proof of release of performance security after completion of the contract Proof of settlement/release of final payment against the contract Certificate of Go-Live / Certification for project being operational as on date of Bid Submission / Completion Certificate as proof of services provided (<i>*Operational Projects only include projects where Go-Live is declared and FMS is ongoing</i>) <i>*Completion Certificate is issued after the Go-Live and FMS period is over)</i>
3.2	The bidder should have developed and implemented at least 5 enterprise-wide integrated applications/modules out of the following proposed ERP modules: 1. Finance & Accounting 2. Technical Appraisal 3. Loan Accounting & Management 4. Loan application system	Documents required: Copy of Work order/contract/LoA (Mandatory) & Any document out of the following: • Payment receipts duly certified by CA • Proof of release of performance security after completion of the contract

Sr No	Requirements	Supporting Documents
	5. Investment/Resource Management 6. HR 7. Payroll 8. ESS 9. Compliance 10. Credit Risk Management 11. NPA Management 12. Customer Portal	• Proof of settlement/release of final payment against the contract • Certificate of Go-Live / Certification for project being operational as on date of Bid Submission • Completion Certificate as proof of services provided (<i>*Operational Projects only include projects where Go-Live is declared and FMS is ongoing</i>) • <i>*Completion Certificate is issued after the Go-Live and FMS period is over)</i>
3.3	The bidder should have developed, implemented and maintained at least 2 enterprise-wide open sourced integrated applications/modules	Documents required: Copy of Work order/Agreement/LoA (Mandatory) & Any one document out of the following: • Payment receipts duly certified by CA • Proof of release of performance security after completion of the contract • Proof of settlement/release of final payment against the contract • Certificate of Go-Live / Certification for project being operational as on date of Bid Submission • Completion Certificate as proof of services provided (<i>*Operational Projects only include projects where Go-Live is declared and FMS is ongoing</i>) • <i>*Completion Certificate is issued after the Go-Live and FMS period is over)</i>

SECTION-VI BID EVALUATION METHODOLOGY

6.1 Bid Evaluation

First Stage (Pre-Qualification (PQC) & Technical Bid Evaluation):

- 6.1.1. The *Pre-qualification bid* will be evaluated first as per the PQC criteria mentioned in Section V. *Technical evaluation* will then take place only for those bids qualified in the PQC evaluation criteria. Bids scored the minimum cut-off marks specified will qualify for the 2nd stage of bid evaluation.
- 6.1.2 Technical Bid evaluation will be done according to the table below. Bidder(s) obtaining 60 marks or above will be considered as technically qualified bidders and shall be eligible to participate in the next phase:

		Maximum Marks 100	
Sr No	Parameters / Documents required		Marks
1.		Maximum	10
	The bidder must be an Indian firm/LLPs/ organization/company for providing similar solutions/services under the Indian Laws and should have a valid registered office in India with a valid GST Registration as on the date of RFP. Company Incorporation / Registration Certificate.	4 to 7 years	5
		7 years to 10 years	7
		More than 10 years	10
2.		Maximum	15
	The Bidder should have developed and implemented web-based applications in CPSUs / NBFCs / Government (Central/State)/ Listed Financial Institutions in India. Copies of work orders/contracts/ Certificate from Client.	No. of installations < 3	7
		No of installations between 3 and 5.	12
		No of installations more than 5	15
3.		Maximum	15
	The bidder should have implemented/developed/ supported web	No. of Implementations < 3	7

	application for Banking/NBFC	No. of implementations between 3 to 5	10
	Copies of work orders/contracts/ Certificate from Client.	No. of implementations > 5	15
4.		Maximum	20
	The bidder has experience of developing functional modules/applications given below:	More than 1 and up to 3 modules / applications per list	5
	1. Finance & Accounting	More than 3 and up to 5 modules / applications as per list	10
	2. Loan Accounting & Management		
	3. Loan Origination System	More than 5 and up to 7 modules / applications as per list	15
	4. ALM		
	5. HRMS		
	6. Credit Risk Management	More than 7 modules / applications as per list	20
	7. Dashboard		
	8. NPA Management		
	9. Customer Portal		
	Copies of work orders/contracts/ Certificate from Client.		
5.		Maximum	10
	The Bidder have experience of either develop / implement /support Loan Accounting Module/system in NBFC/Banks	At least one project	10
	Copies of work orders/contracts/ Certificate from Client.		
6.		Maximum	15
	The Bidder have experience of either develop / implement /support IT application using open source platform in NBFC/Banking/Listed FI	> 1 and <= 3 Projects	5
	Copies of work orders/contracts/ Certificate from Client.	> 3 and <=5 projects	10
		> 5 projects	15
7.		Maximum	15

	Demonstration & Presentation	Demonstration of business-critical processes, open source technology stack and capability to cater to scope of work	15
	TOTAL		100

*Bidder has to score at least 60 marks in First Stage evaluation to qualify for opening of financial bid. Marks obtained by a Bidder as per above table will be the **Technical Score** of that Bid.*

6.1.3 Second stage (Financial or Commercial Bid Evaluation): Financial bid of only technically qualified bidders (First stage) will be opened and the selection be based on QCBS method mentioned herein:

6.1.4 Bidder has to score a minimum of 60 marks in the Technical Evaluation to qualify for opening of financial bid. Subsequent to the financial bid opening, Financial score of the bidder shall be calculated as per the formula given below:

6.1.4.1 Lowest financial bid (L1) will get 100 marks as financial score

6.1.4.2 Commercial Score of a Bidder = {Lowest quote / Bidder's quote} x 100

6.1.4.3 Final score calculation through QCBS method as follows:

The final score will be calculated through Quality and Cost based selection method with the following weightage:

Technical weightage: 70%

Commercial weightage: 30%

Final Score of a bidder = (0.70*Technical Score) + (0.30* Commercial Score)

Bidder who will score the highest mark (H1) in this evaluation process will be selected as the finally selected bidder.

Arithmetic errors in the bid, if any, shall be treated as follows:

6.1.4.4 Wherever there is a discrepancy between the amounts in figures and in words, the amount quoted in words shall govern;

6.1.4.5 Where there is a discrepancy between the unit rate and the line-item total resulting from multiplying the unit rate by the quantity, the unit rate will govern, unless, in the opinion of the company, there is obviously a gross error such as a misplacement of a decimal point, in which case the line-item total will govern.

6.1.4.6 Where there is a discrepancy between the total amount obtained as per the amount quoted as the GeM commercial bid (QP) and the total price obtained as per the uploaded customized price (CP) break-up pdf file, the amount (QP) quoted in the commercial bid will govern and shall be treated as the final price bid. In such case and if the bidder

happens to be the H1 bidder as per the evaluation process mentioned above, then the bidder shall resubmit the customized price pdf file so that the derived total (CP) matches with the final price bid (QP) quoted by the bidder.

6.1.4.7 Bidder shall quote their rates/prices in Indian Rupees only for entire scope of work as per Price Schedule including that in Format – 2 of Section VIII of this tender document. The bid shall be uploaded on GeM portal as per methodology mentioned in Annexure -I of Section II.

6.1.4.8 SMFC LTD will open the financial bids of only those bidders, who have been found to be eligible/qualified as per the Pre-Qualification Criteria as well as technically qualified as per the technical evaluation criteria mentioned in this RFP document.

6.1.4.9 The qualified Financial Bids shall be opened in virtual presence of their representatives, who choose to be present, on a specified date and time.

6.1.4.10 The date, time of opening of financial bids shall be informed to the technically qualified bidder only.

6.1.5 **Third Stage** – Award of project to the H1 bidder who scored the highest mark and following the mitigation processes described in case of a tie, as well as discrepancy in the figures, if required, in the evaluation process.

6.4.5.1 Award of Contract

SMFC LTD will award the contract to the bidder whose bid has been determined to be in full conformity to the bid documents and has been selected as successful bidder as per QCBS computation defined herein.

6.2 Make in India

Preference as per Public Procurement Policy of Govt of India on MSME, The Department for Promotion of Industry and Internal Trade has issued the revised 'Public Procurement' (Preference to "Make in India"), Order 2017 dated 16.09.2020, etc., as amended from time to time and applicable shall be extended. PREFERENCE TO MAKE IN INDIA AND GRANTING OF PURCHASE PREFERENCE TO LOCAL SUPPLIERS.

Purchase preference shall be given to local suppliers as per methodology specified MoP Letter No A-1/2021-FSC-Part (5). Dated 16.11.2021. Further, the detailed methodology is mentioned in Annexure-A to Section VI.

SI shall provide a certificate from statutory auditor or cost auditor of the company (in the case of companies) or from a practicing cost accountant or practicing chartered accountant (in respect of suppliers other than companies) giving the percentage of Local Content to be eligible as Class-I or Class-II in line with the Public Procurement (Preference to Make in India) to provide for Purchase Preference (linked

with local content) in respect of Power Sector' order dated 28.07.2020, 16.09.2020 and subsequent amendments issued by Ministry of Power and MeitY notification (F.No. W-43/4/2019-IPHW-MeitY) dated 07.09.2020. Cloud services being provided from Data Centers located in India will be treated as local services for purpose of Minimum Local Content. The above requirements for PPP-MII compliance to be ensured by the SI while submitting the certificate to be eligible as Class-I /Class-II supplier as per PPP-MII guidelines

6.3 Notification of Award

Prior to the expiration of the period of bid validity, the SMFCL will notify the successful Bidder in writing, that its bid has been accepted. The notification of award will also constitute the formation of the contract.

6.4 Extension of Bid validity

If necessitated for un-avoidable reasons, the SMFCL may ask the bidders for extension of the bid validity period. On receiving the request, bidders shall extend the Bid validity period up to a maximum period of 90 days.

6.5 Signing of the Contract Agreement

At the same time as SMFCL notifies the successful Bidder that its bid has been accepted, SMFCL, in consultation with the successful Bidder, will prepare the Contract Agreement including NDA, based on the Bidding Documents, incorporating all agreements between the parties.

The Contract Agreement shall be prepared within thirty (30) days of the Notification of Award and the successful Bidder and SMFCL shall sign and date the Contract Agreement immediately thereafter.

6.6 Performance Security

Total 2 Performance securities will be submitted by the selected bidder in 2 phases, viz

6.6.1 First phase for the period starts from date of issuance of work order up to completion of warranty period, The value of Performance security in this phase will be equivalent to 10% of the sum total of amounts quoted at Serial 1-3 of Format 2 of Section VIII-Financial proposal. Validity period of this Security will be up to 6 months of completion of Warranty period (2 years 9 months).

6.6.2 2nd phase, from commencement of AMC period till end of AMC period. The value of the Performance Security in this phase will be equivalent to 10% of the sum total of the amounts quoted at Serial 4-8 of Format 2, Section VIII-Financial proposal. Validity

period of this Security will be up to 6 months of completion of AMC period (5 years 6 months)

6.6.3 The Performance Securities shall be deposited by the selected agency in the form of Bank Guarantees from a scheduled Commercial Bank on non-judicial stamp papers of appropriate value mentioned above in the prescribed format provided in Section-VII, for satisfactory work performance before 15 days of commencement of AMC period. The Performance Security is to remain valid for entire AMC Contract period plus six months. EMD of the selected agency shall be released after submission of Phase 1 Performance security.

6.6.4 The Performance Security submitted in Phase 1 will be released on submission of Performance Security for Phase 2 and completion of Phase 1. Performance Security of Phase 2 will be released on expiry of the Security. There will be no interest accrual of the securities.

6.6.5 Failure of the selected agency to comply with the requirements of bid documents shall constitute sufficient grounds for the annulment of the award and forfeiture of the bid security, in which event SMFC LTD may make the award to the next lowest evaluated Bidder or call for new bids.

6.6.6 Any payments shall be made to the Bidder only after receipt of relevant Performance Security by SMFC LTD. Upon Termination of the Contract due to SMFC LTD Event of default as detailed in GCC or expiry of the Contract Period, the Performance Security shall be discharged by SMFC LTD without any interest and returned to the Bidder not later than 14 (fourteen) working days following the date of Termination of the Contract. Upon Termination of the Contract due to Bidder Event of default as detailed in GCC, the Performance Security shall be forfeited by SMFC LTD.

During the period of contract up to completion/termination and thereafter, all data, metadata, configurations, audit logs, and backups shall remain exclusive property of SMFC Ltd. Bidder shall ensure unrestricted access and provide complete data export in open formats (CSV/XML/JSON) during and after the contract period.

6.6.7 In case of any delay by the bidder in performing the activities of the scope of work with respect to the Project Implementation Schedule, then upon SMFC LTD's request, the bidder shall extend the validity of the separate Performance Security for the period for which the Contract is extended. In the event delay is solely due to acts and/ or omission of the SMFC LTD cost of extending the validity of separate Performance Security shall be reimbursed to the bidder by the SMFC LTD.

6.7 Effectiveness of Contract

The Contract shall be considered as having come into force from the date of the Notification of Award unless otherwise provided in the Notification of Award.

Annexure-A: Purchase Preference to Make in India

Preference for Non-Divisible Contracts for procurement of goods/services/works from ‘Class –I local suppliers’ under Public Procurement (Preference to Make in India) Order, 2017

In line with Public Procurement (Preference to Make in India) Order, 2017 issued by Department for promotion of Industry and Internal Trade (DPIIT), Ministry of Commerce and Industry, Government of India vide order dated 15/06/2017, its revision dated **16/09/2020** (PPP-MII Order),

#‘Public Procurement (Preference to Make in India) to provide for Purchase Preference (linked with local content) in respect of Power Sector’ order dated 28/07/2020 issued by Ministry of Power (MoP Order)

Or

Public Procurement (Preference to Make in India) Order, 2017- Notification of Telecom products, Services or Works issued by Department of Telecommunications (DoT), Ministry of Communications, Government of India, vide Notification dated 29.08.2018 (DoT Order)

Or

[Public Procurement (Preference to Make in India) Order related any other Order issued by a Nodal Ministry which is applicable to the procurement]

[# Choose as applicable while preparing bidding documents/amendments]

and any subsequent modifications/Amendments, if any, ‘Class –I local suppliers’ shall be eligible for purchase preference as follows:

(i) For the purpose of purchase preference under the PPP-MII Order

‘Local Content’ means the amount of value added in India which shall be the total value of the item procured (excluding net domestic indirect taxes) minus the value of imported content in the item (including all customs duties) as a proportion of the total value, in percent.

‘Class –I local supplier’ means a supplier or service provider, whose goods, services or works offered for procurement, meets the minimum local content as prescribed for ‘Class-I local supplier.’ Presently, the local content requirement to categorize a supplier as ‘Class-I local supplier’ is minimum 50%*.

‘Class-II local supplier’ means a supplier or service provider, whose goods, services or works offered for procurement meets the minimum local content as prescribed for ‘Class- II local supplier’ but less

than that prescribed for 'Class-I local supplier.' Presently, for 'Class-II local supplier,' the 'local content' requirement is minimum 20%*.

[The Minimum Local Content percentage for Class-I and Class-II Local Suppliers to be suitably incorporated in line with directions issued by the Nodal Ministries in this regard. This note may be removed while issuing RFB documents]*

'Margin of Purchase Preference' means the maximum extent to which the price quoted by a 'Class – I local supplier' may be above the X1 for the purpose of purchase preference. Presently, this margin shall be 20%.

(ii) If L1 bid is from a 'Class –I local supplier', the contract will be awarded to L1.

(iii) If L1 bid is not from a 'Class –I local supplier', the lowest evaluated bidder among the 'Class –I local suppliers' will be invited to match the L1 price subject to 'Class –I local supplier's' Evaluated Bid Price falling within the Margin of Purchase Preference i.e. +20% of X1 and the contract shall be awarded to such 'Class –I local supplier' subject to matching the L1 price.

(iv) In case such lowest eligible 'Class –I local supplier' fails to match the L1 price, the eligible 'Class –I local supplier' with the next higher bid within the Margin of Purchase Preference as brought at (iii) above, shall be invited to match the L1 price, and so on, and the contract shall be awarded accordingly.

–

For the purpose of iii and iv above, the order in which the 'Class –I local supplier' shall be given an opportunity to match L1 price will be in the order of their rank (lowest evaluated price first) determined as follows:

(v) In case none of the 'Class –I local supplier' within the Margin of Purchase Preference matches the L1 price, then the contract shall be awarded to the L1 bidder.

(vi) 'Class-II Local supplier will not get purchase preference.

(vii) The 'Class –I local supplier'/'Class-II Local supplier' shall give a self-certification in his bid in the given format, indicating the percentage of Local Content and certifying that the item offered meets the Local Content requirement for 'Class –I local supplier'/'Class-II Local supplier', as the case may be and shall give details of the location(s) at which value addition is made. Further, in case of packages above Rs. 10 Cr, the 'Class –I local supplier'/'Class-II Local supplier' shall provide a certificate from statutory auditor or cost auditor of the company (in the case of companies) or from a practicing cost accountant or practicing chartered accountant (in respect of suppliers other than companies) giving the percentage of Local Content. False declaration regarding Local Content by the bidder shall be a transgression of Integrity Pact and action shall be taken in line with provisions of the Integrity pact and in line with the provisions of the subject Order

SECTION-VII BIDDING FORMS- TECHNICAL PROPOSAL

7.1 Checklist of Required Forms

This Checklist shall be filled in and submitted by the bidder along with the Technical Bid. Except Form 1 given in Section VIII (to be completed and submitted by the Bidder in the Financial Bid) all other documents/ forms duly filled and complete in all respect are to be submitted by the Bidder in the Technical Bid.

S. No.	Document	Attached? (Yes/ No)	For Official Use
1.	Form 1: Eligibility Criteria Compliance		
2.	Form 2: Technical Bid Compliance		
3.	Form 3: List of SI Representative and Key personnel		
4.	Form 4: Bid Annexure		
5.	Form 5: Bidder Information		
6.	Form 6: Project Implementation Plan		
7.	Form 7: Resume and Declaration		
8.	Form 8: Format for Performance Security (Bank Guarantee)		
9.	Form 9: Format of Covering Letter by Sole Bidder for Submission of Bid		
10.	Form 10: Format of Power of Attorney by Bidder authorizing an Individual Designated Representative for this bid		
11.	Form 11: Format of undertaking on compliance of tender requirements along with terms and conditions		
12.	Form 12: Format for undertaking towards not being blacklisted		
13.	Form 13: Record of Similar Work Done		
14.	Form 14: Pre-Contract Integrity Pact		
15.	Form 15: Format of summary of audited financial statements		
16.	Form 16: Table of Compliance		
17.	Form 17: Change Request Form		
18.	Form-18 - List of Software		
19.	Form-19 – Undertaking related to ESG		

Form 1: Eligibility Criteria Compliance

Sr No	Requirements	Supporting Documents	Page Number	Fill Details and submit documentary evidence
1.	GENERAL			
1.1	The Bidder should be CPSE/PSU/Govt Bodies.	Copy of the following documents needs to submit along with the bid: Certificate of Incorporation/ Registration Certificate PAN Card GST Certificate & Documentary proof.		
1.2	The bidder should have at-least any one of the following valid certifications as on the last date of bid submission: 1. CMM/CMMI level 3 or above 2. IEC/ ISO 27001:2022 certification 3. ISO 9001:2015 certification	Copy of certification from authorized certification body valid as on date		
1.3	The bidder should not be blacklisted or debarred by any govt. organization or public sector organisation as on the date of submission of bid.	Self-declaration on non-Judicial stamp paper of Rs. 100/-		
1.4	The bidder must have at least 10 full time developer resources on it's payroll out of	Separate letter by HR dept. to be submitted for full-time		

Sr No	Requirements	Supporting Documents	Page Number	Fill Details and submit documentary evidence
1.	GENERAL			
	which at least 5 full time resources in the mandatory module (HR, LMS, F&A) as on last date of submission of bid.	professionals in each category.		
1.5	Bidder should have a functional office in Delhi/NCR	Address proof and letter of HR		
2	FINANCIAL			
2.1	The bidders should have at least an average annual turnover of Rs 1 Cr. (Rupees One core only) per year during the last three years, ending 31st March of the previous financial year i.e., FY: 2024-25, 2023-24, 2022-23. The turnover refers to the individual Bidder and not the composite turnover of its affiliates, subsidiaries / sister concerns or parent company(ies) etc.	Copy of Annual Audited Financial Statements or Certificate by chartered Accountant with specific mentioning that the turnover so certified is based on the audited accounts of the company/firm incl. LLP		
2.2	Positive Net-Worth for the each of last three Audited Financial Years.	Copy of Annual Audited Financial Statements or Certificate by chartered Accountant with specific mentioning that the net-worth so certified is based on the audited accounts of		

Sr No	Requirements	Supporting Documents	Page Number	Fill Details and submit documentary evidence
1.	GENERAL			
		the company/ firm incl. LLP		
3	CREDENTIALS AND EXPERIENCE			
3.1	The Bidder should have developed and implemented web-based applications in at least 4 Govt owned (Central/State) PSUs/ NBFCs.	Bidder should submit Copy of Work order/LoA (Mandatory) & Any document out of the following: Payment receipts duly certified by CA Proof of release of performance security after completion of the contract Proof of settlement/release of final payment against the contract Certificate of Go-Live / Certification for project being operational as on date of Bid Submission / Completion Certificate as proof of services provided <i>(*Operational Projects only</i>		

Sr No	Requirements	Supporting Documents	Page Number	Fill Details and submit documentary evidence
1.	GENERAL			
		<i>include projects where Go-Live is declared and FMS is ongoing</i> <i>*Completion Certificate is issued after the Go-Live and FMS period is over)</i>		
3.2	The bidder should have successfully developed and implemented at least 5 enterprise-wide integrated applications/modules out of the following proposed ERP module: 1. Finance & Accounting 2. Technical Appraisal 3. Loan Accounting & Management 4. Loan application system 5. Investment/Resource Management 6. HR 7. Payroll 8. ESS 9. Compliance 10. Credit Risk Management 11. NPA Management 12. Customer Portal	• Necessary Purchase order/LOI/Contract/Certification on client letterhead/Completion certificate/certification for project being operational as on date of Bid as proof of services provided • Certificate of Go-Live / Completion Certificate/ Certification for project being operational as on date of Bid Submission as proof of services provided <i>(*Operational Projects only include projects where Go-Live is declared and FMS is ongoing</i>	•	•

Sr No	Requirements	Supporting Documents	Page Number	Fill Details and submit documentary evidence
1.	GENERAL			
		<i>*Completion Certificate is issued after the Go-Live and FMS period is over)</i>		
3.3	The bidder should have developed, implemented and maintained at least 2 enterprise-wide open sourced integrated applications/modules	Documents required: Copy of Work order/Agreement/LoA (Mandatory) & Any one document out of the following: • Payment receipts duly certified by CA • Proof of release of performance security after completion of the contract • Proof of settlement/release of final payment against the contract • Certificate of Go-Live / Certification for project being operational as on date of Bid Submission • Completion Certificate as proof of services		

Sr No	Requirements	Supporting Documents	Page Numb er	Fill Details and submit documentary evidence
1.	GENERAL			
		provided (<i>*Operational Projects only include projects where Go-Live is declared and FMS is ongoing</i>) <i>*Completion Certificate is issued after the Go-Live and FMS period is over)</i>		

Form 2 : Technical Bid compliance

Sl No	Category	Unit	Value
1	The bidder must be an Indian firm/LLPs/ organization/company for providing similar solutions/services under the Indian Laws and should have a valid registered office in India with a valid GST Registration. Bidder must be operational for at least 10 years as on the date of RFP.	No Of Years	
2	The Bidder should have developed and implemented applications in CPSUs NBFCs.	No of CPSUs/NBFCs	
3	The bidder should have implemented/ developed/ supported web applications for Banking/ NBFC/ Listed FI	No of implementations	
4.	The bidder has experience of developing functional modules/applications given out off below: 1. Finance & Accounting 2. Entity Appraisal 3. Technical Appraisal 4. Loan Accounting & Management 5. Loan Origination System 6. Investment/Resource Management 7. ALM 8. HR 9. Payroll 10. ESS 11. Compliance 12. Dashboard 13. Credit Risk Management 14. NPA Management 15. Customer Portal 16. Vendor portal 17. Inventory 18. Website Creation	No of modules	
5	Bidder have developed/implemented/supported Loan Accounting Module in NBFCs/Listed FI	No of Implementations	

5	Bidder have developed/implemented/supported Open Source software in NBFCS/Listed FI	No of Implementations	
---	---	-----------------------	--

Form 3: List of SI Representative and Key personnel

Form 4: Bid Annexure**(BOTH - ONLINE and HARDCOPY)**

(To be submitted on the firm's letter head and signed by an authorized person - Documentary proof authorizing the person by the bidder to be attached)

To

Mr. _____,

Sagarmala Finance Corporation Limited,
Western Wing, 1st Floor, Thapar House,
Janpath, New Delhi-110001.

Ref: Bid Document No.

Dated:

Sir/ Ma'am,

Having examined the bid documents, the receipt of which is hereby duly acknowledged, I/We, the undersigned is deemed to have accepted the same without any violations and/or deviations etc. pertaining to the tender scope, validity of quoted rates in line & pursuance to the schedule of requirements & all terms & conditions of the tender and in conformity with the said bidding documents.

We undertake, if our bid is accepted, to deliver the entire scope of work in accordance with the delivery schedule specified in the tender/Bid/RFP etc. documents.

If our bid is selected as successful bid, we will submit the required Performance Bank Guarantees/Securities (PBG), as per the Annexure prescribed by SMFC LTD as per the tender terms and conditions.

The same will also be treated as security deposits in case of defaults like non-delivery, cancellation, liquidated damages, penalties etc. valid during the entire period of contract plus three months.

We agree to abide by this bid for a period of 180 Days after the date fixed for opening and it shall remain binding upon us and may be accepted at any time before the expiration of that period. I/We undertake that on completion of the validity period, unless the I/We withdraw

my/our bid in writing by giving a notice of seven working days, it will be deemed to be valid until such time that I/we really withdraw my/our bid.

Herein, we declare:

1. That we have a team of technically qualified officials and have state-of-the-art infrastructure, and that our office premises are equipped with all the facilities specified in the document.
2. We hereby offer to supply the Services at the prices and rates mentioned by us in the Financial Bid Format/Schedule.
3. We have satisfied ourselves as to the correctness and sufficiency of the Contract Price cover all its obligations under the Contract

-
4. We enclose herewith the complete Eligibility Criteria Bid as required by you.
 5. We have carefully read and understood the terms and conditions of the bid document and the conditions of the contract applicable to the bid document and we do hereby undertake to supply as per these terms and conditions.
 6. Certified that the bidder is a company and the person signing the document is the authorized signatory/constituted attorney.
 7. We do hereby undertake that, until a real work order is prepared and executed, this bid, together with your written acceptance thereof and placement of letter of intent awarding the work order, shall constitute a binding contract between us.

Dated this day of 20__

Signature of Authorized Signatory
of Bidder Official Address: _____

Telephone No.

Telegraphic Address: Fax No.

E-mail

Contact Person Name:

Contact Person Mobile No:

Contact Person email:

Form 5: Bidder Information

[Bidder must provide all documents required to prove/ substantiate its Eligibility as required in Eligibility Criteria defined in Section V]

1	Name & Legal Status of the Service provider			
2	Organization Registration Details (Incorporation or Commencement of Business/ Other Statutory Registrations etc.)		Date of Incorporation/ Registration:	
3	GST Number:		PAN Number:	
4	Registered/ Corporate office Address of Service provider			
	Address & Contact Details (E-Mail, Ph. Nos. etc.) of Proprietor/ Directors of the Service provider	1)		
		2)		
		3)		
	Delhi (NCR) Office Address if any & Contact Details:			
	Names and Designations of the persons authorized for single point interaction with SMFC LTD			
	Mobile Numbers of Contact persons:		E-mail of Contact persons:	
	GeM (Government e-Marketplace) Registration:	(Yes/No)	If Yes, Regd. No.:	
			Date:	
			Category:	
Range of Supply/ Services:				
TReDS (Trade Receivables Discounting System) Registration:	(Yes/No)	If Yes, Regd. No:		
		Date:		
		Category:		
		Range of Supply/ Services:		

	Whether SC/ST/OBC Entrepreneur? (Yes, No)	(Yes/No)	(If Yes, please provide Supporting Documents)
	Whether Women Entrepreneur? (Yes/No)	(Yes/No)	(If Yes, please provide Supporting Documents)

Signature of Authorized Signatory of SI

Official Address:

Telephone No.:

Form 6: Project Implementation Plan

The Bidder shall submit a preliminary Project implementation plan along with the Bid which shall include at least the following activities:

- 1) Understanding the requirement as per this bid document*
- 2) Proposed overall system architecture*
- 3) Proposed project implementation phases*
- 4) Approach towards data privacy and cyber security;*
- 5) Details of proposed roll out and testing methodology along with data migration plan with mock runs;*
- 6) Approach paper documenting the interfaces for integration with existing and future applications based on the information provided by SMFC LTD;*
- 7) Project team structure;*
- 8) Quality Assurance Program;*
- 9) Training Schedule,*
- 10) Change Management Plan*
- 11) Documentation*
- 12) Cutover and Go-Live Plan*
- 13) Exit Management and Knowledge Transfer Plan*

This document will form the basis of the ‘Demonstration & Presentation’ to be given by the bidder before the Evaluation Committee, as specified in the Technical Evaluation, Section VI.

Form 7: Resume and Declaration

Name of Bidder:

Position [#1]: [title of position]		
Personnel information	Name:	Date of birth:
	Address:	E-mail:
	Professional qualifications: Academic qualifications: Language proficiency: <i>[language and levels of speaking, reading, and writing skills]</i>	
Details		
	Address of employer:	
	Telephone:	Contact (manager / personnel officer):
	Fax:	
	Job title:	Years with present employer:

Summarize professional experience in reverse chronological order. Indicate technical and managerial experience relevant to the Project.

Project	Role	Duration of involvement	Relevant experience
<i>[main project details]</i>	<i>[role and responsibilities on the project]</i>	<i>[time in role]</i>	<i>[describe the experience relevant to this position]</i>

Declaration

I, the undersigned [*insert either "Contractor's Representative" or "Key Personnel" as applicable*], certify that to the best of my knowledge and belief, the information contained in this Form 6 correctly describes myself, my qualifications, and my experience.

I confirm that I am available as certified in the following table and throughout the expected time schedule for this position as provided in the Bid:

Commitment	Details
Commitment to duration of contract:	<i>[insert period (start and end dates) for which this Contractor's Representative or Key Personnel is available to work on this contract]</i>
Time commitment:	<i>[insert period (start and end dates) for which this Contractor's Representative or Key Personnel is available to work on this contract]</i>

I understand that any misrepresentation or omission in this Form may:

- (a) be taken into consideration during Bid evaluation;
- (b) result in my disqualification from participating in the Bid;
- (c) result in my dismissal from the contract.

Name of Bidder's Representative or Key Personnel: *[insert name]*

Signature: _____

Date: (day month year): _____

Countersignature of authorized representative of the Bidder:

Signature: _____

Date: (day month year): _____

Form 8: Format for Performance Security (Bank Guarantee)

(To be stamped in accordance with Stamp Act if any, of the country for issuing bank)

Ref.: _____ Bank Guarantee: _____ Date: _____

Dear Sir,

In consideration of Sagarmala Finance Corporation Limited (hereinafter referred as the “**Client**”, which expression shall, unless repugnant to the context of meaning thereof include its successors, administrators and assigns) having awarded to M/s [name of the bidder] a [type of company], established under laws of [country] and having its registered office at<address> (hereinafter referred to as the “**Vendor**” which expression shall unless repugnant to the context or meaning thereof, include its successors, administrators, executors and permitted assigns), an Assignment for preparation of [name of assignment] Contract by issue of Client’s Contract Letter of Award No. <reference> dated [date] and the same having been unequivocally accepted by the Vendor, resulting in a Contract valued at INR [amount in figures and words] for (Scope of Work) (hereinafter called the “**Contract**”) and the Vendor having agreed to furnish a Bank Guarantee amounting to INR [amount in figures and words] to the Client for performance of the said Agreement.

We [Name of Bank] incorporated under [law and country] having its Head Office at [address](hereinafter referred to as the Bank), which expression shall, unless repugnant to the context or meaning thereof, include its successors, administrators executors and assigns) do hereby guarantee and undertake to pay the Client immediately on demand an or, all monies payable by the Vendor to the extent of INR [amount in figure and words] as aforesaid at any time up to [date] without any demur, reservation, contest, recourse or protest and/ or without any reference to the Vendor. Any such demand made by the Client on the Bank shall be conclusive and binding notwithstanding any difference between the Client and the Vendor or any dispute pending before any Court, Tribunal, Arbitrator or any other authority.

We agree that the Guarantee herein contained shall be irrevocable and shall continue to be enforceable until the Client discharges this guarantee.

The Client shall have the fullest liberty without affecting in any way the liability of the Bank under this Guarantee, from time to time to vary the advance or to extend the time for performance of the Contract by the Vendor nor shall the responsibility of the bank be affected by any variations in the terms and conditions of the contract or other documents. The Client shall have the fullest liberty without affecting this guarantee, to postpone from time to time the exercise of any powers vested in them or of any right which they might have against the Client and to exercise the same at any time in any manner, and either to enforce or to forbear to enforce any covenants, contained or implied, in the Contract between the Client and the Vendor any other course or remedy or security available to the client. The Bank shall not be relieved of its obligations under these presents by any exercise by the Client of its liberty with reference to the matters aforesaid or any of them or by reason of any other act or forbearance or other acts of omission or commission on the part of the Client or any other indulgence shown by the

Client or by any other matter or thing whatsoever which under law would but for this provision have the effect of relieving the Bank.

The Bank also agrees that the Client at its option shall be entitled to enforce this Guarantee against the Bank as a principal debtor, in the first instance without proceeding against the Vendor and notwithstanding any security or other guarantee that the client may have in relation to the Vendor's liabilities.

This Guarantee shall be irrevocable and shall remain in full force and effect until discharge by the Bank of all its obligations hereunder. This Guarantee shall not be affected by any change in the constitution or winding up of the Vendor / the Bank or any absorption, merger or amalgamation of the Vendor / the bank with any other Person.

Notwithstanding anything to the contrary contained herein, no obligation of the Bank to pay any amount under this guarantee shall arise prior to the fulfillment of the following conditions precedent:

(a) Written claim/demand(s) in terms of this guarantee of an aggregate amount less than or equal to the guaranteed amounts is/are made by the beneficiary hereunder; and

(b) Such written claim/demand(s) is/are delivered to the Bank on or before (claim expiry date) at the

.....Bank Branch.

Notwithstanding anything contained herein above our liability under this guarantee is limited to INR [amount in figure and words] and it shall remain in force up to and including [date] and shall extend from time to time for such period(s) (not exceeding one year), as may be desired by M/s [name of vendor] on whose behalf this guarantee has been given. Date this [date in words] day <month> of <year> in ('yyyy' format) at <place>.

WITNESS

1. [signature, name and address]

2. [signature, name and address]

[Official Address] Designation

[With Bank Stamp]

Attorney as Per Power of Attorney No.

Dated

Strike out, whichever is not applicable.

The stamp papers of appropriate value shall be purchased in the name of bank which issues the "Bank Guarantee". The bank guarantee shall be issued either by a bank (Nationalized / Scheduled) located in India or a foreign bank through a correspondent bank (scheduled) located in India or directly by a foreign bank which has been determined in advance to be acceptable to the Client.

Form 9: Format of Covering Letter by the Bidder for Submission of Bid

[Covering Letter shall be on the official letterhead of the Bidder]

[Reference No.]

From:

[Address of the Sole Bidder]

[Telephone No., Fax No., Email]

[Date]

To:

SMFC LTD

Western Wing, 1st Floor,

Thapar House, Janpath,

New Delhi-110001.

Sub: Bid for Selection of ERP Developer-cum-System Integrator for Understanding, Design, Develop, Install, Configure, Implement, Commission, Stabilize and Support & website for Enterprise Resource Planning (ERP) System

Ref: [Tender Details]

Dear Sir/ Madam,

I/We, the undersigned /Sole Bidder/ having read, examined, and understood in detail the RFP for Selection of vendor for Understanding, Design, Develop, Install, Configure, Implement, Commission, Stabilize and Support for Enterprise Resource Planning (ERP) System hereby submit our Bid comprising of Technical and Financial Bids.

1. We give our unconditional acceptance to the RFP including but not limited to all its instructions, terms and conditions, and formats attached thereto, issued by SMFC LTD, as amended. In token of our acceptance to the RFP, the same have been signed by us and enclosed to the Bid. We hereby submit our commitment to execute such requirements as per the provisions of the RFP and provisions of such RFP shall be binding on us.

2. Fulfilment of Eligibility

We undertake that we fulfil the Eligibility Criteria stipulated in the RFP and fulfil all the eligibility requirements as the Sole Bidder as outlined in the RFP.

We hereby confirm that in accordance with Form 1 of the RFP, we are herewith submitting legally binding undertaking supported by a board resolution from the *[insert name of Technically Evaluated Entity and/or Financially Evaluated Entity or its Ultimate Parent Company, as the case may be]* that all the equity investment obligations of *[insert name of the Sole Bidder]* shall be deemed to be equity investment obligations of the *[insert name of Technically Evaluated Entity and/or Financially Evaluated Entity or its Ultimate Parent Company, as the case may be]* and in the event of any default by *[insert name of the Sole Bidder]*, the same shall be met by *[insert name of Technically Evaluated Entity and/or Financially Evaluated Entity or its Ultimate Parent Company, as the case may be]*.

[To be inserted only in case the Bidder has sought qualification on the basis of technical and financial capability of its Affiliate(s) and/or its Parent]

3. Bid Security

We have enclosed a Bid Security of [Amount] in the form of a Bank Guarantee No. *[Insert Bank Guarantee Number]* (OR Demand Draft) dated *[Insert date of the Bank Guarantee]* as per Form 7 given in Section VII from *[Insert name of Bank providing Bid Bond]* and valid up to [Date].

4. No Deviation

We have submitted our Technical & Financial Bid strictly as per terms and formats of the RFP, without any deviations, conditions and without mentioning any assumptions or notes for the Financial Bid in the said format.

5. Acceptance

We hereby unconditionally and irrevocably agree and accept that the decision made by SMFC LTD in respect of any matter regarding or arising out of the RFP shall be binding on us. We hereby expressly waive all claims in respect of Bid process.

We confirm that there are no litigations or disputes against us, which materially affect our ability to fulfil our obligations about fulfilling our obligations as per the RFP.

6. Familiarity with Relevant Indian Laws and Regulations

We confirm that we have studied the provisions of the relevant Indian laws and regulations as required to enable us to submit this Bid and execute the RFP Documents, in the event of our selection as Selected Bidder. We further undertake and agree that all such factors as mentioned in the ERP Contract have been fully examined and considered while submitting the Bid.

7. Contact Person

Details of the contact person representing our Sole Bidder (registered Company) supported by the Power of Attorney prescribed in Form 10 given in Section VII of the RFP are furnished as under:

Name:

Designation:

Company:

Address:

Mobile:

Phone:

Fax:

Email:

1. We are submitting herewith the Technical Bid containing duly signed formats in electronic form only, (duly attested) as desired in the RFP for your consideration.
2. We are also submitting herewith the Financial Bid in electronic form only, as per the terms and conditions in the RFP.
3. The original copy of EMD/POA/Integrity pact, if any, will be submitted in hard copy.
8. It is confirmed that our Bid is consistent with all the requirements of submission as stated in the RFP and subsequent communications from SMFC LTD.
9. The information submitted in our Bid is complete, strictly as per the requirements stipulated in the RFP and is correct to the best of our knowledge and understanding. We would be solely responsible for any errors or omissions in our Bid.
10. We confirm that all the terms and conditions of our Bid are valid for acceptance for a period of 180 days from the Bid Submission Deadline.
11. We confirm that we have not taken any material deviation so as to be deemed non-responsive with respect to the provisions stipulated in the RFP.
12. We confirm that no order/ ruling has been passed by any Competent Court or Appropriate Commission against us or in the preceding 1 (one) year from the Bid Submission Deadline for breach of any contract and that the Bid Security submitted by the us has not been forfeited, either partly or wholly, in any bid process in the preceding 1 (one) year from the Bid Submission Deadline.

-
13. We confirm that we are not currently blacklisted by any Govt. Organization or Regulatory Agencies or Govt. undertaking.
14. We undertake to hand over complete Source code, Data Dump of complete database & table structure design along with all technical documents, licenses and IPR documents to SMFCL whenever asked for. The code procured or developed, documents, and licenses procured shall be in the name of SMFC Ltd. with perpetual, irrevocable, transferable rights, no vendor renewal dependencies.
15. We are registered / exempt from registering in accordance with applicable laws
[Evidence of valid registration by the Competent Authority shall be attached if applicable]

Dated the *[Insert date of the month]* day of *[Insert month, year]* at
..... *[Insert place]*.

Thanking you,

Yours Sincerely,

[Insert Signature here]

[Insert Name here]

[Insert Designation here]

Form 10: Format of Power of Attorney by Bidder authorizing an Individual Designated Representative

[To be on non-judicial stamp paper of Rupees One Hundred Only (INR 100/-) or appropriate value as per Stamp Act relevant to place of execution. Foreign companies submitting Bids are required to follow the applicable law in their country.]

To be on non-judicial stamp paper of appropriate value as per Stamp Act relevant to place of execution.

Know all men by these presents, We (Name and address of the registered office of the Bidder) do hereby constitute, appoint and authorize Mr./Ms..... (name and residential address) who is presently employed with us and holding the position of as our attorney, to do in our name and on our behalf, all such acts, deeds and things necessary in connection with or incidental to our Response for **implementer of ERP for SMFC LTD web applications & portal**, including signing and submission of all documents and providing information / responses to <NAME OF THE BIDDER>, representing us in all matters before <NAME OF THE BIDDER>, and generally dealing with <NAME OF THE BIDDER>. in all matters in connection with our Response to RFP.

We hereby agree to ratify all acts, deeds and things lawfully done by our said attorney pursuant to this Power of Attorney and that all acts, deeds and things done by our aforesaid attorney shall and shall always be deemed to have been done by us.

For [Insert name of the Bidder on whose behalf PoA is executed]

.....

(Signature)

Name:

Designation:

Accepted

.....

(Signature of the Attorney)

Name:

Designation:

Address:

.....

(Name, Designation and Address of the Attorney)

Specimen signatures of attorney attested by the Executant

.....

(Signature of the Executant)

.....

(Signature of Notary Public)

Place:

Date:

Notes:

- a) To be executed by Bidding Company
- b) The mode of execution of the Power of Attorney should be in accordance with the procedure, if any, laid down by the applicable law and the charter documents of the executant(s) and the same should be under common seal of the executant affixed in accordance with the required procedure. Further, the person whose signatures are to be provided on the power of attorney shall be duly authorized by the executant(s) in this regard
- c) Also, wherever required, the executant(s) should submit for verification the extract of the chartered documents and documents such as a Board resolution / power of attorney, in favor of the Person executing this power of attorney for delegation of power hereunder on behalf of the executant(s).

Form 11: Format of undertaking on compliance of tender requirements along with terms and conditions [(To be submitted on Rs.100 Stamp paper issued in Delhi-NCR/States where Service provider's office is located duly signed by the authorized signatory duly signed by the authorized signatory of the Service provider)]

I/We hereby undertake that I/we have examined/ perused, studied and understood the tender no.__dated__and any corrigendum/ addendum/ clarification etc. completely and have submitted my/our bid in pursuance to the said documents.

I/We hereby undertake that I/We understand that the Scope of Work and Requirement of this Tender is indicative only and not exhaustive in any manner. I/We understand that the scope of work may undergo minor changes as per prevailing SMFC LTD requirements at the time of signing of contract.

I/We hereby undertake that we shall comply with the final Scope of work and requirements and tender terms and conditions completely and there are no deviations and/or submissions and/or clarifications of any manner and/or sort and/or kind in this regard from my/our side.

I/We hereby undertake to provide the further requisite OEM authorization as and when required and/or asked for by SMFC LTD, as per the solution and/or requirements, as decided by SMFC LTD at their discretion.

I/We hereby undertake that I/We understand that the SMFC LTD reserves the right to float a separate tender for the scope of work and requirements as mentioned in this tender irrespective of the outcome of this tender. I/We understand that in such a case I/We shall bid separately for that tender and in no case our bid to this tender shall be deemed as a bid for the said tender.

I/We hereby undertake to provide the services and undertake to be the single point of contact for SMFC LTD for all services, terms and conditions and for the entire scope of work and requirements as defined in this tender document.

I/We hereby undertake that I/We do understand that my/our bid should be as per the tender document and should be accordingly submitted to the SMFC LTD. In case of a failure to comply and/or a variation the SMFC LTD has got sole discretion to consider or disqualify my/our bid for the tender and I/We shall be not having any claim of any sort/kind/Annexure on the same.

I/We agree to bind by this bid for a period of 180 days after the date fixed for opening and it shall remain binding upon us and may be accepted at any time before the expiration of that period and till the time I/We after the expiry of the bid validity period really withdraw my/our response in writing with a notice period of seven working days and associated terms and conditions and as specified in the tender document and in all such cases my/our bid shall be deemed to be valid.

I/We hereby attach the duly signed and stamped/digitally signed tender document as an acceptance and compliance of tender specifications and terms & conditions with the technical response without any deviations and/or submissions and/or clarifications of any manner and/or sort and/or kind in this regard from my/our side.

I/We understand that mentioning of any pre-requisites, presumptions, assumptions, hiding/ twisting/ deletion/ reduction/ manipulation/ disguising of scope of work and/or application features and/or infrastructure and/or project deliverables etc. in any Annexure and/or by any means and/or under any head shall not be constituted as a part of the bid and in case of award of the tender the same should not be claimed by me/us while award and/or subsequent execution of work. The decision of SMFC LTD on such issues shall be binding on me/us and the same cannot be arbitrated upon by me/us.

I/We hereby undertake that we abide by all the terms and conditions mentioned in the tender along with corrigendum, if any

I/We hereby undertake that I/We shall meet all business requirements of SMFC LTD and shall provide the same solution as proposed in the bid document during contract period. In case of a default SMFC LTD can levy liquidated damages on myself/ ourselves as per tender terms and conditions.

I/We hereby declare that our company/ organization has not been blacklisted, debarred, banned or disqualified by any Government or any Government agencies including PSUs during a period of last five years.

I/We understand that at any stage during the tenure of the contract if it is found that any statement or document submitted by I/We is false/forged/invalid, SMFC LTD has discretion to terminate the contract and get the work done through third party as per the risk purchase clause mentioned in this tender.

I/We hereby affirm that our bid is valid for the period including the deemed period as specified in the tender document.

Signature of Authorized Signatory Name of the Signatory

Date

Place

Company Name Company Seal

Form 12: Format for undertaking towards not being blacklisted

[(To be submitted on Rs.100 Stamp paper issued in Delhi-NCR / States where Service provider's office is located duly signed by the authorized signatory duly signed by the authorized signatory of the Service provider)]

I,_____Authorized Signatory of M/s_____ hereby give undertaking that we, as a company are not black-listed by any Government Department/Regulatory body/CPSU/ PSU Banks/Autonomous Bodies/Statutory Bodies/ SMFC LTD/ Ministry of Ports, Shipping & waterways (GOI) PSU or any entity controlled by them under any Central/ State Govt/ PSU act/ rule or by National/ International financial institutions/ Private Institution in India.

Further, if information furnished above stands false at any stage, we shall be completely liable for actions taken by SMFC LTD as per terms & conditions of the tender including disqualification and exclusion from future contracts/assignments.

(Signature of Authorized Signatory) Name:

Designation:

Seal:

Form 13: Record of Similar Work Done

Name of the Project:	Location:
Client Name:	Client Address:
Type of Client: (PSU / Power SMFC LTD/ Indian Power SMFC LTD/ Private/ Others):	
Project Duration (In Months):	Project Value: (In INR Crores):
Status: (Complete / Ongoing)	
Start Date:	Completion Date:
Number of Users*:	Modules covered*:
Type of software implemented: ERP product/Tailored ERP/Other product/Other(specify)* If product, name of the OEM & Product implemented*:	
Complete Documentary Evidence Attached (Yes/No):	Documentary Evidence (Start Page No. To End Page No.):

S. No.	Name of Technically Evaluated Entity	Relationship with the Bidder	Date of PO/ WO	Contract Period	No. of Consumer, Nodes, etc.	Description of Work	PO/ WO Value (In INR)	Confirmation of PO/ WO	Confirmation of attachment of Installation Milestone/
1.									

Form 14: Pre-Contract Integrity Pact

[(To be submitted on Rs.100 Stamp paper issued in Delhi-NCR / States where Service provider's office is located duly signed by the authorized signatory duly signed by the authorized signatory of the Service provider)]

Between

Sagarmala Finance Corporation Limited (SMFCL) hereinafter referred to as "The Principal";

and

..... hereinafter referred to as "The Bidder";

Preamble

The Principal intends to award, under laid down organizational procedures, contract/s for -----

-

----- The Principal values full compliance with all relevant laws of the land, rules, regulations, economic use of resources and of fairness / transparency in its relations with its Bidder(s) and / or Contractor(s).

In order to achieve these goals, the Principal will appoint Independent External Monitors (IEMs) who will

monitor the tender process and the execution of the contract for compliance with the principles mentioned above.

Section 1 - Commitments of the Principal

(1) The Principal commits itself to take all measures necessary to prevent corruption and to observe the following principles:-

- a. No employee of the Principal, personally or through family members, will in connection with the tender for, or the execution of a contract, demand; take a promise for or accept, for self or third person, any material or immaterial benefit which the person is not legally entitled to.
- b. The Principal will, during the tender process treat all Bidder(s) with equity and reason. The Principal will in particular, before and during the tender process, provide to all Bidder(s) the same information and will not provide to any Bidder(s) confidential / additional information through which the Bidder(s) could obtain an advantage in relation to the tender process or the contract execution.
- c. The Principal will exclude from the process all known prejudiced persons.

(2) If the Principal obtains information on the conduct of any of its employees which is a criminal offence under the JPC/PC Act, or if there be a substantive suspicion in this regard, the Principal will inform the Chief Vigilance Officer and in addition can initiate disciplinary actions.

Section 2 - Commitments of the Bidder(s)/ Contractor(s)

(1) The Bidder(s)/ Contractor(s) commit themselves to take all measures necessary to prevent corruption. The Bidder(s)/ Contractor(s) commit themselves to observe the following principles during participation in the tender process and during the contract execution.

a. The Bidder(s)/ Contractor(s) will not, directly or through any other person or firm, offer, promise or give to any of the Principal's employees involved in the tender process or the execution of the contract or to any third person any material or other benefit which he/she is not legally entitled to, in order to obtain in exchange any advantage of any kind whatsoever during the tender process or during the execution of the contract. The Bidder(s)/ Contractor(s) will not enter with other Bidders into any undisclosed agreement or understanding, whether formal or informal. This applies in particular to prices, specifications, certifications, subsidiary contracts, submission or non-submission of bids or any other actions to restrict competitiveness or to introduce cartelization in the bidding process.

b. The Bidder(s)/ Contractor(s) will not commit any offence under the relevant JPC/PC Act; further the Bidder(s)/ Contractor(s) will not use improperly, for purposes of competition or personal gain, or pass on to others, any information or document provided by the Principal as part of the business relationship, regarding plans, technical proposals and business details, including information contained or transmitted electronically.

c. The Bidder(s)/Contractor(s) of foreign origin shall disclose the name and address of the Agents/representatives in India, if any, Similarly the Bidder(s)/Contractor(s) of Indian Nationality shall furnish the name and address of the foreign principals, if any. Further details as mentioned in the 'Guidelines on Indian Agents of Foreign Suppliers' shall be disclosed by the Bidder(s)/Contractor(s). Further, as mentioned in the Guidelines all the payments made to the Indian agent/representative have to be in Indian Rupees only.

d. The Bidder(s)/ Contractor(s) will, when presenting their bid, disclose any and all payments made, is committed to or intends to make to agents, brokers or any other intermediaries in connection with the award of the contract.

e. Bidder(s) /Contractor(s) who have signed the Integrity Pact shall not approach the Courts while representing the matter to IEMs and shall wait for their decision in the matter.

(2) The Bidder(s) / Contractor(s) will not instigate third persons to commit offences outlined above or be an accessory to such offences.

Section 3 - Disqualification from tender process and exclusion from future contracts

(1) If the Bidder(s)/Contractor(s), before award or during execution has committed a transgression through a violation of Section 2, above or in any other form such as to put their reliability or

credibility in question, the Principal is entitled to disqualify the Bidder(s)/Contractor(s) from the tender process or take action as per the procedure mentioned in the 'Guidelines on Banning of business dealings'.

Section 4 - Compensation for Damages

- (1) If the Principal has disqualified the Bidder(s) from the tender process prior to the award according to Section 3, the Principal is entitled to demand and recover the damages equivalent to Earnest Money Deposit/ Bid Security.
- (2) If the Principal has terminated the contract according to Section 3, or if the Principal is entitled to terminate the contract according to Section 3, the Principal shall be entitled to demand and recover from the Contractor liquidated damages of the Contract value or the amount equivalent to Performance Bank Guarantee.

Section 5 - Previous transgression

- (1) The Bidder declares that no previous transgressions occurred in the last three years with any other Company in any country conforming to the anti-corruption approach or with any Public Sector Enterprise in India that could justify his exclusion from the tender process.
- (2) If the Bidder makes incorrect statement on this subject, he can be disqualified from the tender process or action can be taken as per the procedure mentioned in 'Guidelines on Banning of business dealings'.

Section 6 - Equal treatment of all Bidders/ Contractors/ Subcontractors

- (1) In case of Sub-contracting, the Principal Contractor shall take the responsibility of the adoption of Integrity Pact by the Sub-contractor.
- (2) The Principal will enter into agreements with identical conditions as this one with all Bidders and Contractors.
- (3) The Principal will disqualify from the tender process all bidders who do not sign this Pact or violate its provisions.

Section 7 - Criminal charges against violating Bidder(s)/ Contractor(s)/ Subcontractor(s)

- (1) If the Principal obtains knowledge of conduct of a Bidder, Contractor or Subcontractor, or of an employee or a representative or an associate of a Bidder, Contractor or Subcontractor which constitutes corruption, or if the Principal has substantive suspicion in this regard, the Principal will inform the same to the Chief Vigilance Officer.

Section 8 - Independent External Monitor

- (1) The Principal appoints competent and credible Independent External Monitor for this Pact after approval by Central Vigilance Commission. The task of the Monitor is to review independently and objectively, whether and to what extent the parties comply with the obligations under this agreement.
- (2) The Monitor is not subject to instructions by the representatives of the parties and performs his/her functions neutrally and independently. The Monitor would have access to all Contract documents, whenever required. It will be obligatory for him / her to treat the information and documents of the Bidders/Contractors as confidential. He/ she reports to the MD, SMFCL.
- (3) The Bidder(s)/Contractor(s) accepts that the Monitor has the right to access without restriction to all Project documentation of the Principal including that provided by the Contractor. The Contractor will also grant the Monitor, upon his/her request and demonstration of a valid interest, unrestricted and unconditional access to their project documentation. The same is applicable to sub-contractor.
- (4) The Monitor is under contractual obligation to treat the information and documents of the Bidder(s)/ Contractor(s)/ Sub-contractor(s) with confidentiality. The Monitor has also signed declarations on 'Non-Disclosure of Confidential information' and of 'Absence of Conflict of interest'. In case of any conflict of interest arising at a later date, the IEM shall inform MD, SMFCL and rescues himself/ herself from that case.
- (5) The Principal will provide to the Monitor sufficient information about all meetings among the parties related to the Project provided such meetings could have an impact on the contractual relations between the Principal and the Contractor. The parties offer to the Monitor the option to participate in such meetings.
- (6) As soon as the Monitor notices, or believes to notice, a violation of this agreement, he/she will so inform the Management of the Principal and request the Management to discontinue or take corrective action, or to take other relevant action. The monitor can in this regard submit non-binding recommendations. Beyond this, the Monitor has no right to demand from the parties that they act in a specific manner, refrain from action or tolerate action.
- (7) The Monitor will submit a written report to the MD, SMFCL within 8 to 10 weeks from the date of reference or intimation to him by the Principal and, should the occasion arise, submit proposals for correcting problematic situations.
- (8) If the Monitor has reported to the MD, SMFCL, a substantiated suspicion of an offence under relevant JPC/ PC Act, and the MD, SMFCL has not, within the reasonable time taken visible action to proceed against such offence or reported it to the Chief Vigilance Officer, the Monitor may also transmit this information directly to the Central Vigilance Commissioner.
- (9) The word 'Monitor' would include both singular and plural.

Section 9 - Pact Duration

- (1) This Pact begins when both parties have legally signed it. It expires for the Contractor 12 months after the last payment under the contract, and for all other Bidders 6 months after the contract has been awarded. Any violation of the same would entail disqualification of the bidders and exclusion from future business dealings.
- (2) If any claim is made / lodged during this time, the same shall be binding and continue to be valid despite the lapse of this pact as specified above, unless it is discharged / determined by MD of SMFCL.

Section 10 - Other provisions

- (1) This agreement is subject to Indian Law. Place of performance and jurisdiction is the Registered Office of the Principal, i.e. New Delhi.
- (2) Changes and supplements as well as termination notices need to be made in writing. Side agreements have not been made.
- (3) If the Contractor is a partnership or a consortium, this agreement must be signed by all partners or consortium members.
- (4) Should one or several provisions of this agreement turn out to be invalid, the remainder of this agreement remains valid. In this case, the parties will strive to come to an agreement to their original intentions.
- (5) Issues like Warranty / Guarantee etc. shall be outside the purview of IEMs.
- (6) In the event of any contradiction between the Integrity Pact and its Annexure, the Clause in the Integrity Pact will prevail.

For & On behalf of the Principal
For & On behalf of Bidder/Contractor
(Office Seal)
(Office Seal)
Place -----•
Date -----
Witness -1
Witness-2
Name:
Name:
Address:
Address:

Form 15: Format of summary of audited financial statements

< This Annexure needs to be submitted by the Bidder. In case of an AIF or Foreign Investment Fund using ACI, ACI would be considered as per the certificate issued by statutory auditor (or such other certificate as filed with the regulator in the relevant jurisdiction) not older than 1 (one) month prior to the date of Bid Submission>

[Reference No.]

From:

[Address of the Bidder]

[Telephone No., Fax No., Email]

[Date]

To:

SMFC LTD

Western Wing, 1st Floor, Thapar House,

Janpath, New Delhi-110001

Sub: Audited Financial Statement for [Insert name of the Bidder].

Ref: [Tender Details]

Dear Sir/ Madam,

This is to certify that [Insert name of the Bidder] having its Registered Office at [Insert Registered Address of the bidder] are in the business of [Insert briefly the nature of the business], have recorded the following:

NETWORTH FOR LAST THREE FINANCIAL YEARS

S.No.	Name of Financially Evaluated Entity(ies)	Relationship with Bidder	Financial Year	Net Worth Amount(in Indian Rupees)
1			2024-25	
2			2023-24	
3			2022-23	

Or

ACI FOR PRECEDING FINANCIAL YEAR

S.No.	Name of Financial Entity(ies)	Relationship with Bidder	Financial Year	ACI Amount(In Indian Rupees)
1			2024-25	
2			2023-24	
3			2022-23	

The above Net worth/ACI are arrived from our Audit Reports for the last three/ preceding financial years duly submitted to the Income Tax SMFC LTD along with our Audit Reports.

Hence, we certify from the records submitted to us. Thanking you,

Sincerely yours,

Yours Sincerely,

[Insert Signature here]

[Insert Name here]

[Insert Designation here]

Date: [Date]

Place: [Place]

Form 16: Table of Compliance

The Bidder shall submit 'Clause by Clause' compliance to the RFP document including the technical specifications and functional requirements (with amendments, if any) as per the format prescribed in Form 16

The Bidder shall annotate the Table of Contents of each section to provide a high-level summary of compliance status. In all cases, the following symbols, and no others shall be used:

- **C - Bid complies with all requirements in the adjacent paragraph.**
- **A - Bid is not compliant with the requirements in the adjacent paragraph, but a functional alternative is proposed.**
- **X - Bid takes exception to the requirements of the adjacent paragraph and no functional alternative is proposed.**

Only one symbol shall be assigned to paragraph and shall indicate the worst-case level of compliance for that paragraph. This annotation may be handwritten.

The Bidder shall also underline, on the compliance copy, all requirements to which exceptions have been taken (X) or to which alternatives have been proposed (A).

Each alternative shall be clearly and explicitly described. Such descriptions shall use the same paragraph numbering as the bid document sections addressed by the alternatives. All alternative descriptions shall be in one contiguous section of the bidder's proposal, preferably in the same volume, and titled "Alternatives." A separate section titled "Exceptions" shall also be provided containing any discussion or explanation chooses to provide concerning exceptions taken. Alternatives which do not substantially comply with the intent of the Bid documents will be considered exceptions.

Any clause which is not included in this compliance table shall be treated as "fully complied" or C.

The SMFC LTD will assess the merits of each alternative and exception and will be the sole judge as to their acceptance.

The bidder must provide the details of PQR and TQR supporting documents in the following format

Annexure 2: Bid Security Declaration Format

(On Bidders Letterhead)

Date: Tender No: _____

To

Sagarmala Financial Corporation Limited
124, Thapar House, Janpath Lane,
Delhi 110001

I/We undersigned declare that:

1) I/We understand that, according to your conditions, bids must be supported by a Bid Securing Declaration.

2) I/We accept that I/We may be disqualified / debarred from bidding against SMFCL tenders for a period of year from the date of notification if I/We are in a breach of any obligation under the bid conditions, because I/We

a) have withdrawn/modified/amended, impairs or derogates from the tender, my/our bid during the period of bid validity specified in the form of Bid; or

b) having been notified of the acceptance of our Bid by the purchaser during the period of bid validity (i) fail or refuse to execute the contract, if required, or (ii) fail or refuse to furnish the Performance Security within the timeline, in accordance with the instructions to Bidders & as per tender terms & conditions.

3) I/We understand this Bid Security Declaration shall cease to be valid on the Thirty First day from following,

a) If I am/we are not the successful Bidder, the receipt of your notification of the name of the successful Bidder; or

b) the expiration of the validity of my/our Bid or any extension thereof.

Signed:

(insert signature of person whose name and capacity are shown)

In the capacity of (insert legal capacity of person signing the Bid Security Declaration)

Name: (insert complete name of person signing the Bid Security Declaration)

Duly authorised to sign the bid for an on behalf of (insert complete name of Bidder)

Dated on _____ day of _____ (insert date of signing)

Corporate Seal (where appropriate)

Table of Compliance

Sl. No.	PQR/TOR Clause Ref.	Criteria Description	Supporting Document	Compliance Status (C/A/X) (Complied/Alternative/Exception)	Page at which document provided as part of Technical Proposal
1	Section I 1.2.24	Bid Validity: 180 days from date of opening	Form 4: Bid Annexure / Form 1: Undertaking		72, 108
2	Section II 2.3	EMD Deposit and MSME Exemption Conditions	EMD Instrument / MSME Certificate		9
3	Section II 2.4, 2.5	EMD Refund / Forfeiture Policy	Compliant, agreed		10, 54, 73, 83
4	Section II 2.6	Pre-bid Query Submission Format	Compliant, agreed		11
5	Section II 2.7	Zero Deviation Bidding Declaration	Form 11: No deviation undertaking		11, 89
6	Section II 2.10	Bid Submission Mode, Language, Currency	Compliant, agreed		12–14
7	Section II Annexure I	Financial Bid Submission Process (QP format + Excel)	Compliant, agreed		18, 56-57, 108-112
8	Section III 3.1	Objective of Assignment – ERP Deployment	Form 6: Technical Proposal		19,78
9	Section III 3.2	Overall ERP Architecture	Architecture Document		20–24
10	Section IV 4.1	Scope of Work: ERP lifecycle implementation	Compliant, agreed		26–32
11	Section IV 4.5	Functional Requirements of All ERP Modules	Compliant, agreed		33–49
12	Section V 5.5.1	General Eligibility – Regn. Certs, Certifications, HR Strength, Office Location	Forms 1 & 5 + HR Letter + Certs		51–54, 65–75, 76-77
13	Section V 5.5.1 Table (2.1)	Financial Eligibility – ₹1 Cr Turnover + Positive Net-worth (FY 22–25)	Form 15: CA Certificate / Audited FS		98
14	Section V 5.5.1 Table (3)	Experience in PSU NBFCs + Delivered Functional ERP Modules	Form 13: Project References		92

Sl. No.	PQR/TOR Clause Ref.	Criteria Description	Supporting Document	Compliance Status (C/A/X) (Complied/Alternative/Exception)	Page at which document provided as part of Technical Proposal
15	Section VI 6.4.3	Technical Evaluation Matrix (Min. 60 marks)	Form 2: Technical Bid Compliance		70
16	Section VI 6.4.4	QCBS Evaluation (Technical 70%, Financial 30%)	Compliant, agreed		55-57
17	Section VI 6.9	Performance Security (10%) Phase 1 & 2 (Form 8)	Compliant, agreed		60
18	Section VII	Forms 1 to 19 Submission with Index	All Forms: Signed and Indexed		64–106
19	Section VIII Format 1–2	Financial Proposal Format – ERP, S/W, DB, AMC, Man-day breakup	Excel Sheet and Undertaking Letter		107–111
20	Section IX 9.1–9.34	Implementation Phases, Testing, Go-Live & Stabilization	Compliant, agreed		112–154
21	Section IX 9.35	Exit Management and Knowledge Transfer Policy	Compliant, agreed		154–162
22	Section IX 9.11-9.12	Training & Change Management Plan	Compliant, agreed		125-127
23	Section IX 9.36-9.39	Payment Milestones and % Allocation & penalty	Compliant, agreed		162–165
24	Section IX 9.40	SLA Matrix: Availability, Resolution, Penalties	Compliant, agreed		165–173
25	Section IX Form 12	Declaration of Not Being Blacklisted	Form 12: Self-declaration		91

Form-17: Change Request Form

- **Project Name:** **Module Name:**

- **Request Number & Date of Request**

- **Requested by:**
 Requester Email Id/ Contact Phone Number
 Requester Project Role: End User / Project Manager / Vendor PM etc.
 Name & Designation:

- **Subject/Reference**
 <Deviation reference to the scope viz. Name of Requirements Document, clause number, para etc.>

- **Description of Change**
 Problem definition

- **Proposed Changes**
 High level explanation of solution

- **Impact Analysis**
 Resources, Schedules and modifications as a result of the Change – locations where software needs to be updated – changes in database to be taken care of - impact on on-going training and handholding etc.

- **Effort Estimation**
 Number of person-days

- **Evaluation for Acceptance of Change Request**
 Evaluation Comments
 Name, Designation and Signature of Evaluator
 Date of Evaluation

- **Priority: High / Medium / Low**

Sl. No.	PQR/TOR Clause Ref.	Criteria Description	Supporting Document	Compliance Status (C/A/X) (Complied/ Alternative/ Exception)	Page at which document provided as part of Technical Proposal
• Approved: Yes / No Date: xx/xx/xxxx Name, Designation of Approver Signature of Requester Signature of Approver Expected Date of Start: xx/xx/xxxx Expected Date of Completion: xx/xx/xxxx					

Form 18- List of Software/Licenses proposed

Sub: SELECTION OF VENDOR FOR UNDERSTANDING, DESIGN, DEVELOPE, INSTALL, CONFIGURE, COMMISSION, STABILIZE & MAINTAIN OF WEB & MOBILE BASED ENTERPRISE RESOURCE PLANNING (ERP) SOLUTION in SMFC LTD

SOFTWARE RELATED

	(select one per item)			(select one per item)	
Software Item	System Software	General-Purpose Software	Application Software	Standard Software	Custom Software

LICENSE RELATED

Description of Item	License type	Version	Quantity	Validity	Remark

Form 19- Undertaking related to ESG

(On letter Head of the Company/Agency)

Undertaking related to ESG

1. Name of the Agency:

2. Address of Agency:

We herewith declare that –

1. We adheres to fair labour practices, ensuring a safe working environment, fair wages, and compliance with applicable labour laws.
2. We upholds ethical business conduct, including anti-corruption measures.
3. We provide products that are environmentally sustainable, have consciously minimized carbon footprints in the production or sourcing process and invariably incorporate a minimum percentage of recycled materials wherever applicable.
4. We encourage diversity and inclusion within its organization and supply chains and complies with health and safety regulations, ensuring the well-being of their employees

It is certified that the information furnished above is true and correct.

(Signature of Authorized Signatory)

(With Official Seal)

Date :-

Place :-

SECTION VIII FINANCIAL PROPOSAL- FORMS

Sr.	Document	Attached? (Yes/ No)	For Official Use
1	Undertaking as per format provided in Format 1		
2	Format for Financial Breakup of Cost Components in Format 2		

Format 1: Format of undertaking of Financial Bid

[IMPORTANT NOTE: THE FINANCIAL BID SHALL ONLY BE SUBMITTED IN THE ELECTRONIC FORMAT. IT SHALL NOT BE SUBMITTED IN HARD COPY OR AS A PART OF THE TECHNICAL BID.]

[On the letter head of the Bidder]

[Reference No.]

From:

[Address of the Bidder]

[Telephone No., Fax No., Email]

[Date]

To:

SMFC LTD

Western Wing, 1st Floor, Thapar House,

Janpath, New Delhi-110001

Sub: Financial Bid for Selection of ERPSI for Understanding, Design, Develop, Install, Configure, Commission, Stabilize and Maintain for an integrated Enterprise Resource Planning (ERP) System.

Ref: [Tender Details]

Dear Sir/ Madam,

We, the undersigned [Insert name of the Bidder] having read, examined and understood in detail the RFP for Implementation of [SMFC LTD]'s integrated ERP System hereby submit our Financial Bid. We hereby undertake and confirm that:

- A. We have submitted our Financial Bid strictly in accordance with the RFP without any deviations or condition.

-
- B. Our Financial Bid is consistent with all the requirements of submission as stated in the RFP and subsequent communications.
- C. Price quoted clearly mentions the total cost (basic cost, Goods and Services Tax, or any other taxes/duties/levies). There is no price information quoted in the Eligibility-cum-technical bid document.
- D. It is hereby confirmed that the financial bid submitted strictly follows that of RFP format; no price information has been included in the technical bids and quoted prices are firm during entire contract term.
- E. Under no circumstances shall escalation in prices of this Financial Bid be entertained by SMFC LTD during entire tenure of the contractual period, irrespective of any factors within or beyond control of the Bidder.
- F. The details quoted herein shall stand valid at least for 180 days from the date of submission of this Financial Bid and for implementation of Project, if awarded, as per the timeframe indicated in the RFP.
- G. Breakup of the quoted price are as per the Annexure attached herein.

Dated the [Insert date of the month] day of [Insert month, year] at [Insert place].

Thanking you,

Sincerely yours,

[Insert Signature here]

[Insert Name here]

[Insert Designation here]

Format 2: Format for Financial Breakup of Cost Components

SI. No.	Description	Unit Price (Excluding GST)(Rs.)	Qty (#)	GST (%)	GST (In Rs.)	Total Price (including GST) (In figures) (In Rs.)
	2	3	4	5	6	(7) = (3*4) + (6)
1	ERP System Software implementation cost up to warranty period		1			
2	Data Base License Cost (For ____ users) (100 users for DR) for 5 years		1			
3	Cost of SLA Management & ticketing tool		1			
4	AMC Cost for 1st year		1			
5	AMC Cost for 2nd year		1			
6	AMC Cost for 3rd year		1			
7	AMC Cost for 4th year		1			
8	AMC Cost for 5th year		1			
9	Man Days charges (For additional work through change request as per Form-17 mentioned under Section VII)		100			
10	Any other cost (provide detail) for 5 years		1			
11	hosting cost for Website		1			
	Grand Total =SUM of Column-7 of Srl-1 to 13)					

Optional items

Srl	Description	Unit cost (A)	Tax (B)	Line Item Total (C=A+B)
1	Additional 1 vCPU			
2	Additional 4 GB RAM			

3	Additional 20 GB storage (SSD)			
---	--------------------------------	--	--	--

Note:

Any item/ material either hardware or software required to meet the functionality specified in the tender document whose related component is missing in the above table must be accounted by the Bidder and the price of the same is assumed to have reflected and taken care off in the price bid by the Bidder, in the 'Any other cost' line-item (Srl-10) in this commercial bid.

Quoted price shall be firm for the entire tenure of contract period.

SMFC LTD is liable only to pay the quoted price and as per the payment terms mentioned in the RFP to meet all the requirements as specified in the RFP.

The Sl. No 9 is for price discovery of the man-days for any additional work which is out of cope of this RFP, will be done through change request and will be considered for evaluation of L1 price. It is to mention that price quoted against Sl. No 9 will not be considered as part of the Contract Amount for monthly payment.

SECTION IX. ERP SYSTEM REQUIREMENTS AND SERVICE LEVEL AGREEMENTS

9. Understand, Design, Develop, Supply, Install, Configure, Integrate, Migrate, Commission, stabilize, maintain an integrated ERP system:

Enterprise Resource Planning system together with relevant database, licenses, and other software in conformance to Industry standards

9.1 GENERAL REQUIREMENTS

9.1.1 LATEST VERSION OF THE DATABASE AND OTHER TOOLS OFFERED

9.1.2 ERPSI shall prepare and submit a detailed project plan for the software development /customization.

9.1.3 The ERPSI shall deploy a dedicated team experienced in installation, configuration, customization, integration and testing, implementation, deployment of the proposed ERP system.

9.1.4 Development, Configuration of the specific ERP modules, third party bolt-on applications, development of interfaces wherever and whenever necessary.

9.1.5 The ERPSI shall ensure that the proposed ERP system provides adequate interfacing mechanisms (both at the application and data level) with a view to integrate future applications of SMFC LTD. Such interfaces shall follow industry standards such as Application Programming Interface (API's) and web services, etc.

9.1.6 The ERPSI shall supply and install the application, database and related software, integration tools, requisite licenses. The SI shall also describe and document the process to be followed for installing and operating the same.

9.1.7 The ERPSI shall handover the latest version of complete ERP Source Code, Data Dump, Technical IPR documents to SMFCL (soft copy) whenever asked for. The code developed or procured, documents and all licenses procured shall be in the name of SMFC Ltd. with perpetual, irrevocable, transferable rights, no vendor renewal dependencies.

9.1.8 The ERPSI shall consider stakeholder inputs when they are finalizing all processes including user interfaces, mode of data entry, storage and retrieval, output reports, queries, and the application design as a whole. Essentially it is expected that the ERPSI shall follow a SSDLC Agile framework in implementing the project establishing regular Conference Room Pilots.

9.1.9 ERPSI to suggest industry standard best practices for backing up (archiving), purging and restoring current ERP data / future new ERP.

- 9.1.10 The UAT shall be carried out in the Testing environment created. Bidder shall be responsible for setting up the Testing environment and also for creating / populating the necessary configuration data as well as master data as would be required for the purpose of UAT.
- 9.1.11 The patches/fixes shall be tested by the support team of ERPSI in Development environment and subsequently UAT will be done in the Testing environment before they are implemented in production.
- 9.1.12 ERPSI shall develop purging policy in coordination with SMFC LTD to get optimum performance of the new ERP.
- 9.1.13 In the new ERP, as per industry standard practice, for any scanned documents created by user, images shall be stored outside the ERP database in a different file server as a part of document management system and only the document link shall be available in the ERP database.

9.2 PHASES OF IMPLEMENTATION OF ERP SYSTEM

There shall be two broad phases in the implementation. Phase 1 shall be about assessment of current business process and legacy systems, gap analysis and firming up of the business functions and workflows, if necessary, through business process engineering. Phase 2 will take care of stage wise implementation of design approved in Phase 1 and conducting unit testing, system testing and User Acceptance Testing.

9.2.1 Phase 1

- Study of Business Processes Documents, reference documents prepared by functional team of SMFC LTD and prepare/update AS-IS, TO-BE and GAP Analysis.
- Study of the current implemented environment, conduct assessment of the existing and proposed business functions / Process flows, and uncovered Business requirements for which legacy systems are being continued including statutory and regulatory reporting requirements if any.
- Conduct a full-fledged assessment of the existing applications including a thorough technical and functional review of all current applications.
- To prepare & present prototypes of each of the proposed modules as part of the TO-BE (Blueprint) phase to ensure that there is no surprises for the users during UAT.

-
- ERPSI shall follow Agile Methodology for requirement study of the Business Process and through interface with all application module owners revise requirements at each sprint if all requirements cannot be identified at the outset. Functional requirements will be captured and managed in the form of user stories in pre-defined format and shall be maintained in a prioritized product backlog.
 - Compile and validate AS-IS, TO-BE and GAP Analysis in consultation with SMFC LTD. Submit & get approval of these documents Module wise. These documents will form the base documents for the subsequent phases.
 - Process mapping and mapping the best practices available with the existing business processes. Formulate business process re-engineering plan where necessary, clearly identifying the impact on current business processes.
 - Map all MIS / Dashboard / Reporting requirements and statutory reporting requirements of SMFC LTD and identify new reports that need to be customized / freshly developed in standard format (e.g. .xlsx, .pdf, .xml etc.) defined by users.
 - Define strategy for data migration from existing application databases to new ERP database, providing appropriate filters in consultation with the SMFC LTD. This includes verification of the plan with mock runs.
 - Establish industry standard policy for archiving and purging of enterprise data in the ERP environment.
 - Define desired access security and data validation controls.
 - Factoring in the above assessment inputs, create/update overall design, UAT, Configuration documents, Customized objects carried forward etc.
 - Submit architectural design as part of the SDLC deliverables. Upon approval from SMFC LTD, proceed to Phase II.

9.2.2 Phase 2


- Stage wise development and implementation of assessment Phase I as per approved design and submitted documents.
- Carry out data migration from existing application databases to new ERP database by providing appropriate filters on the existing data.

-
- Arrange Test Management Plan (Unit, System, UAT, Security testing, Load testing & Stress testing, Device-based testing across desktop/laptop/tablet/iPad/mobile devices of the ERP system.
 - Conduct Conference Room Pilot (CRP 1 & 2) including reports.
 - Conducting other testing activities, the Final User Acceptance Testing (UAT) and submission of final documents inclusive of Integration Testing results.
 - Provide basic and specialized training to the user community pertaining to their areas of work. Also, handhold and institute advanced training and capacity building measures for system administrators, technical staff, IT community regarding all aspects of technical and operational features of the new ERP platform
 - Configure various instances at local DC and Cloud as per requirement
 - Go-Live of the entire ERP. Here, on the basis of mutual agreement, module-wise Go-Live may also be considered, if Agile model of Project Management is followed. However, the milestone will be treated to have reached after Go-Live of the entire ERP applications with all modules and set-up mentioned herein.
 - Stabilization of the entire ERP system, clause 9.14
 - Warrantee Support of ERP System, clause 9.13
 - Go-Live, clause 4.3

9.2.3 Phase 3

- Support & Maintenance. This consists of operation support and maintenance of the developed ERP system as well as development/modification/improvement of the ERP system as per requirement within the broad scope mentioned in this RFP. Refer clause 9.16

Detailed approach for development, implementation & maintenance with focus on process, data, technology, people and governance

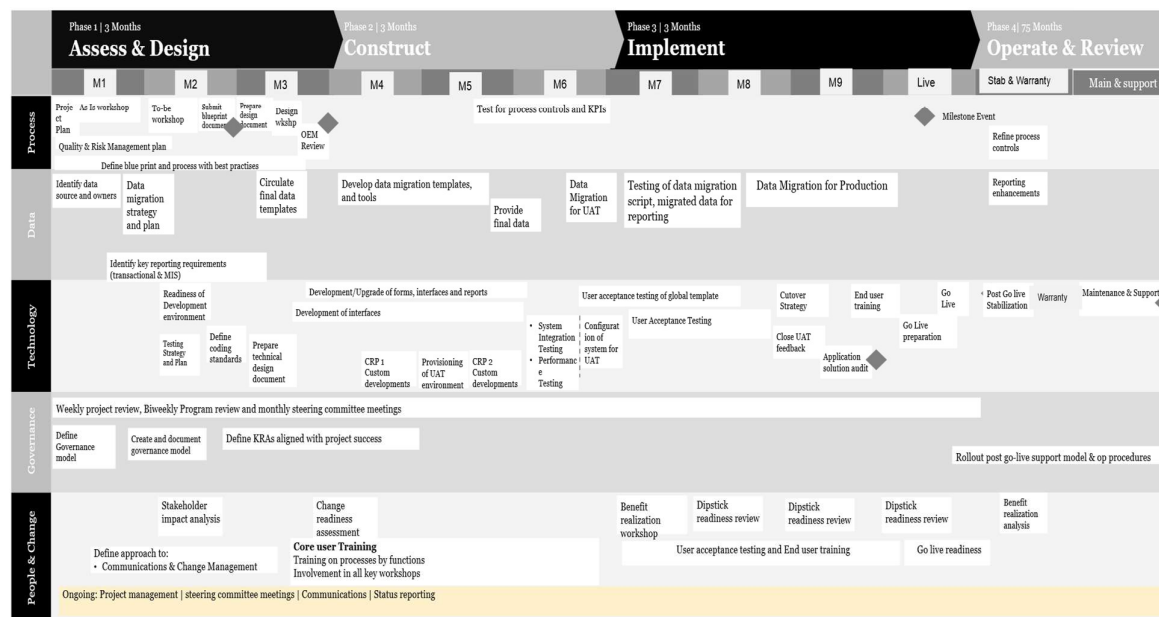

Note: Core User training to continue across all phases till Go-Live phase

9.2.4 Summary of Deliverables

The ERPSI shall handover the system with source code (latest version) of the application, licenses and other relevant documents, in hard Copy/Soft Copy (as per requirement) to SMFC LTD, as defined in Section IX.

9.3 Data Digitization and Migration

9.3.1 Data Assessment

The study of the source/legacy systems must provide comprehensive insights into the content, structure, quality, and integrity of the source/legacy systems.

Risk Identification and Mitigation Plan for Data Migration: The SI shall identify all risks associated with the data migration and enumerate mitigation measures and prepare a Data Migration Strategy enumerating the Risk Identification & Mitigation plan for Data Migration. The strategy must address the contingency measures to be adopted to address issues like incomplete/unreliable legacy data or the event of data migration failure. It must also clearly specify measures to be taken to prevent data loss. It may be

preferable to consider migration of data to a backup system at the same time as the new system to address data loss due to system failures.

9.3.2 Data Mapping and Cleaning

A comprehensive data mapping exercise must be undertaken by the SI before embarking on data migration. A good data map will detail an in-depth cross referencing of all mutual fields across the source system and the target system. It must include the following (but not limited to):

- 9.3.2.1 Names of applicable fields -to (destination) and from (source)
- 9.3.2.2 Lengths and data types of these fields
- 9.3.2.3 Mapping of relationships between entities
- 9.3.2.4 Check on the constraints, unique fields, and integrity checks
- 9.3.2.5 Any logic involved in mapping such as string truncations or validations against any business rules.

The ERPSI shall be responsible for migration of operational data as required, including financial transaction data such as ongoing contracts, employee transaction data etc.

In the event of any gaps in data migration, the SI shall discuss with SMFC LTD, document the findings, and get it approved from SMFC LTD.

- a) ERPSI shall run mock data migration tests to validate the conversion programs that have been written.
- b) ERPSI shall validate the data before uploading the same to the production environment.

The ERPSI shall support in conducting the acceptance testing and verifying the completeness and accuracy of the data migrated from the legacy systems to the proposed solution.

9.3.3 Data Migration

Data Migration refers to validation and migration of data from the manual/legacy system to the new database schema, linking and Meta tagging the documents to the relevant records in the Document Management System (DMS) and conformance to quality control requirements. The data should be migrated from the current application and media to the ERP System during roll out at all locations and prior to 'Go-Live' of the application.

The key data migration requirements include:

- 9.3.3.1 Prepare comprehensive Data Migration Strategy mentioned above and approved by SMFCL
- 9.3.3.2 Data conversion: Since there would be significant difference between existing legacy database format vis-a-vie ERP System database table structures, therefore mapping shall be done between existing tables and proposed tables and data to be made compatible for migration and migrated into new tables.
- 9.3.3.3 Perform data cleansing for incorrect/ incomplete data.

- 9.3.3.4 Perform validation of digitized/scanned records
- 9.3.3.5 Perform mock data migration exercise(s) to verify the effectivity of the strategy/plan
- 9.3.3.6 Perform final Data Migration just before go-live with audit logs
- 9.3.3.7 Perform Data Migration audit by Cert-In empaneled auditor and close all findings
- 9.3.3.8 Obtain approval from competent authority on migrated data

The tool and solutions required for performing data digitization and migration must be designed by SI after adequate study of the data to be migrated.

The SI should submit data digitization and migration strategy in their bid, detailing all the activities to be performed during the data migration. Indicative broad activities to be performed by the SI are as follows:

- a) An assessment needs to be done to identify the database requirements for the application envisaged for this project. The data requirements in terms of master data and transaction data need to be identified, which is required for the envisaged solution.
- b) Migration of complete records available in electronic form is required to be performed to acceptable quality and standards as prescribed in this RFP.
- c) Development of merged database structure
- d) Mock run
- e) Porting of all the data into the database
- f) Final updating of the single database
- g) Data Migration Audit

9.3.4 Additional Requirements for Data Migration

- 9.3.4.1 The ERPSI shall migrate the data at the implementation sites of SMFC LTD.
- 9.3.4.2 The ERPSI shall formulate the “Data Migration Strategy document” which will also include internal quality assurance mechanism. This will be reviewed and approved by SMFC LTD prior to commencement of data migration.
- 9.3.4.3 The ERPSI shall incorporate all comments and suggestions of SMFC LTD in the Data Migration
- 9.3.4.4 The ERPSI shall perform mock data migration tests to validate the conversion programs.
- 9.3.4.5 The ERPSI shall ensure complete data cleaning and validation for all data migrated from the legacy systems to the new application.
- 9.3.4.6 The ERPSI shall generate appropriate control reports before and after migration to ensure accuracy and completeness of the data.
- 9.3.4.7 The ERPSI shall convey to SMFC LTD in advance all the mandatory data fields required for functioning of the proposed solution, and which are not available in the legacy systems and are required to be obtained by SMFC LTD.

-
- 9.3.4.8 ERPSI shall conduct the acceptance testing and verify the completeness and accuracy of the data migrated from the legacy systems to the proposed solution.
 - 9.3.4.9 The ERPSI shall give the template for data migration to SMFC LTD and SMFC LTD shall furnish the required data on the templates provided by the SI. The SI shall furnish adequate guidelines to fill the data templates to SMFC LTD.

9.4 ERP System Integration

- 9.4.1 ERPSI shall ensure that the ERP system is able to share data in industry acceptable protocols and formats. The proposed solution shall be based on an open architecture and supports various types of interoperability and integration methods including viz. SOA, API, EAI, Messaging Queuing, XML based file transfer, Flat file transfer etc.

ERP System must maintain integration logs that confirm the success or otherwise of the integration interface. All external systems should be integrated with the ERP System based on a consistent, real-time or batch processing data exchange methodology operating in an automatic manner without any manual intervention unless specifically required.

The Bidder are expected to make note of the application modules that could be identified by SMFC LTD at the time of implementation.

- 9.4.1 ERPSI needs to propose appropriate middleware solution for integration between ERP System and other supporting system including but not limited to the followings:
 - 9.4.1.1 All required data residing in existing legacy applications to be identified and transferred / integrated with ERP System.
 - 9.4.1.2 End to End Integration of supplied ERP system and supporting solution with existing IT /Business Solutions and applications implemented across the value chain of SMFC LTD.
 - 9.4.1.3 Integration with any upcoming IT/Business systems at SMFC LTD like Payment Gateway, Bio-metric system etc.
 - 9.4.1.4 All interfaces should self-checking so that any exceptions or data validation errors are reported by the system.
 - 9.4.1.5 The integration middleware should be preferably use open API standard. The middleware to enable real-time and batch processing with audit logs.
 - 9.4.1.6 The Solution to be proposed as part of the bid will need to be integrated with any or all the above-mentioned application modules
 - 9.4.1.7 To ensure that the integration is seamless with other applications would also be in the scope of Bidder

-
- 9.4.1.8 Any adapters, licenses, tools, scripts etc. required for integration with the existing and upcoming IT solutions of SMFC LTD will need to be arranged by the Bidder
 - 9.4.1.9 Since all the existing IT Solutions & application modules are already in production and are business critical applications which bring in huge revenue for the SMFC LTD, it will be ERPSI's responsibility to ensure minimal downtime for integration and flawless integration which doesn't disrupt any of existing business processes or cause any revenue loss to the SMFC LTD.
 - 9.4.1.10 The integration mechanism adopted must have minimal impact on the existing systems
 - 9.4.1.11 The access to data will only be through business rules i.e., the applications will not access data directly without going through APIs managed by business rules/validation/workflow.
 - 9.4.1.12 The integration middleware/interface must validate the Data to be integrated
 - 9.4.1.13 It must maintain integration logs that confirm the success or otherwise of the interface.
 - 9.4.1.14 SMFC LTD can arrange for a session with existing the SI in case the SI need to understand any of the existing solutions and clarify their doubts.
 - 9.4.1.15 In addition to above, the development system shall have the provision to integrate with other software through standard/open API standard.

9.5 Feedback system

9.5.1 User and SMFC LTD feedback

- 9.5.1.1 The ERPSI is expected to build adequate mechanisms to get the feedback from different users of the ERP system during different stages of the project. The users/stake holders for providing their feedback will be identified by SMFC LTD.
- 9.5.1.2 The ERPSI is expected to deploy in this project the expertise and experience of similar projects carried out by them earlier. Although it is not expected that these experts will be full time on site for the project, it is expected that all the key deliverables will go through a review with these experts. Similarly, the SI is expected to deploy all the quality assurance mechanisms as per international quality standards for this project.
- 9.5.1.3 The ERPSI should clearly indicate up front what are the deliverables which will go through internal review, what type of expertise will be deployed for these reviews and what are the deliverables which will follow the quality assurance plans.
- 9.5.1.4 If any of the deliverables are not acceptable to SMFC LTD or its appointed experts, it will have the right to seek deployment of experts from the SI to review the deliverables.

9.5.2 Mechanism to adopt feedback

There are two types of feedback for the deliverables – from the users/stake holders and from the internal experts of the ERPSI. The following is expected from the ERPSI on the feedbacks.

-
- 9.5.2.1 All the feedback will be discussed with SMFC LTD and based on guidance from SMFC LTD, will be incorporated into the project
 - 9.5.2.2 Since the feedback for any rework is by nature correcting the inadequacy of quality of the work produced in the first place, SMFC LTD will not accept any change notice requests for these modifications
 - 9.5.2.3 The ERPSI has to build adequate mechanisms to control the risks of time over runs possibly due to effort required to rework bad quality deliverables
 - 9.5.2.4 The ERPSI has to indicate in the beginning and during the start of each phase how it plans to take feedback and the mechanisms to incorporate the feedback into the project plan and deliverables

ERPSI will report to SMFC LTD on how the feedback have been incorporated into the project deliverables and take a sign off from the designated authority of SMFC LTD.

9.6 IT Security/Cyber Security Audit/Information Systems Audit

Annual Audit of the newly developed ERP system will be conducted by SMFCL for Information System, IT security and Cyber security practices by CERT-IN certified Third-party agency to assess and evaluate the implementation of security policy and vulnerability assessment, including the top 10 OWASP vulnerabilities. The report shall include the parameters as per the agreement with SMFC LTD and rate the security implementation in three grades i.e., Satisfactory, Requires Improvement and Unsatisfactory.

- 9.6.1 Security Audit/Information Systems Audit shall include but not limited to input validation and authentication, vulnerability assessment, penetration testing, application security assessment, application assessment for entire infrastructure.
- 9.6.2 Third party agency shall be responsible for implementation of information security controls and perform periodic assessment.
- 9.6.3 It shall propose ways to enhance the protection of ERP System & supporting cloud/ IT Infrastructure.
- 9.6.4 Secure Configuration Review: Third Party Agency shall review the security configuration of ERP System and provide the detailed report that include the recommendations for remedial actions.

9.7 Follow-up Audit

Post completion of audit assessments (Internal or external) may have the findings that require corrections and corrective action by the bidder/SMFCL. Since most of the corrective actions cannot be performed at the time of audit. SMFC LTD may require a further follow-up audit to verify that corrections were made, and corrective actions were taken.

SMFC LTD may also conduct various regular audits to assess and ascertain the system and the infrastructure of the ERP system is efficient, secured, performing as per need and also for opportunities for improvement.

9.8 Reporting

The SI shall generate all reports from ERP necessary to run the organization. Further, the SI shall provide the necessary support and co-operation for overall monitoring of the ERP System. For purpose of monitoring the SI shall provide the system generated reports with a provision of further detailed analysis, if required.

9.9 Security Requirements and Features

9.9.1 General security

The ERPSI will have to establish all the necessary procedures / technology / personnel to ensure that the ERP System Security is not compromised.

Broad Security requirements, which are nor exhaustive, are:

- 9.9.1.1 The entire project should follow globally accepted SSDLC (Secured Software Development Life Cycle) standard.
- 9.9.1.2 The Security features should be compliant with the e-Governance Security Guidelines (e Gov Security Standards Framework (www.egovstandards.gov.in), [National Cyber Security Policy \(NCSP 2013\)](#) and [NCIIPC Guidelines](#) All systems should have integrated security features that are configurable by the system administrator to control access to the application, functional modules, transactions, and data.
- 9.9.1.3 The applications should require the use of unique user IDs and passwords for authentication purposes and digital signatures, Biometric and other devices as applicable. Password should comply with the standard.
- 9.9.1.4 Application will have module wise and role-base access control security features i.e. there should be configurable control for access of modules including remote access (through Internet/VPN) (some modules can be accessed through internet and some sensitive modules will be restricted for access on Intranet or via VPN).
- 9.9.1.4 The application should allow for the following:
 - i. The enforcement of password standards
 - ii. The establishment of a specified period for password expiration, and
 - iii. The prohibition of recent password reuse
- 9.9.1.5 System administrator should be able to define functional access rights and data access rights by assigned user ID, functional role, and owner organization.

-
- 9.9.1.6 The systems should permit the system administrator to assign multiple levels of approval to a single user.
 - 9.9.1.7 System administrator should be able to restrict access to sensitive data elements by named user, groups of users, or functional role.
 - 9.9.1.8 System should be auditable as per requirements from time to time.
 - 9.9.1.9 System should have audit logging capability to record access activity, including the following:
 - i. All log-in/log-out attempts by user and workstation
 - ii. User-submitted transactions
 - iii. Initiated processes
 - iv. System override events; and direct additions, changes, or deletions to application-maintained data
 - 9.9.1.10 System should provide the ability to query the audit log by type of access, date and time stamp range, user ID, IP address and terminal ID.
 - 9.9.1.11 All the data / information contained within systems or in hard copies related to this project, are owned by SMFC LTD. No information should be made public either directly or indirectly nor allowed to be accessed by unauthorized persons.
 - 9.9.1.12 System audit should be enabled for all the modules to establish detective controls. System should have evidence, like audit trails, logs, registers, proof of background checks, approvals from SMFC LTD or its designated agency, support for various decisions, support for accounts etc. for the purpose of third- party security audit.
 - 9.9.1.13 There is need to have view only roles for all critical modules to provide access to statutory / other auditors.
 - 9.9.1.14 Should have system development and change control procedures including effective segregation of duties and environment.
 - 9.9.1.15 Should have a business continuity plan and a disaster recovery plan that should be implemented before commencement of the operations. Robust backup procedures should be established for the same.

9.9.2 Security during Development & Integration Phase:

The SI shall meet the security requirements listed below (including but not limited to) during the development and integration stage:

- 9.9.2.1 The SI shall address emerging cybersecurity vulnerabilities in their software coding under Secured System Development Life Cycle (SSDLC). This should be done by taking into consideration the SANS Top 25 Most Dangerous Programming Errors and the OWASP Top 10 Projects.
- 9.9.2.2 The SI shall propose a legacy data cleansing approach.

- 9.9.2.3 The SI shall propose a security mechanism to be used for API and adopt the best practices such as OWAPS guidelines to ensure security.
- 9.9.2.4 The SI shall promptly notify SMFC LTD when vulnerabilities are found in their code.
- 9.9.2.5 The SI shall apply security related patches and updates.
- 9.9.2.6 Remote access by the SI will only be performed using technology authorized by SMFC LTD.
- 9.9.2.7 Any data interfaces implemented or built by the SI will be required to have encryption and authentication (strong authentication when possible.)
- 9.9.2.8 Files containing SMFC LTD information will be transferred using encrypted file transfer techniques agreed upon by both parties.

9.9.3 Security during Operations phase

9.9.3.1 Security Policy

SI will adopt leading information security framework (such as ISO 27001, ISO 22301, ISO9001) to define, monitor and update security policies (including network, server, application, and website/mobile app security).

9.9.3.2 Incident Response

SI shall do the analysis of application and network incidents, do post-incident reporting, and implement practices to ensure rapid response to attacks.

The SI shall do a proactive review of incident response plan to improve incident response time and implement continuous improvement process to strengthen overall effectiveness of security.

9.9.3.3 User Authentication and Control

- ERPSI shall define and implement highest level of access governance. The proposed of this solution is to have an enhanced user role security where access should be restricted to only authorized users with multi-factor or two-factor authentication.
- The system should have access control features for controlling the access rights over the system and over the various functions/features available for different types of users. Best practices from enterprise security including password strength, password aging, password history, reuse prevention etc. must be followed for access control.
- Application user authentication and authorization related transactions should be encrypted and used a wide array of authentication schemes, standards, or token types to ensure that only valid users and applications get access.

9.10 Security Audit

The SI shall engage with the Cert-IN empaneled agency appointed by SMFC LTD for conducting security related to overall ICT infrastructure. The SI will cooperate fully with the auditor. The auditors shall be responsible to conduct the following activities:

- 9.10.1 Security Audit that includes (but not limited to) vulnerability assessment, penetration testing, application security assessment API testing and Mobile application assessment biannually (once in six months) for entire infrastructure.
- 9.10.2 Implementation of information security controls and perform periodic (once in a year) assessment.
- 9.10.3 Propose ways to enhance the protection of ERP System & Supporting IT Infrastructure.
- 9.10.4 Ensure the applications are free from OWASP Top 10/SANS and CERT-IN web/mobile application vulnerabilities as released from time to time.
- 9.10.5 SI is responsible for mitigating all security risks found related to its Scope. All high-risk vulnerabilities must be mitigated within 15 days from the date vulnerabilities are formally identified.
- 9.10.6 Frequency of all audit exercises mentioned in this RFP are subject to change as per policy of SMFCL.

9.11 Training Requirements

The primary objective of the training is to achieve 100% user adoption through technical and behavioral competencies covering all end users of SMFC LTD. Training shall be provided in both Second Language & English Language as required, mostly in Second Language to Field Staffs. The SI shall propose detailed training plans (including training curriculum and calendar) so that there is a proper transfer of knowledge about the deployed ERP systems to SMFC LTD staff.

The audience of the trainings shall vary for each type of training. The end user training for various ERP System Modules and Other associated systems shall be for the users of the respective modules of the system. The SI shall provide training sessions to all employees from lower level to higher level including officers from SMFC LTD on the domains as finalized during implementation.

9.12 Change Management

SMFC LTD considers implementation of ERP will have significant impact on its business processes and people. Effective change management activities will be required to ensure that SMFC LTD employees are aware about the ERP Project and the change in work practices. The ERPSI will be required to carry out activities as part of change management initiatives by focusing on the change management and capacity building approach and plan so as to be able to tackle the issues that might

arise due to introduction of new processes or major change of the ERP system. ERPSI will also prepare and propose detailed change management process defined in subsequent sub-sections for this purpose.

9.12.1 Change Management training

Introducing radical reforms has to be necessarily accompanied by efforts to energize and orient the mindsets of the people – both within and outside the department. For instance, the SMFC LTD staff should be skilled to operate and work in a significantly newer and different way. A well-calculated and well-designed strategy has to be followed for the people to be trained to work effectively in the new environment. It is necessary to formulate a change management plan with appropriate interventions for capacity building, training, and stakeholder communications. A successful Change Management Program will ensure:

- 9.12.1.1 A smooth transition to the new way of working
- 9.12.1.2 The organization/people support the changes implemented
- 9.12.1.3 Individuals know how the changes affect them and the role they have to play
- 9.12.1.4 Stakeholders to understand the benefits of the changes and internalize it
- 9.12.1.5 The new system and its underlying concepts are understood
- 9.12.1.6 People are aware of how roles and responsibilities are changing
- 9.12.1.7 Everyone is motivated and committed to the change program
- 9.12.1.8 The success and progress of the program is monitored and measured
- 9.12.1.9 Key Change Management Implications
- 9.12.1.10 The implementation of a new ERP system, SMFC LTD will have several change implications emanating from the following changes:
 - 9.12.1.11 Process and procedural (introduction of completely new process and systems emanating from the need of changing core functional information flow and not defined in the existing scope of work)
 - 9.12.1.12 Technical and technological (introduction of new technologies for enabling the new /unaddressed business requirements)
 - 9.12.1.13 Organizational (complete change of existing organizational structure and redefined roles and responsibilities)

9.12.2 Change Management Plan for support

ERPSI will also formulate a comprehensive Change Management Policy to carry out enhancements, new requirement and major change in the existing process. Also, all change requirements within the broad scope of this RFP document will be carried out without any price impact. Change requirement which is completely outside of the scope shall be termed as 'New Requirement' and will be executed on extra charge basis.

9.12.3 Change Management Process

- 9.12.3.1 Requirement initiated by user department
- 9.12.3.2 IT department/SI mutually assess the request and categorize type of requirement. If the requirement is within the scope, proceed with Within Scope Change Management. Else proceed with Out-of scope Change management.
- 9.12.3.3 If routine requirement, small changes, bug fixing, regulatory requirement, requirement within broad scope of work of this RFP, **OR** any new requirement which requires maximum 15 man-days effort will be put under AMC/Warranty Support else categorize the requirement under 'Out-of Scope Change Management'
- 9.12.3.4 Out-of Scope Change Management may have price impact. The effort estimate for such development will be decided mutually by SI/SMFCL.
- 9.12.3.5 If there is no amicable decision, issue will be escalated to GM(IT) in charge of IT. Decision of GM(IT) shall be final in this case.
- 9.12.3.6 This process will be in force during entire period of Go-Live stabilization, warranty & AMC support phase.
- 9.12.4 Change Management expense
 - Under no circumstances, the sum total of all change management expenses will exceed 25% of the total contract value.

9.13 Stabilization Support phase

- 9.13.1** Post Go-Live monitoring
- 9.13.2** Hand holding support / operation support / feedback handling
- 9.13.3** Knowledge transfer
- 9.13.4** Configuration tuning
- 9.13.5** Data Validation & Migration Check
- 9.13.6** Document finalization
- 9.13.7** Prepare for the next phases, warranty & AMC.

9.14 Warranty Support phase

- 9.14.1 Commences only after completion of stabilization phase for all modules
- 9.14.2 Bug fixing and defect resolution
- 9.14.3 Enhancement within and out of Scope as per Change Management process
- 9.14.4 Help Desk (on-site) & Operational support (on-site/remote)
- 9.14.5 Patch updation
- 9.14.6 Performance monitoring
- 9.14.7 System health checks
- 9.14.8 Documentation updates
- 9.14.9 Knowledge transfer

9.15 Go-Live phase

Please refer clause 4.3 of this document.

9.16 Annual Maintenance Support (AMC)

Broad Scope of Work, tentative and not limited to, during the AMC phase is narrated below:

- 9.16.1 Management of both production systems at both PDC & DRC. Data refresh to other instances as and when required. Remote support during office hours on week-days.
- 9.16.2 Bug fixing and troubleshooting of the developed software
- 9.16.3 Maintenance of the developed ERP software for small and minor changes, parameter setting, configuration changes, refresher training, training to the technical users etc.
- 9.16.4 Development/Modification/upgradation of developed ERP Software for statutory changes, company policy/practice changes, limited to the broad scope of module as specified in tender document and/or in SRS document.
- 9.16.5 Responsible for renewing all required licenses under the scope until the end of the AMC period.
- 9.16.6 However, implementation of new modules/processes may be considered by SMFCL on extra charges basis (based on man day charges as quoted) through Change Management process. Decision of SMFCL with regards to “New Process” or “Modification of existing process” will be final and binding on ERPSI.
- 9.16.7 Major enhancement, new development out of the scope of this RFP, through change management process
- 9.16.8 Compliance to all statutory & SMFCL policies
- 9.16.9 All software should be supplied with applicable OEM warranties and support (including back-to-back) for the entire duration of the project. During warranty period vendor must provide updates and patches.
- 9.16.10 Annual Technical Support (ATS), if any, will start from the date of acceptance of the installation. ATS should cover 24 by 7 escalation supports from OEM for all software products to be provided through Phone, Email or Onsite visit depending on the criticality and nature of the problem. The support must be ensured by the ERPSI.
- 9.16.11 The ERPSI must carry out any requisite adjustments / changes in the configuration for implementing different versions of the application software.

- 9.16.12 The ERPSI shall provide & update from time to time any Updates/Upgrades/New releases/New versions of the software & Data Base, free of cost, as and when released, through planned outages of the production system.
- 9.16.13 The ERPSI shall provide and apply regular patches to the licensed software including software, operating system, databases, and other applications.
- 9.16.14 The ERPSI shall provide for software license management and control. ERPSI shall maintain data regarding entitlement for software upgrades, enhancements, refreshes, replacements, and maintenance. The SI must perform periodic audits to measure license compliance against the number of valid End User software licenses consistent with the terms and conditions of site license agreements, volume purchase agreements and other mutually agreed upon licensed software terms and conditions and report to SMFC LTD on any exceptions to SERPI's terms and conditions, to the extent such exceptions are discovered.
- 9.16.15 The ERPSI shall manage complete OEM technical support for all the licensed software problems and/or questions, technical guidance, defect, and non-defect related issues. The ERPSI shall provide a single-point-of-contact for software support and provide licensed software support including but not limited to problem tracking, problem source identification, problem impact (severity) determination, bypass and recovery support, problem resolution and management reporting etc.
- 9.16.16 The ERPSI shall undertake regular preventive maintenance of the software. If the Operating System or additional copies of Operating System are required to be installed / reinstalled / de-installed, the same shall be done as part of ATS.

9.17 Project Management

9.17.1 Project Management

The entire Project management phase includes Understand, Design, Develop, Supply, Install, Configure, Commission (Go-Live) and Stabilize (includes hand holding) the Integrated ERP system and is to be completed within a period of **12 Months**. The Project Support and Maintenance phase includes maintenance of the live operation of the Integrated system, enhancement, troubleshooting, training, change management, patch management, incident management, SLA management, audit & closure etc. for a period of 6 years (this includes 1-year warranty at the beginning), which may be extended for a further period of 3 years on mutually acceptable Terms & conditions.

9.17.2 Project Timelines

- 9.17.2.1 The ERP System Integrator (SI) is expected to follow the schedule as mentioned in below table. Each of the phase activity should be accompanied with a presentation on the deliverables by ERPSI.
- 9.17.2.2 The submission of deliverable will be considered complete only after the submission of hard/soft copy of the deliverables and presentation by ERPSI.
- 9.17.2.3 The ERPSI must submit a detailed project implementation plan during or immediately after the Kick-off meeting, including but not limited to the below mentioned project phases and list of deliverables that would be delivered during the project implementation.
- 9.17.2.4 The table gives a set of high level of activities and corresponding expected timelines; which SMFC LTD envisions to be required as a part of this project. The ERPSI should use this list only as an indicative guideline expected in terms of activities. The ERPSI is required to furnish detailed information regarding each step of activities proposed during and after the implementation of the project.
- 9.17.2.5 System Integrator shall supply all licenses as per the schedule suggested by ERPSI and accepted by SMFC LTD.
- 9.17.2.6 The Project activities shall be carried out in a hybrid Agile model as per following:
- 9.17.2.6.1 Agile for: Each phase viz, AS-IS, TO-BE, Development, Testing, Deployment, incremental development & Deployment during AMC
- 9.17.2.6.2 Stage gates: Kick-off/Mobilization/Charter. Approval - UAT, Security readiness/Compliance, Cut-over readiness, Final Go-Live, Stabilization, Warranty & AMC support commencement.
- 9.17.2.6.3 The project activities and timelines (In Months) as mentioned in the table below is the schedule by which the required project activities shall be completed with corresponding and required deliverables. (Where, T – Date of issue of Work Order to the ERPSI)

Detailed break-up of the project activities

Project Phase	Project Activity	Timeline (Months) T=Date of Issue of Work order
Project Initiation	1. Project Kick Off 2. Team Mobilization	T+1

/ Business Blueprint ing	3. Signing of agreement including SLA & Change Management	
	4. Project Charter a) Detailed project plan with work breakdown structure along with dependencies b) Resource schedule & deployment plan c) List of complete deliverables d) Project Governance structure & escalation matrix e) Stakeholder communication matrix f) Project management templates such as Project reports, SLA monitoring, Attendance etc. g) Detailed survey to Identify End User Base, License Requirement, Network Communication Feasibility study, Change readiness Assessment etc.	
	6. Training & Organization change management strategy & schedule.	
	7. Data Conversion and Migration Strategy	
As-Is phase	1. Understanding the existing business processes a) Process manual & circulars b) Discussion c) Requirement gathering workshop d) As-Is report including existing business processes, workflows, report requirements, process maps etc. e) As-Is phase Sign-off	T+8
To-Be phase (Blue- Print)	2. Gap Analysis report with identified gaps and areas of improvement a. Business Blueprint/design documents. (High Level Design & Low-Level Design) b. Business Process Master List (BPML) c. Business Process Re-engineering d. Reporting, Interfaces, Conversions, Enhancements e. FRS & BPML mapping document f. Updated Technical Requirement Specifications g. Requirements Traceability Matrix h. Non-functional Requirements Specifications Documentation i. ERP Module based Roles & Responsibilities (Authorization Matrix) etc. j. Mapped Organogram of SMFC LTD	T+8

	k. Presentation of module-wise prototype to SMFCL 1. To-Be phase sign-off	
Development phase	1. Setup of Test & Development Environment 2.. Development of the proposed ERP Solution-module-wise	T+8
Testing phase	1. Develop test plans 2. Set-up Quality Assurance environment 3. Conference Room Pilot (CRP)-1 4. Integration Testing (CRP-2) 5. Interface testing with legacy systems, if any 6. Train Core team members and technical users 7. User Acceptance Testing (UAT) 8. Incorporation of UAT changes 9. UAT phase sign-off	T+8
Go-Live phase	9.17.2.6.3.1.1 Security Audit 2. Go-Live Strategy 3. Finalization & creation of role-based End users of ERP system 4. ERP System Performance testing 9 All instances set-up 10 Closure of all UAT & Audit observations 11 Drafting of policies 12 Establishment of DR set-up, DR replication and backup/restore mechanism 13 Data Migration from Legacy system, if any 10. ERP Go-Live 11. Training to end-users 12. Tuning of ERP System 13. Demonstration & Acceptance	T+9
Stabilization phase	1. Handholding support 2. Stabilization Support	T1=T+12
Warranty	Warranty support (1 year)	T1+12
Support phase	Maintenance, support, improvement, training, audit assistance & closure	T1+72

Note:

1. *The Project timelines and schedule mentioned above are exhaustive*
2. *Initially, the ERPSI will provide a draft version of the respective deliverables to SMFC LTD for review and feedback within stipulated timelines. Final version will be submitted after incorporating the feedback/suggestions.*
3. *Feedback and revision of documents and deliverables will be an iterative process.*
4. *ERP infrastructure including platform for both PDC & DRC will be provided by SMFCL. However, the requirement for the same will be provided by the ERPSI after the Business Blue print stage. Initially SMFCL may provide local infra for carrying out development, unit & integration testing.*
5. *The SI will sign and execute a Tripartite agreement between SI, the PDC & DRC service provider and SMFCL for segregation of roles & responsibilities, compliance of various parameters and also to fix accountability and responsibility in relation to ERP system testing & operation, maintenance, DR management, risk mitigation & issue resolution.*

9.18 Implementation Approach

The implementation of the Modules would be either Big Bang or phased in progressively, covering successively different geographies and user groups. A summary of the Approach for Implementation shall be as per project timelines mentioned in this contract. This final approach shall be decided during implementation after blue-print phase. However, switching over approach are not allowed.

9.18.1 Project Management Plan

The SI is expected to follow the Project plan. Each of the milestones should be accompanied with a presentation on the deliverables by the SI, related to that milestone.

The submission of deliverable will be deemed complete after the final submission of the hard / soft copy of the deliverable and the presentation by the SI.

The SI shall follow prudent project management practices commensurate with the best international standards during the project implementation. While the actual process of application customization will remain an internal activity of the SI, it is important that SMFC LTD or their nominated agencies shall have adequate visibility into such processes.

The following are some of the major guidelines to be kept in mind for Project Management.

9.18.2 Scope Management

The requirements shall be collected and documented clearly. The scope and requirements shall be controlled against a baseline and any changes shall be communicated to SMFC LTD and documented.

9.18.3 Time Management

The SI shall prepare a detailed project schedule conforming to the stake-holder expectations and exercise stringent control of the schedule. A periodic report on the progress and deviations should be shared with SMFC LTD. Any schedule conflicts with respect to project and/or deliverable timelines will be presented by SI in the Steering Committee and to be approved by the Committee. Thereafter the approved timelines will have to be adhered to by the SI, unless specified otherwise.

9.18.4 Quality Assurance and Quality Control

A detailed Quality Assurance Plan shall be prepared and shared with SMFC LTD. The same shall be monitored and SI shall share a periodic report on the quality activities. These shall include:

- i. Architecture and Design Review Reports
- ii. Test Plans Review Reports
- iii. Test Execution Review Reports

9.18.5 Project Risk management

The SI shall document the risks during implementation and share the same with SMFC LTD. This shall be periodically reviewed and shared with SMFC LTD. A report on the periodic risk analysis, risk responses planned, mitigation strategies executed shall be shared with SMFC LTD.

The SI shall store all the Project Management and Delivery artifacts into a secure configuration database and give access to SMFC LTD for view purposes. During the O&M period, any change requests and enhancements to the software shall be similarly documented so as to create a comprehensive repository of all artifacts relevant to SMFC LTD stakeholders. This will serve as a valuable knowledge input during Exit Management and for any statutory audit.

9.19 Project Governance

Putting a governance structure around SMFC LTD's future ERP implementation plan is essential to ensure that project implementation stays on track and achieves its strategies, objectives, and goals. It acts as a mechanism to measure the progress of the implementation. Also, IT systems today are subject to many regulations such as governing data retention, confidential information, financial accountability, and recovery from disasters. An IT governance framework is an efficient system to ensure regulatory compliance.

Overall responsibility for the implementation of all modules will remain with the ERPSI. Regular Project progress review and monitoring will be the responsibility of PMU during project implementation phase. SMFC LTD will appoint a Single Point of Contact (SPOC) for co-ordination. Escalation of all issues during maintenance will be through this SPOC, who will also be responsible for SLA management. During the project implementation phase, supervision and reporting will be responsibility of ERPSI.

i) Steering Committee for ERP project

Steering Committee needs to be formed consisting of top management who will drive the project and will monitor the overall progress of project. The Steering Committee should monitor the project regularly and preferably once in a fortnight or monthly review.

Role
• Providing Organization Direction for ERP Project. • Review and making decision on Scope, Budget, and Operating Model for ERP Project. • Measure progress against Objectives, milestones, and deliverables etc. • Monitoring the overall progress and clearing bottlenecks of ERP implementation • Monitor financial status by actual spend, and estimated remaining spend compared to budget • Considerations, approval, and authorization of resources (staff, computer facilities etc.), project plans, and revisions to plans as appropriate • Strategic Realignment and setting course correction in case of deviations • Approve cost escalation and scope changes.

ii) ERP Project Management Office, manned by ERPSI PM team

Role
• Co-ordinate between ERPSI development team & functional users • Manage the project on day-to-day basis • Review and manage the project plan • Present regular reports to the steering committee • Monitor and control project progress • Assist ERPSI in Business process understanding by co-ordinating with functional users • Facilitate Study and design of To-Be processes (Business Blueprint) • Coordinate for data preparation, validate and certify the master data for data upload into ERP system • Act as change management agent and assist the end users in adaption of the system • Assist Functional Teams, Module Lead, and IT teams as required. • Assist in training of the end users • Assist in testing of ERP system • Co-ordinate Sign-off activity and processing of payments.

v) SMFC LTD IT Department

The I.T. team shall ensure all the technical aspects of the ERP project such as Hardware/Cloud, Software, Network infrastructure, Data centre requirements etc.

Role
• I.T. team is responsible for preparation of RFP for procurement of Cloud/ hardware, Network & Security Infrastructure, Data centre/cloud for hosting ERP software in consultation with ERPSI. • I.T. team shall assist Project manager for timely completion of the project. • I.T. team shall ensure integration of existing software with ERP software, wherever possible. • I.T. team shall assist in testing and training, • I.T. team shall track, monitor, and resolve the issues raised by end users during ERP implementation. • I.T. Team shall deploy suitable resources to take handover of IT task (Server, DB, Network, Security etc.) after completion of project duration. • I.T. team shall assist Project Manager for sign-off of documents and arranging payment. • Any other work assigned by Project Manager

vi) SMFC LTD ERP Core Team

Role
• Owner of respective ERP module • Assist the ERPSI in coordination with respective functional teams for Preparation of AS-IS study • Assist ERPSI in understanding and documentation of Business processes. • Review and sign-off the respective As-Is document for respective module • Review and Sign-off To-Be processes (Business Blueprint) for the respective module • Conduct UAT and sign-off • A point of contact between respective functional team, I.T team and System Integrator (ERPSI). They shall act as bridge between SI, I.T team and respective Functional module teams. They are responsible for below: ○ providing information & data required by ERPSI ○ convincing ERPSI regarding procedure/system and Regulations currently followed by SMFC LTD ○ Co-operate with SI in development and complete implementation of respective module in coordination with functional team ○ Acquiring the knowledge about implementation process of ERP, such as customisation of software, designing and generation of user defined Reports etc.

Role
○ Clarification of doubts raised by end users and assisting in using functional aspect of software to users ○ Arranging interactions with respective Team and SI as and when required. ○ Reporting the progress of implementation, to respective Functional team leaders and I.T team on daily basis. ○ Reporting the complications that may crop up during the implementation, to team leaders and shall make all efforts for solving such complications in coordination with functional team and I.T team. ○ Imparting Training to the end users ○ Assist in testing of the ERP system ○ Coordinate for data preparation, validate and certify the master data for data upload into ERP system ○ Any other work assigned by Contact Person (IT).

9.20 Minimum Resource Requirement from ERPSI

SI should ensure deployment of required specialized and experienced manpower throughout the execution of the project for successful implementation & stabilization of the ERP System in time.

9.20.2 Initial Composition, Full Time Obligation; Continuity of Personnel

9.20.2.1 The SI shall ensure that Key resources required for project execution and management devotes substantial working time to perform the services to which that person has been assigned.

9.20.2.2 The SI shall not make any changes to the composition of the Key Resources or request any member of the Key Resource to cease or reduce his or her involvement in the provision of the Services during the Term (or agree to any request other than from SMFC LTD that would have the same effect):

9.20.2.2.1 unless that person resigns, is terminated for cause, dies, is long-term disabled, is on permitted mandatory leave under Applicable Law or retires; and

9.20.2.2.2 The person's experience is no longer required for the project further; and

9.20.2.2.3 Without SMFC LTD's prior written consent. The clauses of non-disclosure agreement shall always operate in any such case.

9.20.2.3 The Bidder needs to submit detailed CVs of each of the resource and Project Manager of the proposed project team. The Project team provided by the SI must be on their regular roll and SI shall certify the authenticity of their regular employment.

9.20.3 Before ERP System Go-Live phase

SI shall deploy the Project Manager (Project In-charge) including Technical, Functional Experts and Other Support Staff at the identified project location during the implementation and roll out of ERP System.

9.20.4 Post ERP System Go-Live, up to stabilization phase

SI shall deploy the Project Manager (Project In-charge) including Technical, Functional Experts and Other Support Staff at the identified project location during the post Go-live and Facility Management Support Phase.

9.21 Support & Maintenance phase

SI will provide remote support as per SLA.

9.22 Documentation and Deliverables

To ensure that the proposed ERP System & overall solution conforms to the requirements, specifications and delivery schedule, the SI shall submit the documentation and deliverables for review and approval by SMFC LTD.

The SI shall obtain the approval on the relevant deliverable at each stage of project before proceeding for solution purchase, provisioning, deployment, testing, roll out, training etc. at SMFC LTD.

As part of ERP implementation, the SI shall submit all required deliverables as necessary for successful completion of project and required by the purchaser.

9.22.1 Deliverables Acceptance Procedure

The acceptance procedure of deliverables & overall solution for ERP system shall include:

- Initially, SI will submit a draft version of each deliverable for review and feedback within stipulated timeframe.
- SMFC LTD will provide feedback within the agreed timeframe to make necessary change corrections (if required).
- SI shall submit the final version of the documents/deliverables after incorporating all feedback.

9.22.2 Key Deliverables

The indicative list of project deliverables which are required to be submitted by the SI shall include, but not limited to the following:

Project Phase	Key Deliverables	Frequency
Project Initiation	10 Project Kick-off with presentation on ERP System overview to Senior Management. 11 Agreement	Once

Project Phase	Key Deliverables	Frequency
	12 Project Charter. a) Detailed project implementation plan with work breakdown structure along with dependencies b) Resource schedule & deployment plan c) List of complete deliverables d) Roles & responsibilities	Once
	13 Detailed training/Organization change management strategy & schedule	Once
	14 Data Conversion and Migration Strategy	Once
As-Is	15 As-Is Study sign-off report including existing business process, workflows, reporting requirement, process maps etc.	Once
	15.22.1.1 Gap analysis report with identified gaps & areas of Improvement.	Once
Business Blueprinting	15.22.1.2 Requirement gathering workshops with Updated requirement specification document	Once
	15.22.1.3 Detailed To-Be sign-off report including: a) Business Blueprint/design documents. (High Level Design & Low-Level Design) b) Updated Bill of Material/Bill of Quantity c) Business Process Master List (BPML) d) Business Process Re-engineering e) Development Scope: Reporting, Interfaces, Conversions, Enhancements f) FRS & BPML mapping document g) Business Solution Design Document h) Updated Functional Requirement Specifications i) Updated Technical Requirement Specifications j) Requirements Traceability Matrix k) Non-functional Requirements Specifications Documentation l) ERP Module based Roles & Responsibilities (Authorization Matrix) etc. m) Mapped Organogram of SMFC LTD	Once

Project Phase	Key Deliverables	Frequency
	n) List of role-based End users of ERP system,	
	16 Business Continuity/Disaster Recovery Planning Report	Once
	17 Release Management and Change Management Strategy Document	Once
	18 Training & Handholding Activity	Once
	19 Refined Data Conversion and Migration Strategy	Once
	20 Change Management Workshops	Quarterly
	21 Business Blueprint/Elaboration phase closure report	Once
Design & Development	1. ERP System – Technical Design Document	Once
	2. ERP System – Functional Design Document	Once
	3. Configuration documentation	Once
	4. Documentation on ERP User Profiles and Roles	Once
	5. Test and Development environment	Once
	6. ERP System – Testing Report (Load, Stress, Integration, Performance Etc.) a) Test Plan, b) Roles & responsibilities, c) Test Scripts, d) Issue log, e) Issue Resolution Report	Once
	7. ERP System Integration with Existing Solutions (Legacy, Other Systems)	Once
	8. ERP System – Integration Test Report	Once
	9. Quality Assurance System	Once
	10. Conference Room Pilot (CRP) Report	Once
	11. Approved End-User Training Strategy (along with End-User Training Curriculum, Manuals, and Schedule)	Once
	12. Trainings to Core Team/Nodal Officers	As per training plan

Project Phase	Key Deliverables	Frequency
	13. ERP System implementation & rollout strategy	Once
	14. User Acceptance Testing (UAT) Sign-off Report	After software and hardware delivery and implementation
	15. Documentation for Customization of RICEFW (Reports, Interface, Conversion, Enhancements, Forms and Workflow) Development Objects	Once
	16. Data Archiving Plan	Once
	17. Refined End User's training plan	Once
	18. Comprehensive module-wise User Training Manual, FAQ etc.	Once and with changes
	19. Training attendance and feedback analysis report	Per training
	20. Video-based training material for self-learning	Once
ERP System – Go-Live & Stabilization Support	1. Cut-over Communication Strategy	Once
	2. Draft ERP System audit report with observations (2 nd Iteration)	Once
	3. Final ERP System audit report with compliance (2 nd Iteration)	Once
	4. Pre-Go-Live Assessment Report	Once
	5. Enterprise-wide Go-live completion report	Once
	6. ERP system – Source code	Once
Enhancement, Maintenance & support	1. System Performance Report (SLA compliance)	Monthly
	2. Monthly activities report (including Issue tracker, Helpdesk ticket analysis, Change Request status and Status of all service requests logged with Offered OEM Product etc.)	Monthly
	3. Solution usage reports - transactions and users	Monthly
	4. User Manual with necessary revision.	Once
	5. Change Management & Release Management Reports	Monthly
	6. Issue log and resolution report	Monthly
	7. ERP System – Source code (Latest version)	As & when required and at Exit
	8. ERP System – Data Dump	

Project Phase	Key Deliverables	Frequency
	9. Revised Exit Management Plan	Once

Note:

- The Project deliverables mentioned above are indicative and shall be finalized based on discussion and agreement between System Integrator and SMFC LTD
- SI will provide respective deliverables as per the captured schedule for their review and feedback of SMFC LTD
- SMFC LTD will provide feedback, wherever necessary, within the agreed timelines to make necessary changes, corrections, if required. SI will be required to resubmit the revised deliverables.
- Feedback and revision of documents and deliverables will be an iterative process.

9.23 The documents conventions should as per ISO and/or CMMi standard.

9.24 End-User Documents

Documentation will be supplied and maintained by SI during the project. The ownership of all documents, supplied by SI, will rest with SMFC LTD. The electronic copies shall be submitted along with all the paper documents and manuals, required for operating and configuring the system. The documents provided must include at least:

- 9.24.1.1 User Manual (both online and paper copies) providing detailed instructions on how to use the ERP. In addition, it describes how to access, submit inputs to, and interpret outputs from the application
- 9.24.1.2 System installation guide including the configuration of the supplied infrastructure.
- 9.24.1.3 Module wise - ERP Application Training Manuals

9.25 Technical Documents

The documents including but not limited to are:

- 9.25.1 Product installation and configuration steps
- 9.25.2 Application access procedures
- 9.25.3 User screen layout and content
- 9.25.4 Transaction entry procedures
- 9.25.5 Batch job setup, processing, and recovery/restart procedures
- 9.25.6 Error codes with full descriptions and recovery steps
- 9.25.7 Standard report layout and content
- 9.25.8 Internal processing controls
- 9.25.9 Application security
- 9.25.10 Operating specifications and system flowcharts

- 9.25.11 Database entity relationships, table formats, and data element descriptions; and Program module descriptions
- 9.25.12 Quality Assurance Plan Documenting the planned and systematic pattern of all actions necessary to assure confidence that the software developed will conform to the SMFC LTD functional and technical requirements.
- 9.25.13 Interface Control Document - Documenting the interface characteristics of one or more IT systems and document the Integration & interface agreements between interface owners. It contains information on both physical and data element requirements that are necessary to make the transfer of information between systems feasible.
- 9.25.14 Test Plan Containing information on the software test environment to be used for independent testing, the test cases to be performed, and the overall testing schedule. This includes methodology, schedule, resources, tools, procedures, environment definition, test cases, and software test results.
- 9.25.15 Systems Manual Detailing the data structure, table, forms, and report structures.
- 9.25.16 Installation and maintenance manual for the servers and other hardware
- 9.25.17 Operations Manual providing instructions for installing the application, troubleshooting, interpreting message logs, and FAQs
- 9.25.18 Trouble Shooting Guide/ Handbook for Helpdesk which describes the various trouble shooting methods.

9.26 Roles and Responsibilities

9.26.1 Responsibilities of the SMFC LTD

A designated person of SMFC LTD (Project Manager) shall act as the nodal point for the implementation of the Contract and for issuing necessary instructions, approvals, commissioning, acceptance certificates, payments etc. to the ERPSI.

The SMFC LTD shall:

- Assist ERPSI with all necessary information, documents & circulars during As-Is phase.
- Approve and sign all sign-off documents required for project progress within 15 (fifteen) working days from the date of submission of such documents.
- Review and approval of ERPSI's Project Plan.
- Provide all necessary approvals required during the period of agreement. However, SMFCL reserves the right to ask for clarification and modification before giving such approvals or deny in case of non-conformance.

- Facilitate entry of all operating personnel and for working on all facilities that would demand such presence.
- Participate in periodic review meetings as per the project governance structure and shall support with the required interventions requested;
- To appoint Nodal Person from each functional department and form a Cross-functional Core team and notify to ERPSI of the names and contact details
- Release payments to ERPSI as per agreed terms;
- Facilities to be provided by SMFCL:
 - Providing required details of existing Legacy system and any other Systems which are required for Integration.
 - Arranging any meeting or workshop with the Legacy Application Owners or Vendors.
 - Necessary sitting space with adequate facilities be provided by SMFC LTD at Corporate Headquarters. However, this shall be limited to sitting space and associated infrastructure & Desktop System of normal configuration as being used in SMFCL for max 05 people. All tools and software environments necessary for development shall be the responsibilities of ERPSI.

9.26.2 Responsibilities of the ERPSI

- Preparation of Detailed Project Plan
- Primarily responsible to adhere to the plan and successfully execute the scope of work as specified in this in this RFP. The same should be prepared in consultation with SMFC LTD.
- Deliver all deliverables mentioned in this RFP
- Coordinate with SMFCL as and when required for successful execution of the project
- Arrange, prepare, present in the review meetings
- Meet the defined SLAs for the performance of the system.
- On-going maintenance support, upgrades, and enhancements of the solution (including 3rd party components as applicable)
- Ensure training material for trainers to train the other users of SMFC LTD as mentioned in this RFP
- Delivering training for SMFC LTD employees
- Data Digitization and Migration as mentioned in this RFP document
- During the maintenance phase the responsibility of overall system and version control will continue to be vested with ERPSI only and should not be outsourced
- Provide onsite handholding as mentioned in this RFP document

- Analyzing & managing system performance, network performance, call logs, etc., as well as providing the means of monitoring the SLA metrics
- Providing Help features on the Application Modules that can be used by stakeholders such as Frequently Asked Questions (FAQ), etc. including various tests and audits as mentioned in this RFP
- Any Other as mentioned in this RFP document

9.26.3 RACI MATRIX

R – Responsible, A – Accountable, C – Consulted, I – Informed

Srl	Project Activity	ERPSI	OEM	SMFCL
1	Understanding of Project	R,A		C,I
2	SRS	R,A		C
3	SRS Sign-off	C,I		R,A
4	Design Blue print & Gap Analysis	R,A		C,I
5	Design Blue print Sign-off	C,I		R,A
6	Supply of products, Licenses	R,A		I
7	Acceptance of Products, Licenses	R,C	R,A	R
8	Legacy systems, sitting space, core team	I		R,A
9	Installation of Products, Licenses	R,A	C	C,I
10	Development	R,A		C
11	Unit Testing	R,A		C
12	Integration Testing	R,A		C
13	UAT	C, A		R, A
14	Closure of observations	R,A		C,I
15	UAT Sign-off	C		R,A
16	Configuration of ERP Set-up	R,A		C,I
17	Data Migration	R,A		C
18	Go-Live	R,A		R,C
19	Stabilization	R,A		
20	Framing and complying policies, procedure etc.	R,A		
21	Issue of Go-Live Acceptance Certificates	I		R
22	AMC Phase	R,A		
23	Issue of Project Completion certificate	I		R
24	License Management	R,A		A

25	Payment	A,C,I		R,A
----	---------	-------	--	-----

9.27 Sub Contract

ERPSI shall be allowed for sub-contracting however the approval of SMFCL shall be taken prior to engage any sub-contractor. SMFCL at its discretion may limit the quantum of sub-contracting. ERPSI shall ensure that the selection of Sub-contractor is done based on past performance and technical skills.

9.28 Project Implementation Methodology

The methodology to be deployed by the SI to implement the ERP system will have different work elements and activities.

All these activities and the work elements should coherently focus on achieving the following key results

- Quality of the solution deployed
- Customer satisfaction while deploying and during usage
- Successful implementation in terms of completeness and timely accomplishment of the outcome

While there are different techniques and tools available as part of the methodology, the following are expected to be part of the implementation methodology to be adopted by the SI

- 9.27.1 Workshops with different stakeholders for capturing business requirements, creating awareness of best practices, communicating the changes, building consensus on process design, for signing off the deliverables etc. These need to be organized at different intervals and in different places throughout the duration of the project as demanded by the context.
- 9.27.2 Stakeholder consultation other than workshops, with those stakeholders who will be identified by SMFC LTD, for the purpose of critical inputs, review, suggestions, process description etc.
- 9.27.3 Review sessions with different stakeholders for signing off the deliverables, walking through the deliverables for facilitating quick understanding
- 9.27.4 Internal review mechanisms of SI for ensuring the quality as per QA strategy of the solution and the deliverables
- 9.27.5 Adoption of the review comments - effective mechanisms to adopt the changes suggested
- 9.27.6 Documentation of proceeding – recording the developments, discussions, deliverables, using standard methodology and native tools available with the ERP system
- 9.27.7 Work standards/practices for documentation, configuration, testing, data migration etc.
- 9.27.8 Training different stake holders on a continuous basis

SMFC LTD reserves the right to get the project be reviewed at each stage including deliverables by an external consultant.

9.27.9 Commissioning and Support Services

Follow among other option, the Agile model for implementation

9.28 Configuration

Configure at least 5 instances viz, Production, Staging, Testing, Development and DR. The production system shall be a single instance; centralized installation servicing the entire organization. The ERP system will be installed at the locations identified by SMFC LTD.

Based on the approved Business Design Document, the SI will undertake the development. After completion of development, ERP system will be installed along with tools with proper configuration for testing, Go-Live etc. If needed or/and the result is not up to the expectation of SMFC LTD, further reconfiguration will be done by the SI in order to close any gap left in meeting the desired objective.

All work including development should be carried out in a controlled and planned manner with adherence to ERP prescribed coding standards and naming conventions. The SI needs to provide configuration, customization, and installation documents to SMFC LTD.

9.29 Testing

As part of testing, the SI shall cover all activities during the implementation process (configuration of business processes, development such as conversions, interfaces, reports) which prove that system settings are correct as per business requirement of SMFC LTD. In doing so, the SI shall include test plans, tests cases, and testing report.

The SI shall create the test strategy document that defines the requirements and goals of ERP configuration, determines the tools and methods used to check that the system responds correctly, determines how and when the test will be performed and recommends how the approval process should occur.

The test strategy document shall guide the project team through the implementation to ensure that planning and conducting testing activities in the various phases of ERP implementation as mentioned below.

9.29.1 Development Testing

The SI shall after development and configuration of the ERP system, conduct tests to demonstrate that the system meets all the requirements (functional and Non-Functional) specifications as brought out in this RFP and would be in accordance with the procedures detailed in the approved process document.

The development testing shall cover testing of:

9.29.2 Unit testing of individual modules

9.29.3 Conversions

9.29.4 Code walkthrough

9.29.5 Review of Data Base design

9.29.6 Reports

9.29.7 Testing to be carried out by the SI in association of the IT team to make sure that the test results are correct and reflect the business processes defined in the Business Blueprint Design.

9.29.8 After development unit testing is completed, all customer-specific programs and forms shall be included in the Final Integration Test

9.29.9 Integration and System Testing

The purpose of the Integration Test shall be to plan and execute the integrated components, including simulation of live operations, and analyze the results, important for the functional verification of the production system and to give necessary level of confidence that the solution is complete and will perform the processes.

Integration testing shall be accomplished through the execution of predefined business flows, or scenarios, on cross-functional integration points, as well as end-to-end business processes, which emulate how the system will run the processes of SMFC LTD. These business flows, using migrated data from the pre-existing systems, if available or by creating sample data, shall be performed in an integrated module environment. Integration testing shall be completed in two iterations:

9.29.9.1 The first iteration (Integration Test) shall concentrate on testing all important business processes inside the ERP system, starting with touch point scenarios, and ending with end-to-end-scenarios. It will be done by SI's functional consultants. Customer specific development like user-exits and transactions and authorizations and user roles would also be tested in the Integration Test.

9.29.9.2 System Testing, as a second iteration, shall focus on the most important cross-enterprise scenarios with touch points to external components, including testing of conversions, interfaces, reports, and the necessary authorizations. It will be conducted by SMFC LTD users with the guidance of project operations committee.

9.29.9.3 These selected cases will be combined to represent a business process flow such as a revenue cycle or a material acquisition cycle. Problems encountered during these efforts also need to be tested under an integrated environment.

9.29.9.4 Load and Stress Testing

Load, scalability, and stress testing would be conducted prior to commissioning & Go-Live once the System Integration testing of the configured and customized solution has been conducted successfully. The SI will device the test keeping in view SMFC LTD's projected future load of transactional users as proposed by SMFC LTD.

9.29.9.5 User Acceptance Testing (UAT)

During this activity, UAT team of SI will work directly with SMFCL Business & IT teams. The SI will develop Acceptance Test procedures and the same will need to be approved by relevant

stake holders of SMFC LTD. The purpose of this acceptance is to ensure conformance to the required process operations response time, the integrity of the application after installation, and to eliminate any operational bugs. This will include:

- 9.29.9.5.1 Fine tuning of the application, ensuring all required related component software are installed and any debugging required.
- 9.29.9.5.2 SI shall conduct all tests as a part of Standard Software Testing Life Cycle (STLC)
- 9.29.9.5.3 SI shall facilitate SMFC LTD or its nominated agencies to conduct User Acceptance Testing, Application Security testing (vulnerability testing and penetration testing) and Infrastructure Security Testing.
- 9.29.9.5.4 SMFC LTD shall nominate a team to carry out acceptance testing of all developed ERP modules.
- 9.29.9.5.5 SI shall provide training to the Acceptance Testing team prior to the commencement of the acceptance testing of system.
- 9.29.9.5.6 SI shall setup testing environment at the hosting facilities
- 9.29.9.5.7 SI shall provide necessary tools for logging of defects and carrying out testing if required.
- 9.29.9.5.8 SI should provide detailed sample test scripts for carrying out the acceptance test of various systems supplied.
- 9.29.9.5.9 SI shall resolve all the defects/issues identified by SMFC LTD's acceptance testing team during solution acceptance procedure/phase.
- 9.29.9.5.10 The software would be re-tested to ensure closure of identified defects/issues.

9.30 Data Migration

After the UAT is completed, ERP system will be installed in the staging area. Legacy data will be extracted from the legacy system, if any, transformed and uploaded top the ERP System and verified as per the process mentioned under section 9.

9.31 Cutover and Go-Live

The scope of Cutover would be for each of the core and support processes. The Cutover Strategy needs to detail the sequence of activities required to achieve this and propose drawing up of a schedule for the tasks, dates, data conversion and the upload of the necessary balances and open items into the system before the Final Go-Live. The key requirements for Cutover are as follows:

- 9.31.1 The Cutover plan should detail the strategy by which the data will be uploaded for the different modules and the nature and volume of backlog transactions. Specified forms/formats/templates to put the data in.
- 9.31.2 It should detail the Data elements and open item strategy logic used for planning Cutover before Go-Live.

9.31.3 It should describe the various pre-requisites and assumptions used for each of the data elements before uploading in the live system.

9.31.4 It should detail the various business decisions to be taken collaboratively by SMFC LTD and SI for finalizing the Cutover strategy.

SI then install the ERP system at the Primary Data Centre and Disaster Recovery Centre, configure all parameters, upload/create master data, upload all other data and make the system live for operation from the cut-over date.

SMFC LTD will consider Final Go-Live date of the ERP system once the SI has completed three (3) months of Stabilization Period after the successful rollout of the ERP system for all modules as per scope of this project. SMFC LTD shall issue the “Go-Live Acceptance Certificate” on following acceptance criteria:

- a. Error free operation and running of all ERP modules with real-time data during the Stabilization Period at all the SMFC LTD locations.
- b. Closure of all observation raised during the testing, review, audit exercises
- c. Resolution of all ERP System related issues (Not limited to software application, Data Center & Disaster Recovery Center)
- d. Documentation of all issues/problems that come up during the stabilization support period and resolution methodology / solutions

The following table will be used to ensure compliance to all the activities prior to the Final Go-Live Stage before issuing the ‘Go-Live Acceptance Certificate.’ The ‘Go-Live’ shall be done only after acceptance of UAT.

Sl. No.	Project Activities	Compliance (Yes/No)
1.	Unit Testing	
2.	Execution of System Integration Testing	
3.	Execution of System Perform Testing (Stress, Load, Disaster Recovery, Backup Tests etc.)	
4.	ERP Software Provisioning & Installation	
5.	ERP System Installation on Cloud Infrastructure	
6.	User Acceptance Testing (UAT)	
7.	Completion of Data Digitization (manual data for all modules)	
8.	Completion of Data Migration (for all modules) a) Master Data (Employee, Material, Vendor etc.)	

Sl. No.	Project Activities	Compliance (Yes/No)
	b) Transactional data (Stock Balances, Opening Balances, Contracts, Projects, Assets, Employee etc.)	
9.	End User Creation with defined roles & authorization	
10.	ERP System Accessibility to all End Users	
11.	Completion of advance ERP System Configuration	
12.	Finalize Cutover (Conversion) Plan	
13.	Successful Completion of End-User Training (Rollout locations)	
14.	Tuning of ERP System	
15.	Successful Completion of Stabilization period after ERP-System Rollout	
16.	Error free operations and running of all ERP modules with real-time data for a period three (3) months.	
17.	Documentation of all the issues/problems that come up during the stabilization period and resolution methodology / solutions	
18.	Go-Live Approval	

The system is considered 'Operational' and Payments will be released for Go-Live phase after the SMFC LTD has issued the 'Go-Live Acceptance Certificate' to the ERPSI.

The support-cum-maintenance phase will commence once the certificate is issued. The SMFC LTD will also issue the 'Project Completion Certificate' post the completion of the FMS period as defined in this RFP.

9.32 Post Go-Live Stabilization Support

The SI shall provide post Go-Live support, as part of this scope, by continuing the deployment of the same technical and functional consultants at site for full three months after Go-Live. During the stabilization period the SI would correct any errors/bugs incurred while executing transactions, generating reports, handholding for one financial quarter closure. The SI will update the user manuals and configuration manuals accordingly.

9.33 DR-Drill activity

9.33.1 As part of operation support, SI will take active role in configuring the system for taking backup and also for application & data replication at the DR site. The bidder will also participate in conducting DR-Drill of the ERP system along with other stakeholders, as per defined frequency.

The drill is to be conducted within defined frequency as well as within the RTO & RPO parameters defined as per outcome of the BIA exercise conducted in due course.

9.33.2 As part of the exercise and documentation, the following reports will be generated:

- 9.33.2.1** DR-Drill Plan
- 9.33.2.2** Dr-Drill plan execution report
- 9.33.2.3** Exception report during the DR-Drill activity
- 9.33.2.4** Security and Log exception report
- 9.33.2.5** System Performance report
- 9.33.2.6** Database Recovery Report
- 9.33.2.7** Network and Connectivity report
- 9.33.2.8** Application Recovery report
- 9.33.2.9** RTO & RPO related compliance reports

9.34 Additional Non-Functional Requirements for ERP Implementation (NFR)

The requirement for ERP Implementation which the SI will be responsible for are as follows:

- 9.34.1 The solution should support multitier architectures.
- 9.34.2 System architecture should allow infrastructure simplicity and standardization.
- 9.34.3 The ERP software should be compatible with different hardware.
- 9.34.4 The system should support latest Windows OS & Data Base versions and provide compatibility to future versions
- 9.34.5 All SMFC LTD components must be maintained such that corrective and preventive maintenance can be performed on the system without affecting the entire working of the system.
- 9.34.6 The system should be so configured that in case of down of the PDC, operation continued from DRC as per defined RTO & RPO.
- 9.34.7 The ERP system to be developed and configured to provide an acceptable application response time defined as; for financial transaction: < 2 sec, for non-financial transaction: < 5 sec, for reports: < 1 min.
- 9.34.8 The architecture should be proven to be highly scalable and capable of delivering high performance as and when the transaction volumes increase.
- 9.34.9 The system should provide application architectures that are highly granular and loosely coupled. The solution architecture design should promote flexible business process management for future scalability. The solution should be interoperable in nature and design and development should be based on Service Oriented Architecture (SOA).
- 9.34.10 The system should be so designed to cover all business processes and provide modularity to support addition / removal of one or more modules as and when required. However, these modules should

be seamlessly integrated to the Apex Accounting system. The solution architecture should allow minimum modifications to preserve the upgrade path.

9.34.11 The system should support standard interfaces such as adapters, APIs to interface with other and legacy applications.

9.34.12 The system should support real-time data updates and interfaces with software from other vendor.

9.34.13 The system should be compatible to remote access integration.

9.34.14 Bidder to also consider compliance of guidelines issued by statutory bodies like RBI/CERT-In/MEITY/SEBI etc. listed below but not limited to:

9.34.15 RBI Advisory No. 2/2024 dated January 31, 2024, for Guidelines for Secure Application Design, Development, Implementation & Operations issued by CERT-In.

9.34.16 RBI Master Direction RBI/2023-24/107 DoS.CO.CSITEG/ SEC.7/ 31.01.015/ 2023-24 dated November 7, 2023.

9.34.17 RBI Master Direction RBI/2023-24/102 DoS.CO.CSITEG /SEC.1/31.01.015/2023-24 dated 10-Apr-2023 - Master Direction on Outsourcing of IT Services.

9.34.18 RBI Master Direction for NBFC-Scale Based Regulation 2023, RBI/DoR/2023-24/105-DoR.IN.REC.No.45/03.10.119/2023-24 dated 19-Oct-2023.

9.34.19 Cert-IN guidelines on Information Security Practices for Government Entities dated 30-06-2023

9.34.20 RBI advisory on web App accessibility standard, CO.DOR.BCG.No.56988/01-01-028/2025-2026 dated 10.12.2005

9.35 Exit Management and Knowledge Transfer

9.35.1 Purpose and Objective

Exit Management is enforced either at the end of expiry of contract period or pre-mature termination mentioned in this document. At the time of exit, the ERPSI will be required to provide necessary handholding and transition support including all information as may be necessary and reasonable to effect as a seamless handover as practicable in the circumstances to SMFCL.

This Exit Management Framework (the “Framework”) provides a standardized, comprehensive structure for managing transition activities at the end of any IT related project (software, infrastructure, security) implementation, support, hosting, or managed services contract.

The objectives of this Framework are to:

- Ensure a *structured, controlled and risk-free transition* at the end of contract lifecycle or upon termination.
- Prevent SI lock-in, operational disruption and unforeseen financial exposure.
- Define roles, responsibilities, timelines, deliverables, and processes essential for transition to a new SI or to in-house operations.

- Ensure compliance with SMFCL's IT Governance, Business Continuity and Data Ownership policies.

9.35.2. Scope of Exit Management

The ERPSI, after issue of work order, shall prepare an Exit Management Plan for transfer of operations to SMFCL, in the event of termination or expiry of contract with SMFCL, without affecting services to stakeholders adversely. The ERPSI shall get this process approved by SMFCL. The Exit Management Plan shall include, but not be limited to, the following:

- a) A detailed plan of the transfer process that could be used in conjunction with a replacement SI including details of the means to be used to ensure continuing provision of the services throughout the transfer process or until the cessation of the services and of the management structure to be used during the transfer.
- b) Plans for communication with such of the replacement ERPSI, OEM, and any related third party as are necessary to avoid any material detrimental impact on Project's operations as a result of undertaking the transfer.
- c) Plans for provision of contingent support to SMFCL/Replacement vendor for a reasonable period after transfer.
- d) The ERPSI shall review the Exit Management Plan annually to ensure that it is kept relevant and up to date. Each Exit Management Plan shall be presented to and approved by the Competent authority at SMFCL.
- e) During the Exit management period, the ERPSI shall make its best efforts to deliver the services.
- f) The first Exit Management plan shall be furnished by the ERPSI in writing within 15 days from the date of signing the contract.

This Exit Management Plan shall apply in the following scenarios:

- i. Completion/expiry of contract period or termination as per scope of contract.
- ii. Termination by SMFCL for convenience, breach, or performance issues.
- iii. Termination by the ERPSI pursuant to contract conditions.
- iv. Migration to a successor system, vendor, platform or cloud environment.
- v. Organizational decision to internalize operations.

The Framework covers:

- All IT related projects having estimated budget / contract value of ₹50 lakhs and above
- Associated modules, integrations and customizations.
- Cloud infrastructure, hosting environment, databases, backup systems.
- Third-party tools, licenses, configurations and scripts.

- Knowledge repositories, documentation and artefacts.
- Define acceptable formats:
 - Data: CSV / SQL dump
 - Documentation: editable formats (Word, Excel, Visio, PPT)
 - Diagrams: Visio, PDF
- Explicit rejection of image-only or proprietary-locked formats.
- Support services, ticketing history and operational logs.

It may be noted that all the activities mentioned here-in is an indicative list, any other activity, over and above these, as may be deemed necessary by SMFCL at the time of actual exit, are also required to be performed by the ERPSI at no additional cost.

In the case of closure or termination of the project, the parties shall agree at that time whether, and if so during what period, the provisions of this schedule shall be applied. The Parties shall ensure that their respective associated entities will carry out their respective obligations set out in this Exit Management Schedule.

9.25.3. Exit Management Governance Structure

9.35.3.1 Exit Management Committee (EMC)

SMFCL shall constitute an EMC comprising:

- Director-in-charge of IT (Chair)
- IT head
- Representative / Head of IT Security - CISO (as applicable)
- Project Manager - Convenor
- Representatives from Business /Legal /HR /Finance/Risk
- ERPSI's Exit Manager and technical SPOCs

9.35.3.2 Responsibilities of EMC

- Review and approve Exit Management Plan submitted by ERPSI.
- Monitor progress during notice and transition period.
- Validate artefacts, handover materials and data completeness.
- Certify readiness for final switchover.
- Approve financial closure related to exit.
- Mandatory escrow (code / configs / credentials) for critical systems.
- To recommend an alternate support mechanism if ERPSI ceases operations.

9.35.4 Exit Planning and Trigger Mechanism

9.35.4.1 Exit Notification

- ERPSI shall submit a detailed Exit Plan *within 15 days* of contract signing.

- Upon notice of termination/expiry, Exit Management plan shall automatically be invoked and put in place.

9.35.4.2 Exit Period

- Standard exit period: 90 days (extendable by SMFCL).
- ERPSI shall continue providing all services during exit period without degradation of operation performance.
- Mandatory Annual/half-yearly review and update of the Exit Plan.
- Update triggers on:
 - Major version upgrades
 - Addition of modules/integrations
 - Change in hosting model or cloud tenant

9.35.5 Roles and Responsibilities

9.35.5.1 ERPSI Responsibilities

The ERPSI shall:

- a) Ensure uninterrupted services during the entire transition period.
- b) Provide complete data migration support, including extraction, cleansing and transformation.
- c) Hand over all documentation, including:
 - Technical design documents
 - SRS, FRS, configuration manuals
 - Complete version management registry (including Custom code, extensions and deployment scripts, Interfaces)
 - Integration and API specifications
 - Test cases, UAT results and validation artefacts
 - Security configurations, role matrices and audit logs
- d) Provide source code and related repositories for all customizations developed for SMFCL.
- e) Transfer of all licenses to SMFCL name, provide all license related documents, subscription keys, expiry dates and dependencies.
- f) Provide environment details for staging, production, DR and backup setups.
- g) Transfer operational knowledge through structured sessions.
- h) All policies, procedures, SOPs, guidelines etc. related to the project under its control.
- i) All user-id and password being used by the ERPSI.
- j) Provide a transition support team with defined SLAs.

- k) Support the new ERPSI during on boarding without additional cost unless otherwise agreed.
- l) Comply with SMFCL's data security, BCP and confidentiality requirements during transition.
- m) Signatory to the final Exit Completion Certificate.
- n) Explicit alignment with:
 - o RBI IT Outsourcing Guidelines
 - o Government cloud (Mehran / MEITY) norms, if applicable

9.35.5.2 SMFCL Responsibilities

SMFCL shall:

- Provide access to infrastructure, users and documentation necessary for exit.
- Facilitate joint sessions between outgoing and incoming teams.
- Ensure timely decisions for cut-over.
- Ensure financial settlement subject to satisfactory completion of exit obligations.
- Signatory to the final Exit Completion Certificate.

9.35.6. Handover Requirements

9.35.6.1 Data Handover

ERPSI shall provide:

- Complete application databases in industry-standard formats along with complete version repository.
- All raw, processed and derived datasets.
- Metadata, schemas, dictionaries and relationship diagrams.
- Complete transaction logs for last 36 months.
- DR copies, backup archives, snapshots.
- Data validation reports.
- Interface codes

9.35.6.2 Application Handover

- Source code of custom modules.
- Build and deployment pipelines.
- Configuration parameters.
- User manuals and training content.

9.36.6.3 Infrastructure Handover

- Cloud architecture diagrams.

- VM specifications, storage mapping, firewall rules.
- Tenancy documentation (if applicable).
- Backup schedules, retention policies, DR test reports.

9.35.7. Knowledge Transfer (KT)

ERPSI shall conduct structured KT comprising:

- Functional KT for modules and business processes.
- Technical KT for architecture, integrations, system administration.
- Hands-on sessions for key business users and IT staff.
- Updated training videos, PPTs and process documents.
- Support KT covering ticketing procedures, common issues and troubleshooting guides.
- Minimum two-level knowledge transfer.
- Prohibition on single-point operational dependency.
- Mandatory documentation in SMFCL-controlled repositories.

KT must be signed off by SMFCL with quantified assessment.

9.35.8. Transition to New Incoming Vendor / Internal Team

ERPSI must:

- Work jointly with incoming vendor.
- Provide shadow support for minimum 30 days post-cutover.
- Ensure no service disruption during parallel run.
- Transfer credentials securely and revoke its own access after sign-off.
- Share system health reports and monitoring dashboards.
- Fix exit-related defects at no cost
- Provides support until SMFCL signs NDA with new vendor

ERPSI is prohibited from:

- Obstructing knowledge flow.
- Withholding artefacts or credentials.
- Degrading quality of service during exit period.
- Enforcing restrictive licensing or proprietary lock-ins.

9.35.9. Final Exit Deliverables Checklist

A comprehensive Exit Completion Report must be submitted containing:

- Data migration completion certificate

- System documentation pack
- All licenses and OEM certificates
- Source code and repository handover confirmation
- Credential and access transfer log
- Training completion report
- DR and backup handover report
- Pending defects log with severity and mitigation steps
- Certificate confirming removal of SMFCL data from ERPSI systems
- Assist in closure of audit observation, if any, during the notice period.
- Non-Disclosure and IP compliance certification

Exit will be deemed complete only after EMC approves the Exit Completion Report.

9.35.10. Financials and Cost Structure

- Exit support cost is deemed included in the contract unless explicitly stated.
- Any payment due to the outgoing ERPSI shall be made on pro-rata basis to the tune of last set of completed services/deliverables, subjected to the approval and compliance on contractual and SLA terms & conditions.
- Any additional cost (if mutually approved) must follow transparent rate cards.
- Final payment to ERPSI will be made only upon fulfilment of all exit obligations.
- Release of PBG/Security, if any, only after signing of Exit Completion Certificate. else the same will be forfeited.

9.35.11. Compliance, Audit and Legal Requirements

- ERPSI shall comply with SMFCL's all IT related policies including IT Security Policy, BCP/DR Policy and Data Ownership Policy.
- ERPSI shall permit SMFCL/audit authorities to audit exit-related artefacts.
- Breach of Exit Management obligations shall attract penalties and may impact ERPSI eligibility in future tenders.
- Confidentiality obligations continue *beyond* contract termination.
- ERPSI to ensure:
 - Third-party exit obligations mirror primary contract
 - No sub-contractor IP or access blocks exit
- Written confirmations from key OEMs, wherever applicable

9.35.12. Risk Management & Continuity Provisions

- Maintain service availability throughout exit period.
- Ensure data integrity and zero data loss.
- Document all open risks with mitigation plans.
- Provide interim operational support if new ERPSI on boarding is delayed.

9.35.13. Exit Timeline Template

Stage	Description	Timeline
Stage 1	Formal initiation and submission of detailed Exit Plan	Day 1–15
Stage 2	Data and documentation handover; KT Phase 1	Day 16–45
Stage 3	Joint working with incoming vendor; KT Phase 2	Day 46–75
Stage 4	Cut-over preparation, shadow support	Day 76–90
Stage 5	Final Exit Report and Sign-off	By Day 90

9.35.14. Intellectual Property (IP) & Data Ownership

- All data, metadata, configurations, customizations and deliverables created for SMFCL shall be SMFCL's exclusive property.
- ERPSI shall ensure no proprietary locks are embedded in custom development.
- ERPSI shall delete all SMFCL-related data from its owned systems after final sign-off.

9.35.15. Confidentiality & Access Management

- ERPSI shall disable all user accounts and access related to it on completion.
- Provide detailed access revocation list.
- Ensure total compliance with SMFCL's cyber-security protocols.
- Ensure statement on:
 - Tenant ownership
 - Subscription transfer
 - Admin rights handover
 - Billing account migration

9.35.16. Penalties for Non-Compliance

Non-compliance with Exit Management obligations may result in:

- Withholding of payments.
- Payment will be made after deduction of penalties charges as per SLA
- Invocation of performance bank guarantee.
- Blacklisting from future SMFCL procurements.

- Legal action as per contract terms.

9.35.17. Conclusion

This Exit Management section ensures structured closure of technology engagements, continuity of operations and full protection of SMFCL's strategic IT assets. It directly addresses the deficiencies noted by audit authorities, ensuring future ERP and IT contracts incorporate clear, verifiable and enforceable Exit Management obligations.

9.36 Payment Terms

The payments to the ERPSI shall be strictly made based on acceptance and quality of deliverables, performance and timelines of services delivered by the System Integrator.

9.36.1 No advance payment shall be made.

9.36.2 All payments shall be made, subject to deduction of applicable TDS (Tax deduction at Source) and any other taxes as on the payment date, in INR only.

9.36.3 Payments shall be made after adjustment of any penalty, accrued during that phase of the implementation.

9.36.4 All bills/invoices should be submitted to SMFCL. The decision of Competent Authority, SMFCL shall be final and binding on the bidder.

9.36.5 Price shall remain fixed during the entire contract period. There shall be no increase in price for any reason whatsoever. Therefore, no request for any escalation of the cost / price shall be entertained.

9.36.6 Payment shall be released within 30 days of raising of proper invoice along with all relevant documents and after delivery of concerned deliverables and after providing all clarifications raised by SMFCL.

9.36.7 Payment terms up to Go-Live, Stabilization and Warranty (Sum (Serial 1-3) of Price Format 2, Page 110

9.36.7.1 Payments shall be made in Indian Rupees and after submission of relevant performance security in form of bank guarantee and verification of the same from issuing bank.

9.36.7.2 In case the item(s)/service(s) are covered under the scope and no separate line-item is provided in the Price Format, the same shall be deemed to be included in Contract price, and nothing shall be paid on account of that. Similarly, if any item(s)/service(s) are not covered under Scope, however, are essential for successful operation of the ERP system, the same shall also be deemed to be included in Contract price.

9.36.7.3 All relevant proof of successful provision of services duly signed by the concerned officer by SMFCL, Performance Bank Guarantee (if any) etc. to be submitted by the successful bidder for processing payment.

9.37 Stage wise completion of project and payment schedule (up to Go-Live, stabilization and Warranty) (Refer Serial 1-3 of Price Format 2, Page 110):

	Module/Stage of implementation	Stage of Implementation	% of quoted development cost (Sum (Serial 1,2,3,10) format-2, Section-VIII)
1	Accounting Modules	Go Live. Issuance of certificate	15
2	Fixed Assets		
3	Employee Related Modules	Go Live Issuance of certificate	15
4	Loan related Modules	Go Live Issuance of certificate	30
a.	Loan Origination System		
b.	Technical Loan Appraisal		
c.	Loan Accounting & Management System – Assets		
d.	Loan Payment Control System – Liabilities		
e.	Payable Controls		
f.	NPA Management		
g.	Legal Module		
h.	Asset Liability Management		
i.	Credit Risk Management		
j.	Compliance & Dash Board		
k.	KYC Module		
l.	Credit Rating Module		
5	Other modules		
a.	Payable control	Go Live	10

		Issuance of certificate	
b.	Vendor Portal		
c.	Customer Portal		
d.	Inventory Management		
e.	Grievance Portal		
f.	Reports / MIS		
g.	Mobile Apps		
h.	Website development and Go-Live		
7	Data migration, integration of all modules and Final Go-Live	Issuance of Certificate	10
8	Completion of Stabilization phase	Issuance of Certificate	5
9	Completion of warrantee	Issuance of Certificate	15
	Total		100

9.37.1 Post successful completion of above activities, a certificate shall be issued by SMFC LTD to start the Facility & Support Management Services (AMC phase).

9.38 Penalty Clause up to Go-Live, stabilization & warrantee:

9.38.1 A penalty of 0.5% of project implementation cost (Serial-1 of Format-2 Section-VIII) shall be levied for each week of delay of Go-Live (up to stabilize)

9.38.2 The total penalty charges shall be capped at maximum 10% of total project cost.

9.38.3 Initially, ERP instances will be created on the on-premises Data Center system and then UAT & production will be shifted to the cloud hosted environment.

9.39 Payment during AMC period (Sum (Serial 4-8), Price Format 2, Page 110)

9.39.1 AMC Payment will commence after expiry of warrantee.

9.39.2 Payment shall commence after submission of 2nd Performance Security equivalent to the yearly average value of the AMC cost quoted by the bidder in the price-bid valid for 5 years + 6 months.

9.39.3 Bidder will raise invoice along with monthly performance report as SLA

9.39.4 Payment shall only be done on quarterly basis, at the end of each quarter, on proportional basis of the concerned year AMC cost (= AMC cost quoted for the year / 4)

9.39.5 Payments shall start after completion of following activities which includes but not limited to:

9.39.5.1 Dues verification and acceptance of completed work and services.

9.39.5.2 Issue of Concerned certificate from SMFC LTD.

9.39.5.3 Successfully running the ERP system during the Stabilization phase.

Note: The payment shall be made in the following manner:

- *The agency shall submit all the Key deliverables and services to SMFC LTD as per the contract agreement.*
- *Agency shall submit SLA compliance sheet for the quarter concerned generated from the SLA tool*
- *The completion of work and services shall be verified by SMFC LTD designated technical committees*
- *Payment shall be made after due verification and acceptance of completed work and services and issue of completion certificate from the SMFC LTD.*
- *Applicable taxes, dues, penalties etc. will be deducted before making any payment*

9.40 Payment for Hosting: (Serial 11, Price Format 2, Page 110)

Payment shall only be done on quarterly basis, at the end of each quarter after successful Go-Live of ERP system including website.

9.41 Service Level Agreement (SLA)

Service Level Agreement (SLA) shall be monitored as mentioned in the following table. It is expected that the ERP system shall meet the minimum threshold of service defined against each level. Any degradation below this minimum threshold will attract penalties as per bands of service level met. The idea is that it triggers a proper review of any defect / failure / performance that had been agreed upon for the project, and to find resolutions in keeping with the highest standards of service excellence.

SLA will start immediately after Stabilization phase. Penalty, if any, accrued during the one-year Warranty period will be adjusted from the amount payable at the end of Warranty period.

9.41.1 Service Level Agreements Monitoring

9.41.1.1 The SLA management will be applicable for the components developed and supplied by the ERPSI and the disruption of service is attributable to the ERPSI.

9.41.1.2 The SMFC LTD will carry out monthly monitoring and performance review of ERPSI against the monthly formulated reports for SLA.

9.41.1.3 The System Integrator shall submit the monthly SLA report generated from SLA management tool, to the designated officer as per agreed frequency and timeline.

- 9.41.1.4 The performance review / audit reports will form a basis of any action relating to imposing penalty on or breach of contract of the System Integrator (SI).

9.41.2 Service Level Agreements and Targets

The service levels agreements shall be agreed upon by the System Integrator (SI) as a key performance indicator for this engagement. These key indicators shall be used while monitoring and measuring performance of System Integrator (SI). The service level indicators have been categorized under:

- Availability management
- Problem Resolution and Notification Times
- Performance Parameters
- Services related SLA

SLA management tool required to monitor the performance of the service should be provided by the System Integrator (SI). The SI will provide the tool along with required license and ATS for entire tenure of contract. The System Integrator (SI) would be required to provide access to the management tools to the SMFC LTD for monitoring purposes and would also provide the MIS reports for overall project and SLA monitoring as a part of the contract.

The description of the indicative Service Level Agreement (SLA) has been presented below. A complete Service Level Agreement will be made with the successful bidder at the time of signing the contract.

9.41.2.1 Availability Management

Availability of production applications - Shall be at minimum 99.5% on 24x7 basis. The project must also be able to rebound or recover from any planned or unplanned system downtime, ensuring a minimal impact on the operations.

- Reasons for non-availability will be ascertained and ERPSI will be accountable for the reason attributable to ERPSI
- Availability of non-production application – Shall be at minimum 95% on working days basis.
- Availability will be measured on monthly basis. Planned downtime will not be classified as unavailability. Planned downtime where the system is not available for providing service will be limited to maximum of 48 Hours in a quarter. The selected bidder should endeavor to take such downtimes only during weekends or holidays preferably after End of Day

(EoD). However, duration of the maximum allowable planned downtime time will be reviewed on yearly basis.

- The failure of application on account of non-availability of infrastructure provided by SMFC LTD shall not be considered while calculating SLA for that quarter.
- In case of any breach in the SLA, a penalty amounting to maximum of 30% of the total AMC cost shall be levied on the selected bidder.\

9.41.3 The following table outlines the availability service levels:

Problem Notification & Resolution Times

Following service levels will be applicable to the selected bidder for handholding and maintenance support. It shall be noted that the SLA period is including problem identification, resolution from SI or OEM and shall bear full responsibility with SI:

Type of Service	Metric	Measure	Threshold		Expected Action/Remarks
As per Problem Report (PR)	Delivery	Initial Response	Critical	2 Hour	Initial review for Category, Priority and whether the PR has sufficient information to understand the problem Assignment to respective individual for analysis
			High	4 Hour	
			Medium & Low	6 Hour	
As per Problem Report (PR)	Delivery	Complete Analysis/ Resolution	Critical	Issues reported in first half of day, resolution by end of day and issues reported in second half of the day by first half of next day	Detailed analysis of Problem Report and provide, root cause, potential risk / impact, effort estimate for resolution and closing of the problem
			High	End of Next day	
			Medium & Low	Mutually agreed upon time lines	

9.41.4 Threshold Definitions

- 9.41.4.1 Critical: Show-stopper application breakdown/crash. Has serious implications on running the production server and has impacted all business-critical process.
- 9.41.4.2 High: Serious degradation in the application performance. Has impacted majority of the business processes but able to continue the operations with the system limitations. It may have serious implications on the data integrity. It has affected or may affect, more than 5 users for the same problem.
- 9.41.4.3 Medium: Moderate degradation in the application performance. No implications on the data integrity. No impact on the normal operations/day-to-day working. It has affected or may affect, around less than 5 but 1 or more users for the same problem
- 9.41.4.4 Low: No impact on operation or security. Primarily improvement suggestions given during audits falling under the scope of work.
- 9.41.4.5 Penalties in case of failure to meet Service Levels

Following penalty shall be applicable to the selected bidder in case of failure to meet provisions of Service Level Agreement (SLA) as provided in table above:

- Critical: 2% of monthly AMC cost for every delay of 1 hour.
 - High: 1 % of monthly AMC for every delay of 1 half of the day
 - Medium: 0.5% of monthly AMC for every delay of 1 day.
 - Low: 0.5% of monthly cost for every delay of 1 week.
 - If the same incident occurs more than 2 times in a quarter for critical category and 3 times in a quarter for high & medium categories, an additional penalty of 2% of Monthly O&M prices for that quarter will be levied.
 - If the same incident happened more than 3 times in a quarter for critical category and 4 times in a quarter for high & medium categories, an additional penalty of 5% of Monthly O&M prices for that quarter will be levied.
- 9.41.4.6 If the occurrences of the incidents are more frequent than above or if the total penalty exceeds the maximum ceiling of 30% of the total AMC cost, SMFCL may, at its discretion, terminate the contract and forfeit the performance bank guarantee.
- 9.41.4.7 Consolidated SLA matrix

A. Severity Definitions

Severity	Description
Critical	Show-stopper crash; impacts all business-critical processes
High	Major performance degradation; affects >5 users; possible data integrity risk
Medium	Moderate performance issues; affects <5 users; no data integrity impact
Low	No operational impact; audit-based improvement suggestions

B. Availability Matrix

Component	Metric	Threshold	Measurement Frequency	Notes
Production Applications	Availability	≥ 99.5% (24x7 basis)	Monthly	Planned downtime excluded; max 48 hrs/quarter; preferably on weekends
Non-Production Applications	Availability	≥ 95% (Working days)	Monthly	Same planned downtime rules apply
Infrastructure Failures	Exclusion from SLA	N/A	N/A	Failures due to SMFC LTD infra not counted
SLA Breach Penalty	Penalty Cap	Max 30% of AMC Cost	Quarterly	Reviewed annually

C. Problem Notification & Resolution Times

Type of Service	Metric	Severity	Threshold	Expected Action/Remarks
Problem Report	Initial Response	Critical	2 Hours	Categorize, assign, notify initiator
		High	4 Hours	Same as above
		Medium & Low	6 Hours	Same as above
Problem Report	Complete Analysis/Resolution	Critical	Same day (if reported in first half); next day (if reported in second half)	Root cause, risk, impact, resolution effort estimate
		High	End of next day	Same as above
		Medium & Low	Mutually agreed timeline	Same as above

D. Penalty Structure

Severity	Delay Penalty	Repeated Incidents Penalty (per quarter)
Critical	2% of monthly AMC per hour of delay	>2 times: +2% O&M; >3 times: +5% O&M

Severity	Delay Penalty	Repeated Incidents Penalty (per quarter)
High	1% of monthly AMC per half-day delay	>3 times: +2% O&M; >4 times: +5% O&M
Medium	0.5% of monthly AMC per day of delay	>3 times: +2% O&M; >4 times: +5% O&M
Low	0.5% of monthly AMC per week of delay	Not specified
Overall	Penalty Cap	Max 30% of total AMC cost
Breach	Contract Termination	If penalties exceed cap or frequent breaches

9.41.5 SLA parameters & Penalty for Website

9.41.5.1 SLA parameters

Uptime requirement: 99.5% computed on monthly basis and paid on quarterly basis

9.41.5.2 Penalty

1% of quarterly amount for every 1% drop of SLA parameter or part there-off computed on monthly basis

9.41.6 SLA Change Control

- i) It is acknowledged that SLA may change as SMFC LTD's business needs evolve over the course of the contract period. As such, this document also defines the following management procedures:
- ii) A process for negotiating changes to the SLA.
- iii) An issue management process for documenting and resolving particularly difficult issues.
- iv) SMFC LTD and selected bidder management escalation process to be used if an issue is not being resolved in a timely manner.
- v) Any changes to the levels of service provided during the term of this agreement will be requested, documented, and negotiated in good faith by both parties. Either party can request for a change. Changes will be documented as an addendum to SLA and consequently the contract.
- vi) SLA Change Process
 - i. Both the parties may amend this SLA by mutual agreement in accordance.
 - ii. Changes can be proposed by SMFC LTD only
 - iii. Normally the forum for negotiating SLA changes will be SMFC LTD's monthly review meetings.

-
- iv. Version Control - All negotiated SLA changes will require changing the version control number. As appropriate, minor changes may be accumulated for periodic release (e.g., every quarter) or for release when a critical threshold of change has occurred.

9.41.7 Issue Management

1. This process provides an appropriate management structure for the orderly consideration and resolution of business and operational issues if quick consensus is not reached between SMFC LTD and selected bidder. It is expected that this pre-defined process will only be used on an exception basis if issues are not resolved at lower management levels.
2. All issues will be registered in the on-line ticketing tools, unless agreed upon mutually
3. Issue Management Process
 - (a) Either SMFC LTD or selected bidder may raise an issue by documenting the business or technical problem, which presents a reasonably objective summary of both points of view and identifies specific points of disagreement with possible solutions.
 - (b) SMFC LTD will determine which committee or executive level should logically be involved in resolution.
 - (c) A meeting or conference call may be conducted to resolve the issue in a timely manner. The documented issues will be distributed to the participants at least 24 hours prior to the discussion if the issue is not an emergency requiring immediate attention.
 - (d) Management of SMFC LTD and selected bidder will develop a temporary, if needed, and the permanent solution for the problem at hand. The selected bidder will then communicate the resolution to all interested parties.
 - (e) In the event a significant business issue is still unresolved, the arbitration procedures described in the Contract will be used.

9.41.8 Issue Escalation Process

1. The purpose of this escalation process is to provide a quick and orderly method of notifying both parties that an issue is not being successfully resolved at the lowest possible management level. Implementing these procedures ensures that SMFC LTD and selected bidder management are communicating at the appropriate levels. Escalation should take place on an exception basis and only if successful issue resolution cannot be achieved in a reasonable time frame.
2. All issues would be raised to the project management team, which is completely responsible for the day-to-day aspects of the implementation. The project management team shall classify the issues based on their severity level and resolve them within appropriate timelines.

3. If project management team is unable to resolve an issue, the issue would be escalated to the top management of the party concerned with options/ risks detailed for decision. Top management will make decisions based on the options/ risks presented by the IT team. Escalation list will be prepared at the time of commencement of contract period and will be updated from time to time.
4. In case one or both the parties are unsatisfied with the decision of the top management of SMFC LTD, the dispute will be resolved as specified as per SMFC LTD jurisdiction.

9.41.9 Termination of Contract on breach of SLA

1. Risk and Cost Factor

- a) In the event of termination of contract based on non-performance by the selected bidder during implementation till Warranty period or as per SLA during AMC period, selected bidder will be solely responsible for risk and cost factor thereon.

2. Non-performance during implementation

The selected bidder may approach SMFCL in case of any delay in stipulated implementation timeline for reasons attributed to SMFCL or Force Majeure. SMFCL, based on justification and on case-to-case basis, may grant extension of the timeline to the selected bidder through formal communication.

In case the selected bidder does not adhere to the timeline mentioned in this RFP for three (3) continuous time-periods as specified in the relevant clause, SMFC LTD will treat it as a case of breach of Service Level Agreement. The following steps will be taken in such a case:

- SMFC LTD issues a warning letter to the selected bidder.
- Selected bidder should reply within three working days.
- If breaches occur again, SMFC LTD issues a show cause notice to the selected bidder.
- Selected bidder should reply within three working days.
- If SMFC LTD is not satisfied with the reply, the performance bank guarantee may be forfeited, and contract may be terminated by SMFC LTD as per the contract.

3. Breach of SLA

In case the selected bidder does not meet the service levels mentioned in this RFP for three (3) continuous time-periods as specified in the relevant clause, SMFC LTD will treat it as a case of breach of Service Level Agreement. The following steps will be taken in such a case:

- SMFC LTD issues a warning letter to the selected bidder.

- Selected bidder should reply within three working days.
- If breaches occur again, SMFC LTD issues a show cause notice to the selected bidder.
- Selected bidder should reply within three working days.
- If SMFC LTD is not satisfied with the reply, the performance bank guarantee may be forfeited, and contract may be terminated by SMFC LTD as per the contract.

9.41.10 Exclusions

The selected bidder will be exempted from any delays or slippages on SLA parameters arising out of following reasons: -

- Delay in execution due to delay (in approval, review etc.) from SMFC LTD's side. Any such delays will be notified in written.
- Force Majeure
